

# PUREX TUNNEL 2

## INTERIM STABILIZATION PROGRESS

October 14, 2018

### HEADLINES

This Week	Total To Date
No safety events this week	No safety events
1,910 cubic yards of grout	3,529 cubic yards of grout
191 trucks	365 trucks

Forecasted Completion – March 2019

**Tunnel 2 Bulk Fill  $\approx$  9% Complete**

### GROUT DELIVERY NUMBERS


- Total Volume  $\approx$  39,800 yd<sup>3</sup>
- -10 yd<sup>3</sup> per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 4 Days per Week

### Grouting Risk Tracking

- Weather Delays – none to date
- Grout Delivery Issues – none to date
- Grout Equipment Issues – 2 hours due to grout pumps
- Monitoring Equipment Issues – none to date
- Resource Limitations – none to date
- Grout Flowability Issues – none to date
- Days Lost – 2 (Lessons learned incorporation)

### Tunnel Profile View

(Illustrative only)

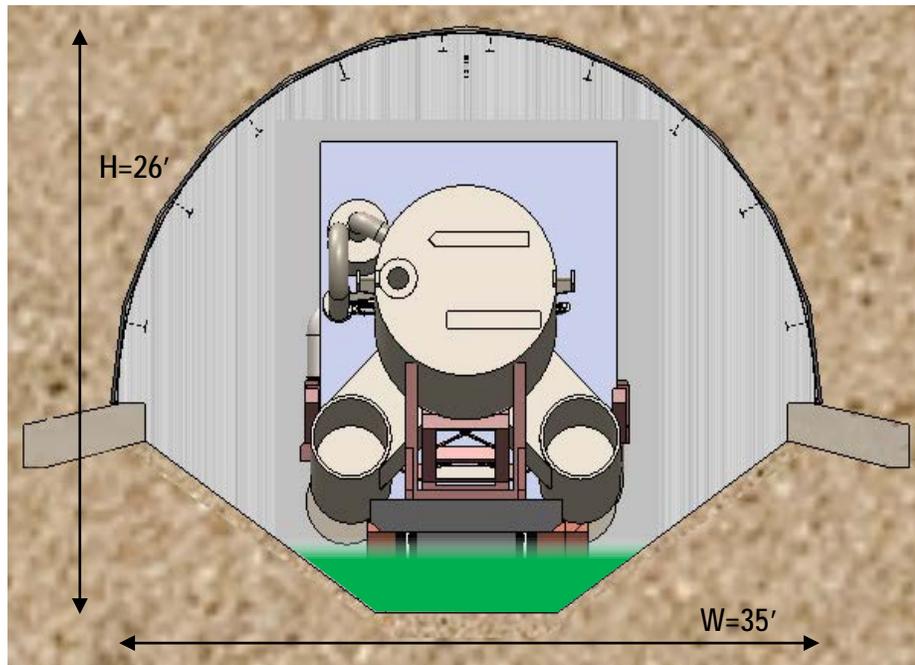

### Purex Tunnel 2 Baseline Status

