

PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

October 21, 2018

HEADLINES

This Week

No safety events this week
3,440 cubic yards of grout
344 trucks

Total To Date

No safety events
6,969 cubic yards of grout
709 trucks

Forecasted Completion – **March 2019**

Tunnel 2 Bulk Fill ≈ 18% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 39,800 yd³
- ~10 yd³ per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 4 Days per Week

Grouting Risk Tracking

Weather Delays – **none to date**
 Grout Delivery Issues – **none to date**
 Grout Equipment Issues – **2 hours due to grout pumps**
 Monitoring Equipment Issues – **none to date**
 Resource Limitations – **none to date**
 Grout Flowability Issues – **none to date**
 Days Lost – **2 (Lessons learned incorporation)**

Tunnel Profile View

(Illustrative only)

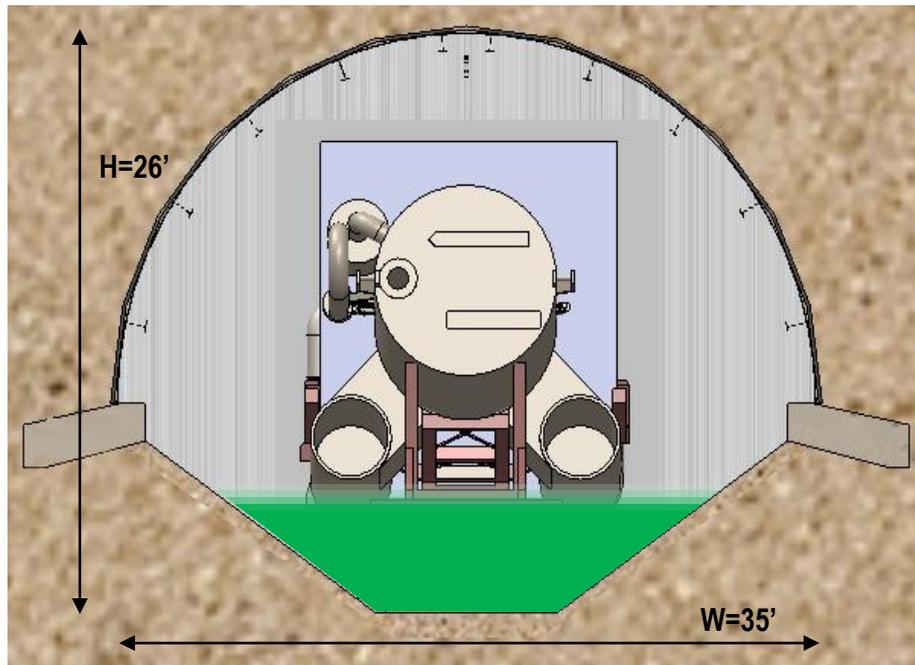

Purex Tunnel 2 Baseline Status

