

PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

October 28, 2018

HEADLINES

<u>This Week</u>	<u>Total To Date</u>
No safety events this week	No safety events
2,010 cubic yards of grout	8,979 cubic yards of grout
201 trucks	910 trucks

Forecasted Completion – March 2019

Tunnel 2 Bulk Fill ≈ 23% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 39,800 yd³
- ~10 yd³ per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week

Grouting Risk Tracking

Weather Delays – **none to date**
 Grout Delivery Issues – **none to date**
 Grout Equipment Issues – **2 hours total to date**
 Monitoring Equipment Issues – **none to date**
 Resource Limitations – **none to date**
 Grout Flowability Issues – **none to date**
 Days Lost – Current Week: **2 (tunnel as found conditions)**
 Total to Date: **4**

Tunnel Profile View

(Illustrative only)

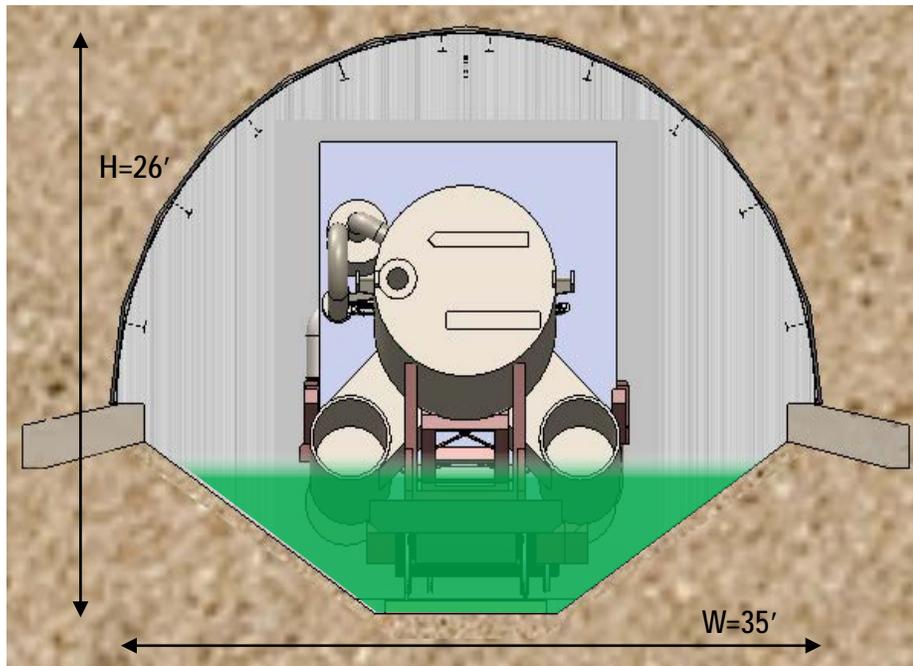

Purex Tunnel 2 Baseline Status

