

PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

November 4, 2018

HEADLINES

<u>This Week</u>	<u>Total To Date</u>
No safety events this week	No safety events
1,682 cubic yards of grout	10,661 cubic yards of grout
169 trucks	1,079 trucks

Forecasted Completion – March 2019

Tunnel 2 Bulk Fill \approx 27% Complete

GROUT DELIVERY NUMBERS

- Total Volume \approx 39,800 yd³
- \sim 10 yd³ per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week


Grouting Risk Tracking

Weather Delays – none to date
 Grout Delivery Issues – none to date
 Grout Equipment Issues – 2 hours total to date
 Monitoring Equipment Issues – none to date
 Resource Limitations – none to date
 Grout Flowability Issues – none to date
 Days Lost – Current Week: 2 (recovery activities related to as found conditions)

Total to Date: 6

Tunnel Profile View

(Illustrative only)

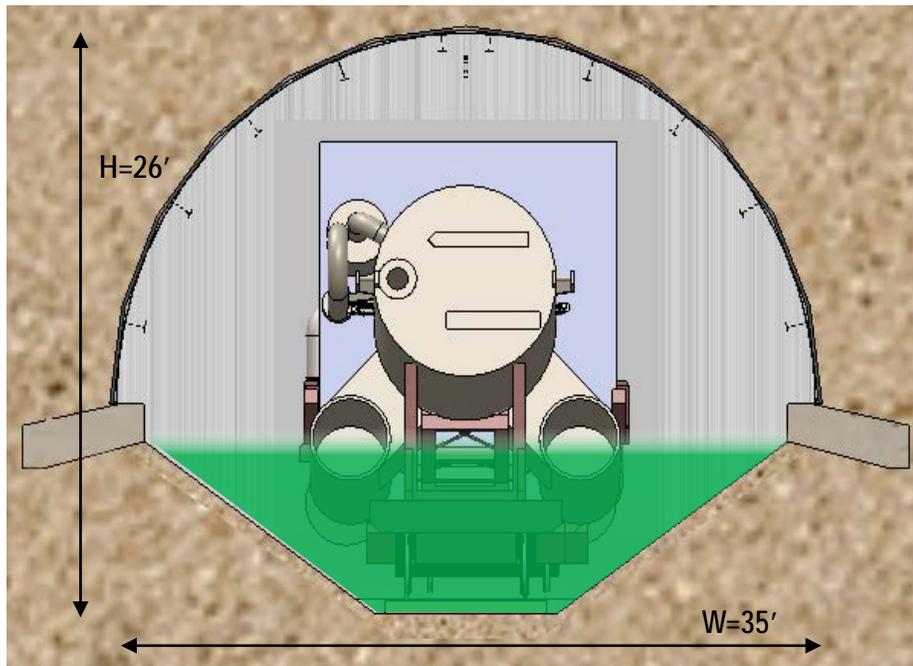

Purex Tunnel 2 Baseline Status

