

# PUREX TUNNEL 2

## INTERIM STABILIZATION PROGRESS

November 11, 2018

### HEADLINES

<u>This Week</u>	<u>Total To Date</u>
No safety events this week	No safety events
<b>1,310</b> cubic yards of grout	<b>11,971</b> cubic yards of grout
<b>131</b> trucks	<b>1,210</b> trucks

Forecasted Completion – March 2019

### Tunnel 2 Bulk Fill ≈ 30% Complete

#### GROUT DELIVERY NUMBERS

- Total Volume ≈ 39,800 yd<sup>3</sup>
- ~10 yd<sup>3</sup> per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week


### Grouting Risk Tracking

Weather Delays – *none to date*  
 Grout Delivery Issues – *none to date*  
 Grout Equipment Issues – **3 days 2 hours to date**  
 Monitoring Equipment Issues – *none to date*  
 Resource Limitations – *none to date*  
 Grout Flowability Issues – *none to date*  
 Days Lost – Current Week: **3 (camera cleaning and hose/valve replacement)**

Total to Date: **9**

### Tunnel Profile View

(Illustrative only)

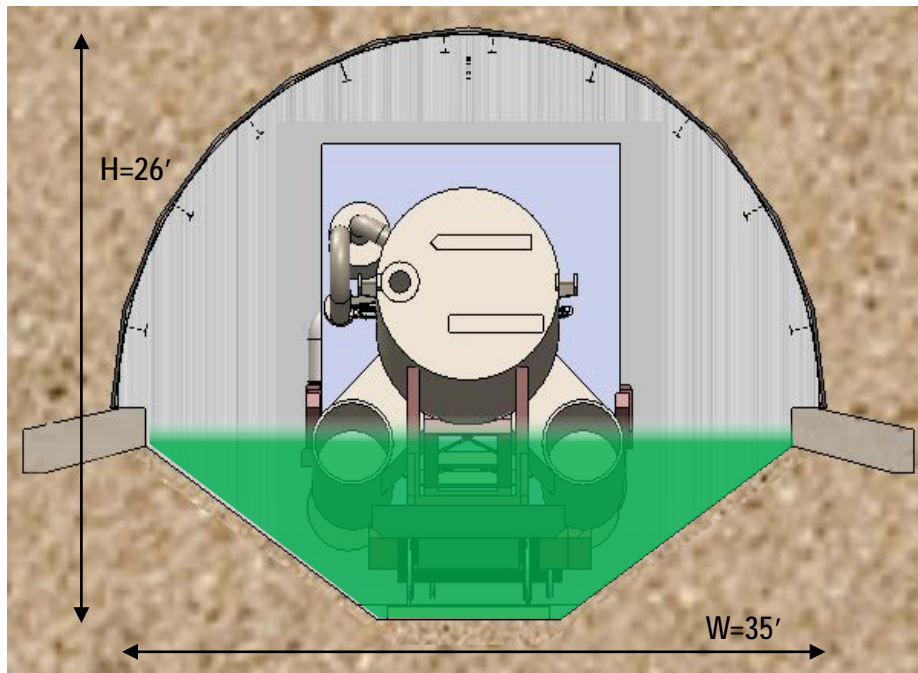

### Purex Tunnel 2 Baseline Status

