



PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

November 25, 2018

HEADLINES

This Week	Total To Date
No safety events this week	No safety events
1,310 cubic yards of grout	16,991 cubic yards of grout
131 trucks	1,712 trucks

Forecasted Completion – March 2019

Tunnel 2 Bulk Fill ≈ 43% Complete

GROUT DELIVERY NUMBERS

- Total Volume ≈ 39,800 yd³
- ~10 yd³ per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week


Grouting Risk Tracking

Weather Delays – none to date
 Grout Delivery Issues – none to date
 Grout Equipment Issues – 3 days 2 hours to date
 Monitoring Equipment Issues – none to date
 Resource Limitations – none to date
 Grout Flowability Issues – none to date
 Days Lost – Current Week: 0

Total to Date: 9

Tunnel Profile View

(Illustrative only)

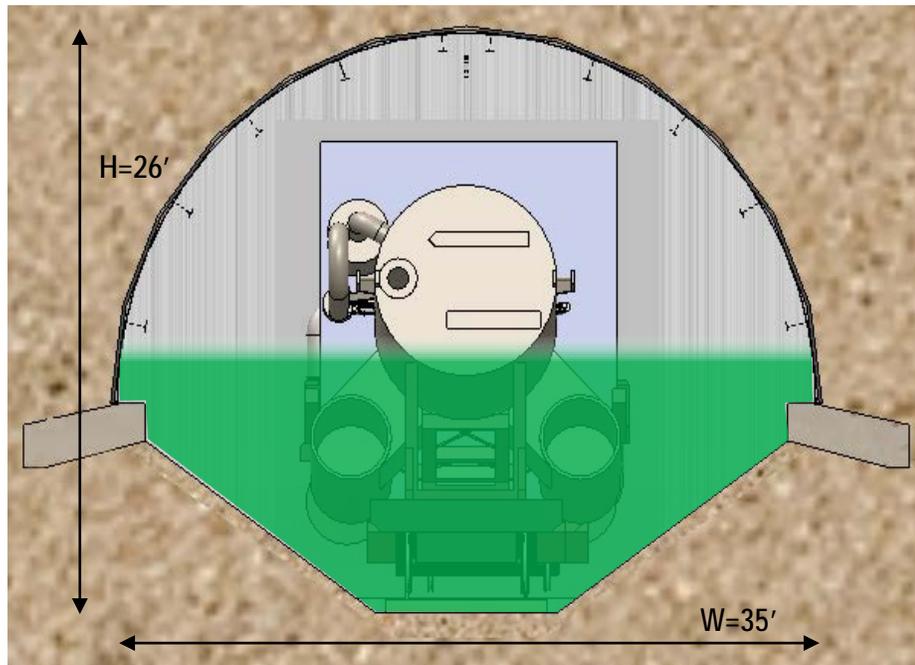

Purex Tunnel 2 Baseline Status

