

PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

December 9, 2018

HEADLINES

This Week	Total To Date
No safety events this week	No safety events
0 cubic yards of grout	19,781 cubic yards of grout
0 trucks	1,991 trucks

Forecasted Completion – March 2019

Tunnel 2 Bulk Fill ≈ 49% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 39,800 yd³
- ~10 yd³ per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week

Grouting Risk Tracking

Weather Delays – none to date
 Grout Delivery Issues – none to date
 Grout Equipment Issues – 4 days
 Monitoring Equipment Issues – none to date
 Resource Limitations – none to date
 Grout Flowability Issues – none to date
 Conveyance System Maintenance – 6 days
 Tunnel As Found Condition Repairs – 4 days
 Days Lost – Current Week: 4
 Total to Date: 14

Tunnel Profile View

(Illustrative only)

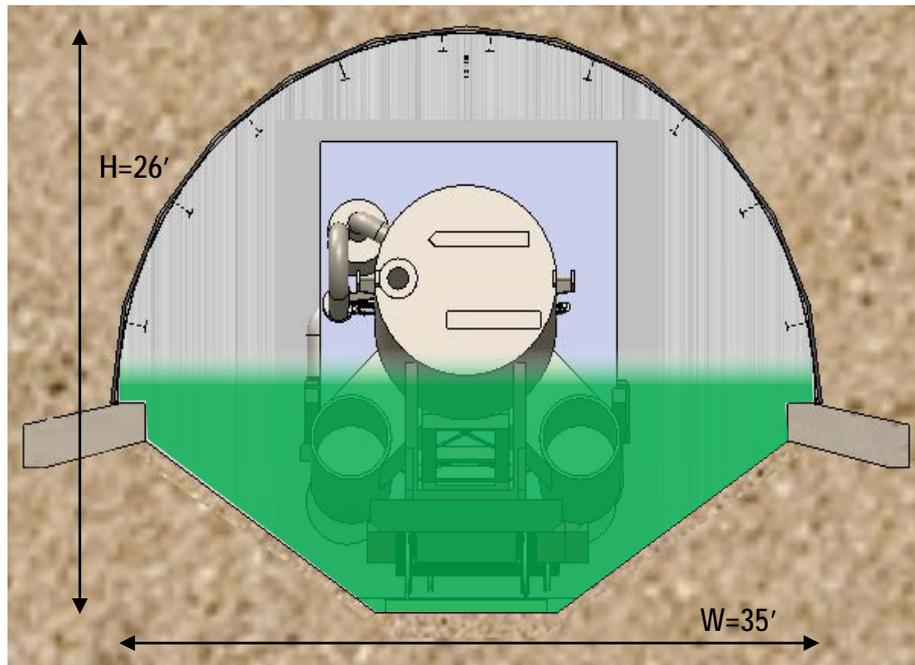

Purex Tunnel 2 Baseline Status

