



PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

January 20, 2019

HEADLINES

This Week	Total To Date
No safety events this week	No safety events
490 cubic yards of grout	26,091 cubic yards of grout
49 trucks	2,622 trucks

Forecasted Completion – March 2019

Tunnel 2 Bulk Fill ≈ 65% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 39,800 yd³
- ~10 yd³ per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week

Grouting Risk Tracking

- Weather Delays – none to date
- Grout Delivery Issues – none to date
- Grout Equipment Issues – 4 days
- Monitoring Equipment Issues – none to date
- Resource Limitations – none to date
- Grout Flowability Issues – none to date
- Conveyance System Maintenance – 15 days
- Tunnel As Found Condition Repairs – 4 days
- Days Lost – Current Week: 3
- Total to Date: 23

Tunnel Profile View

(Illustrative only)

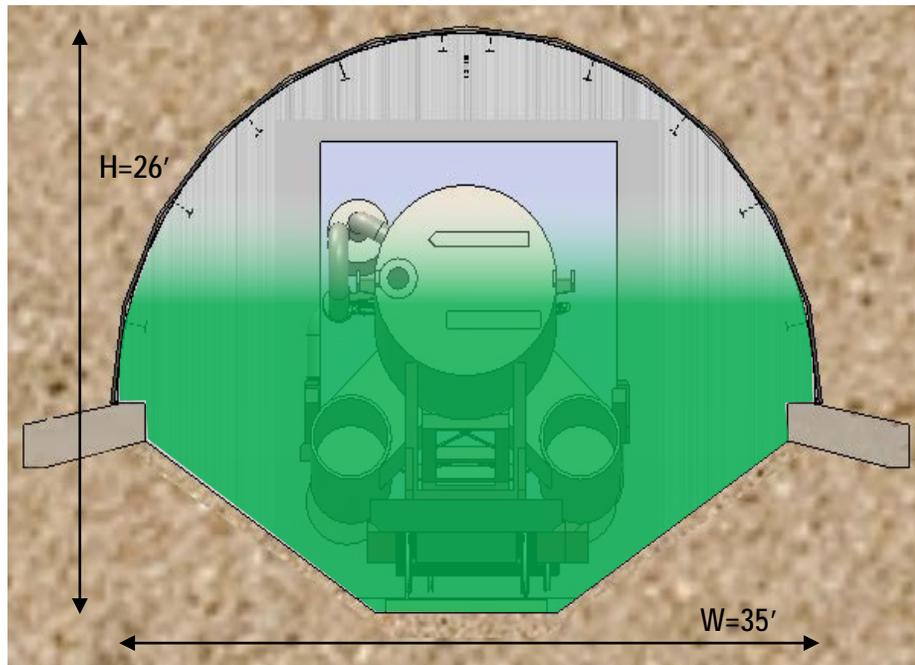

Purex Tunnel 2 Baseline Status

