



PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

January 27, 2019

HEADLINES

| This Week | Total To Date |
|----------------------------|-----------------------------|
| No safety events this week | No safety events |
| 2,075 cubic yards of grout | 28,166 cubic yards of grout |
| 208 trucks | 2,830 trucks |

Forecasted Completion – March 2019

Tunnel 2 Bulk Fill ≈ 70% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 39,800 yd³
- ~10 yd³ per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week

Grouting Risk Tracking

- Weather Delays – none to date
- Grout Delivery Issues – none to date
- Grout Equipment Issues – 4 days
- Monitoring Equipment Issues – none to date
- Resource Limitations – none to date
- Grout Flowability Issues – none to date
- Conveyance System Maintenance – 15 days
- Tunnel As Found Condition Repairs – 4 days
- Days Lost – Current Week: 0
- Total to Date: 23

Tunnel Profile View

(Illustrative only)

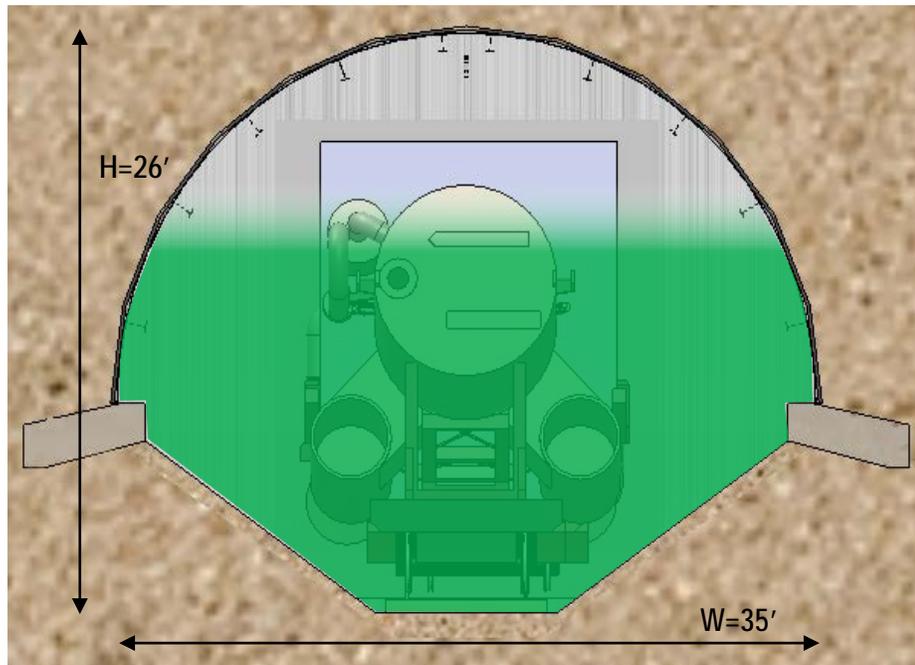

Purex Tunnel 2 Baseline Status

