

# PUREX TUNNEL 2

## INTERIM STABILIZATION PROGRESS

February 3, 2019

**Tunnel 2 Bulk Fill  $\approx$  78% Complete**

### HEADLINES

This Week	Total To Date
No safety events this week	No safety events
<b>3,000</b> cubic yards of grout	<b>31,166</b> cubic yards of grout
<b>300</b> trucks	<b>3,130</b> trucks

Forecasted Completion – **March 2019**

### GROUT DELIVERY NUMBERS


- Total Volume  $\approx$  39,800 yd<sup>3</sup>
- $\sim$ 10 yd<sup>3</sup> per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week

### Grouting Risk Tracking

Weather Delays – **none to date**  
 Grout Delivery Issues – **none to date**  
 Grout Equipment Issues – **4 days**  
 Monitoring Equipment Issues – **none to date**  
 Resource Limitations – **none to date**  
 Grout Flowability Issues – **none to date**  
 Conveyance System Maintenance – **15 days**  
 Tunnel As Found Condition Repairs – **4 days**  
 Days Lost – Current Week: **0**  
 Total to Date: **23**

### Tunnel Profile View

(Illustrative only)

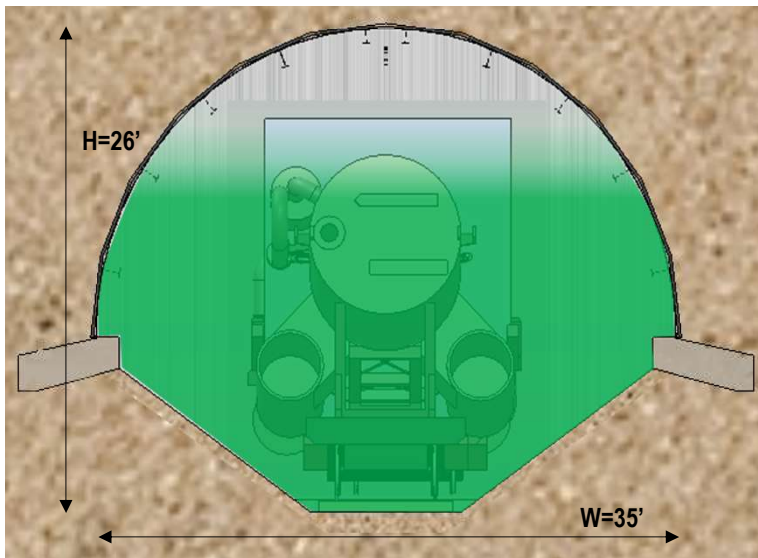

### Purex Tunnel 2 Baseline Status

