

# PUREX TUNNEL 2

## INTERIM STABILIZATION PROGRESS

February 10, 2019

### HEADLINES

<u>This Week</u>	<u>Total To Date</u>
No safety events this week	No safety events
0 cubic yards of grout	31,166 cubic yards of grout
0 trucks	3,130 trucks

Forecasted Completion – March 2019

**Tunnel 2 Bulk Fill ≈ 78% Complete**

### GROUT DELIVERY NUMBERS


- Total Volume ≈ 39,800 yd<sup>3</sup>
- ~10 yd<sup>3</sup> per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week

### Grouting Risk Tracking

Weather Delays – 4 days  
 Grout Delivery Issues – none to date  
 Grout Equipment Issues – 4 days  
 Monitoring Equipment Issues – none to date  
 Resource Limitations – none to date  
 Grout Flowability Issues – none to date  
 Conveyance System Maintenance – 15 days  
 Tunnel As Found Condition Repairs – 4 days  
 Days Lost – Current Week: 4  
 Total to Date: 27

### Tunnel Profile View

(Illustrative only)

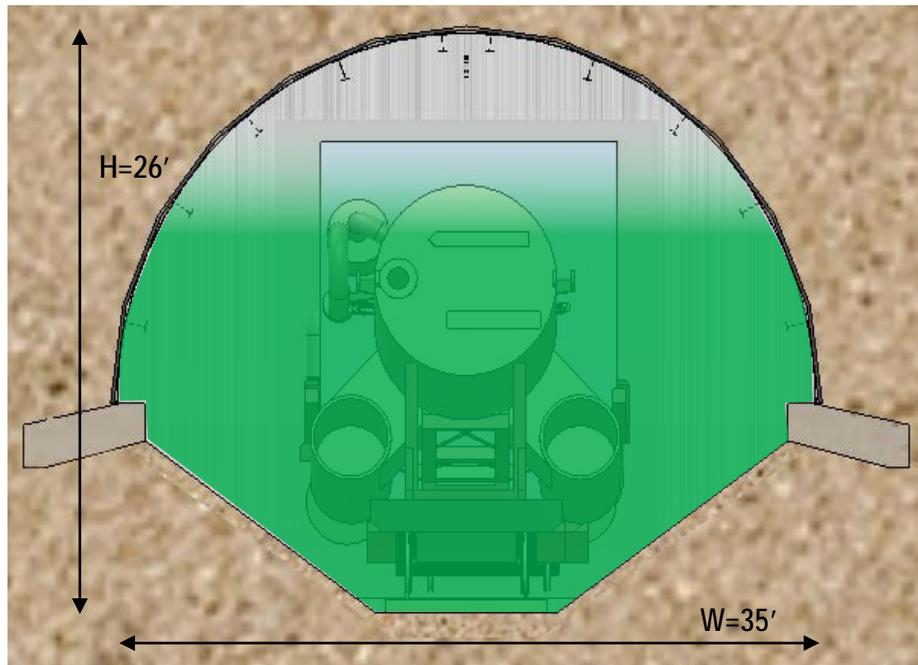

### Purex Tunnel 2 Baseline Status

