

# PUREX TUNNEL 2

## INTERIM STABILIZATION PROGRESS

February 17, 2019

### HEADLINES

This Week	Total To Date
No safety events this week	No safety events
0 cubic yards of grout	31,166 cubic yards of grout
0 trucks	3,130 trucks

Forecasted Completion – March 2019

**Tunnel 2 Bulk Fill ≈ 78% Complete**

### GROUT DELIVERY NUMBERS


- Total Volume ≈ 39,800 yd<sup>3</sup>
- ~10 yd<sup>3</sup> per Truck
- 6 Trucks per Hour (max)
- Pour 8 Hrs each 10 Hr Day
- 5 Days per Week

### Grouting Risk Tracking

- Weather Delays – 8 days
- Grout Delivery Issues – none to date
- Grout Equipment Issues – 4 days
- Monitoring Equipment Issues – none to date
- Resource Limitations – none to date
- Grout Flowability Issues – none to date
- Conveyance System Maintenance – 15 days
- Tunnel As Found Condition Repairs – 4 days
- Days Lost – Current Week: 4
- Total to Date: 31

### Tunnel Profile View

(Illustrative only)

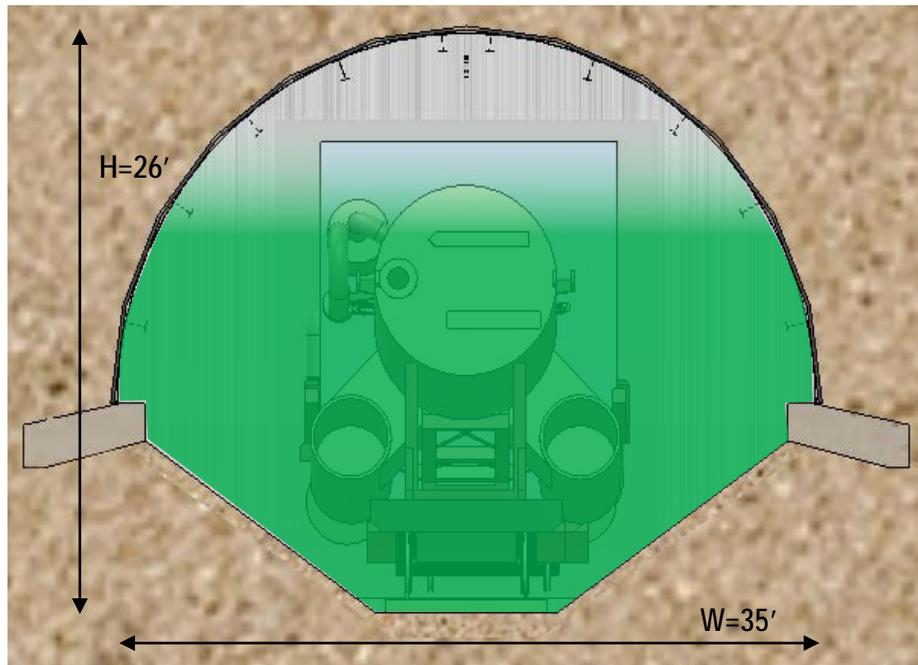

### Purex Tunnel 2 Baseline Status

