



PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

March 3rd, 2019

HEADLINES

This Week	Total To Date
No safety events this week	No safety events
0 cubic yards of grout	31,166 cubic yards of grout
0 trucks	3,130 trucks

Forecasted Completion – March 2019

Project is analyzing completion date impact due to weather delays

Tunnel 2 Bulk Fill ≈ 78% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 39,800 yd³
- 500 yd³ per day
- -10 yd³ per Truck

Grouting Risk Tracking

Weather Delays – 15 days
 Grout Delivery Issues – none to date
 Grout Equipment Issues – 4 days
 Monitoring Equipment Issues – none to date
 Resource Limitations – none to date
 Grout Flowability Issues – none to date
 Conveyance System Maintenance – 13 days
 Tunnel As Found Condition Repairs – 4 days
 Days Lost – Current Week: 4
 Total to Date: 36

Tunnel Profile View

(Illustrative only)

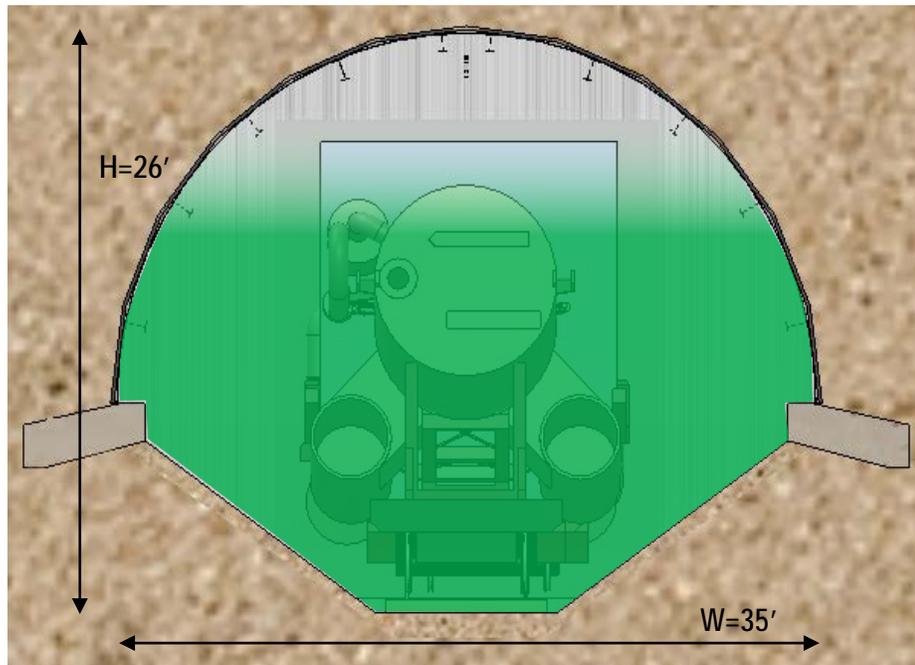

Purex Tunnel 2 Baseline Status

