

PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

March 17th, 2019

HEADLINES

This Week	Total To Date
No safety events this week	No safety events
1,710 cubic yards of grout	32,876 cubic yards of grout
171 trucks	3,301 trucks

Forecasted Completion – April 18th, 2019

Tunnel 2 Bulk Fill ≈ 88% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 37,270 yd³
- 500 yd³ per day
- -10 yd³ per Truck

Grouting Risk Tracking

- Weather Delays – 21 days
- Grout Delivery Issues – none to date
- Grout Equipment Issues – 4 days
- Monitoring Equipment Issues – none to date
- Resource Limitations – none to date
- Grout Flowability Issues – none to date
- Conveyance System Maintenance – 13 days
- Tunnel As Found Condition Repairs – 4 days
- Days Lost – Current Week: 2
- Total to Date: 42

Tunnel Profile View

(Illustrative only)

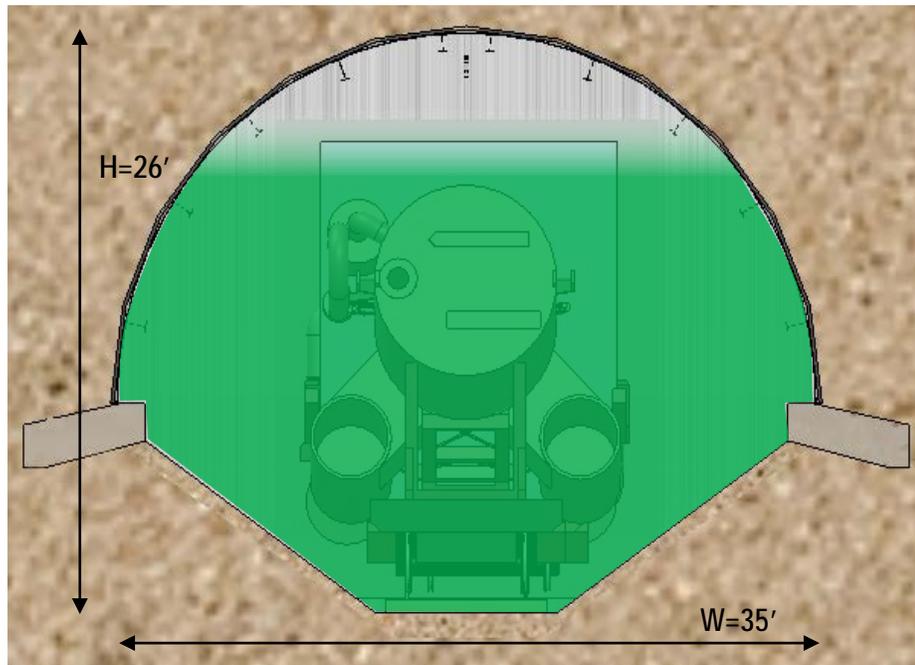

Purex Tunnel 2 Completion Forecast

