



PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

April 7th, 2019

HEADLINES

This Week	Total To Date
No safety events this week	No safety events
440 cubic yards of grout	36,766 cubic yards of grout
44 trucks	3,690 trucks

Forecasted Completion – April 18th, 2019

Tunnel 2 Bulk Fill ≈ 98% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 37,270 yd³
- 500 yd³ per day
- -10 yd³ per Truck

Grouting Risk Tracking

Weather Delays – 22 days
 Grout Delivery Issues – none to date
 Grout Equipment Issues – 4 days
 Monitoring Equipment Issues – none to date
 Resource Limitations – none to date
 Grout Flowability Issues – none to date
 Conveyance System Maintenance – 15 days
 Tunnel As Found Condition Repairs – 4 days
 Days Lost – Current Week: 2
 Total to Date: 45

Tunnel Profile View

(Illustrative only)

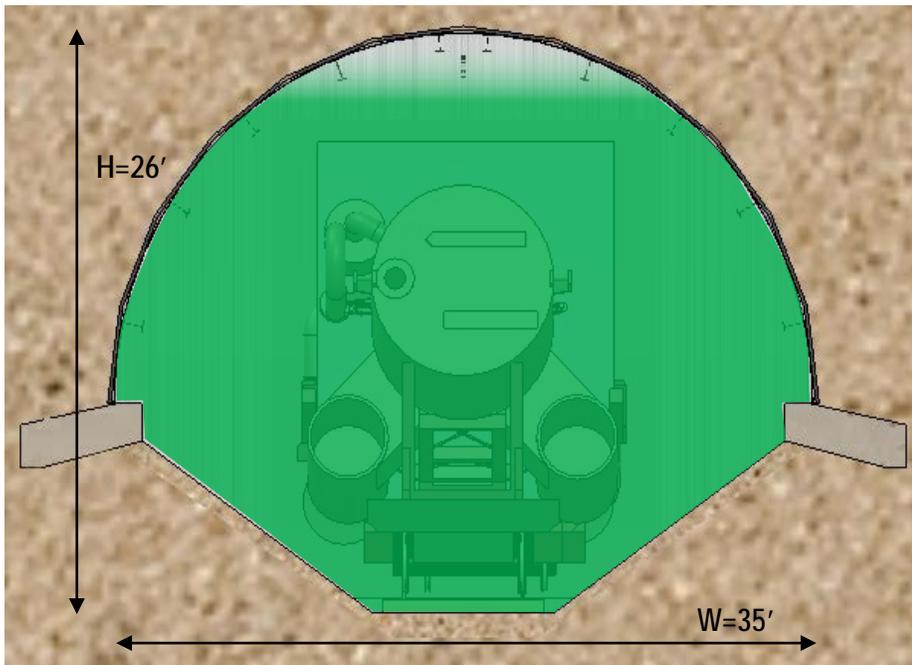

Purex Tunnel 2 Completion Forecast

