



PUREX TUNNEL 2

INTERIM STABILIZATION PROGRESS

April 14th, 2019

HEADLINES

This Week	Total To Date
No safety events this week	No safety events
1800 cubic yards of grout	38,566 cubic yards of grout
180 trucks	3,870 trucks

Forecasted Completion – April 18th, 2019

Tunnel 2 Bulk Fill ≈ 100% Complete

GROUT DELIVERY NUMBERS


- Total Volume ≈ 37,270 yd³
 - 100% of estimated grout quantity
 - Estimated 1,240 cu-yds remaining between riser 2 and the water door
- 500 yd³ per day
- ~10 yd³ per Truck

Grouting Risk Tracking

- Weather Delays – 23 days
- Grout Delivery Issues – none to date
- Grout Equipment Issues – 4 days
- Monitoring Equipment Issues – none to date
- Resource Limitations – none to date
- Grout Flowability Issues – none to date
- Conveyance System Maintenance – 16 days
- Tunnel As Found Condition Repairs – 4 days
- Days Lost – Current Week: 2
- Total to Date: 47

Tunnel Profile View

(Illustrative only)

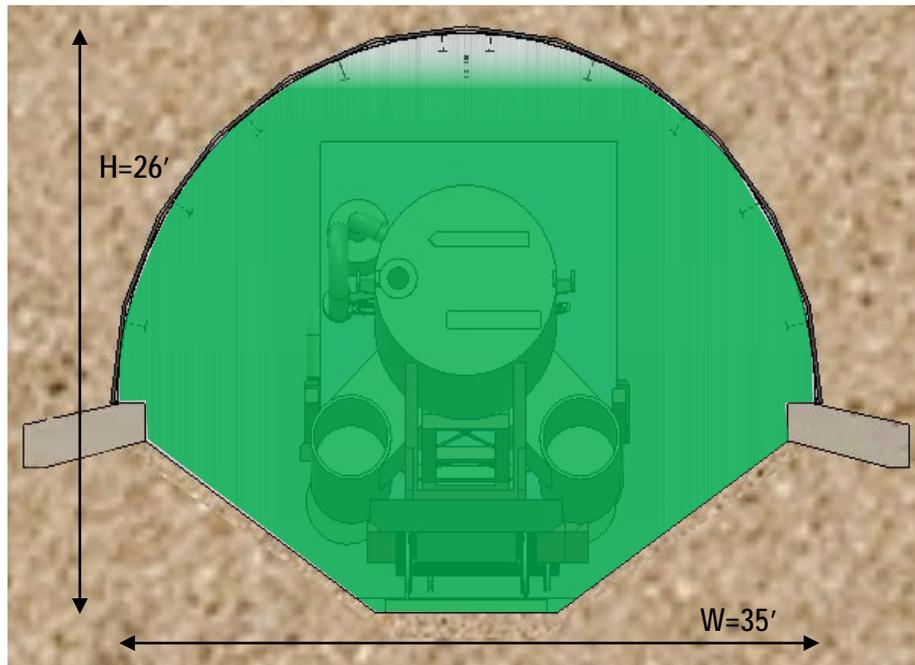

Purex Tunnel 2 Completion Forecast

