

# PUREX TUNNEL 2

## INTERIM STABILIZATION PROGRESS

April 21<sup>st</sup>, 2019

### HEADLINES

This Week	Total To Date
No safety events this week	No safety events
970 cubic yards of grout	39,536 cubic yards of grout
97 trucks	3,967 trucks
Forecasted Completion – April 25 <sup>th</sup> , 2019	

### GROUT DELIVERY NUMBERS


- Original Estimated Volume ≈ 37,270 yd<sup>3</sup>
  - Placed 100% of original estimated volume on April 15<sup>th</sup>, 2019
  - Estimated 900 yd<sup>3</sup> remain to be placed between riser 2 and the water door
- Only riser 1 remains to max fill
- ~10 yd<sup>3</sup> per Truck

### Grouting Risk Tracking

- Weather Delays – 23 days
- Grout Delivery Issues – none to date
- Grout Equipment Issues – 4 days
- Monitoring Equipment Issues – none to date
- Resource Limitations – none to date
- Grout Flowability Issues – none to date
- Conveyance System Maintenance – 17 days
- Tunnel As Found Condition Repairs – 4 days
- Days Lost – Current Week: 1
- Total to Date: 48

### Tunnel Profile View

(Illustrative only)

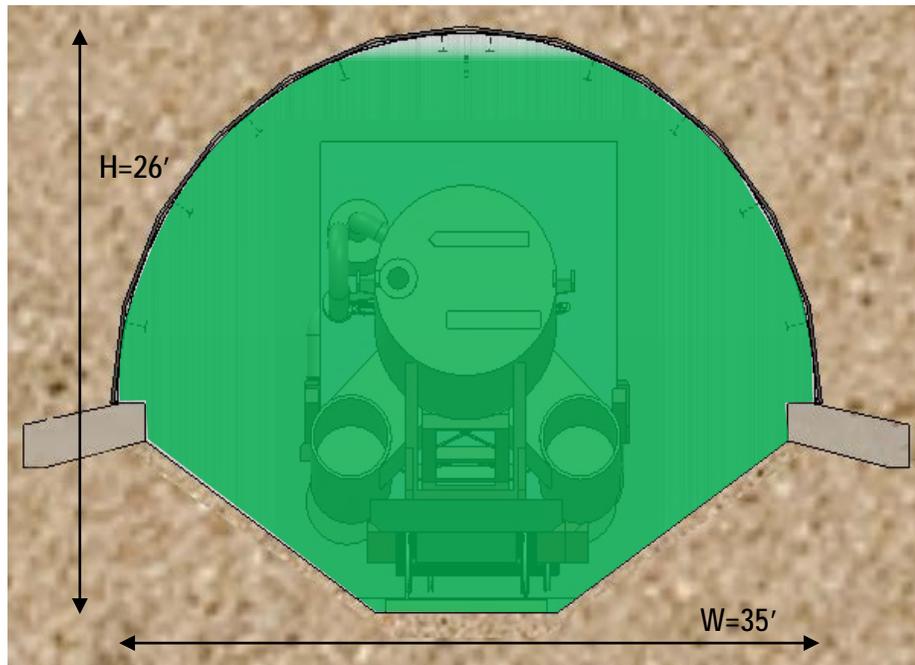

### Purex Tunnel 2 Completion Forecast

