



# PUREX TUNNEL 2

## INTERIM STABILIZATION PROGRESS

April 28<sup>th</sup>, 2019

### HEADLINES

This Week	Total To Date
No safety events this week	No safety events
1960 cubic yards of grout	41,496 cubic yards of grout
196 trucks	4,163 trucks

Grouting Complete on April 26<sup>th</sup>, 2019

### GROUT DELIVERY NUMBERS


- Original Estimated Volume ≈ 37,270 yd<sup>3</sup>
  - Placed 100% of original estimated volume on April 15<sup>th</sup>, 2019
- Final grout placed volume = 41,496 yd<sup>3</sup>
  - Placed final grout on April 26<sup>th</sup>, 2019

### Final Grouting Risk Tracking

- Weather Delays – 23 days
- Grout Delivery Issues – none to date
- Grout Equipment Issues – 4 days
- Monitoring Equipment Issues – none to date
- Resource Limitations – none to date
- Grout Flowability Issues – none to date
- Conveyance System Maintenance – 17 days
- Tunnel As Found Condition Repairs – 4 days
- Days Lost – Current Week: 0
- Total to Date: 48

### Tunnel Profile View

(Illustrative only)

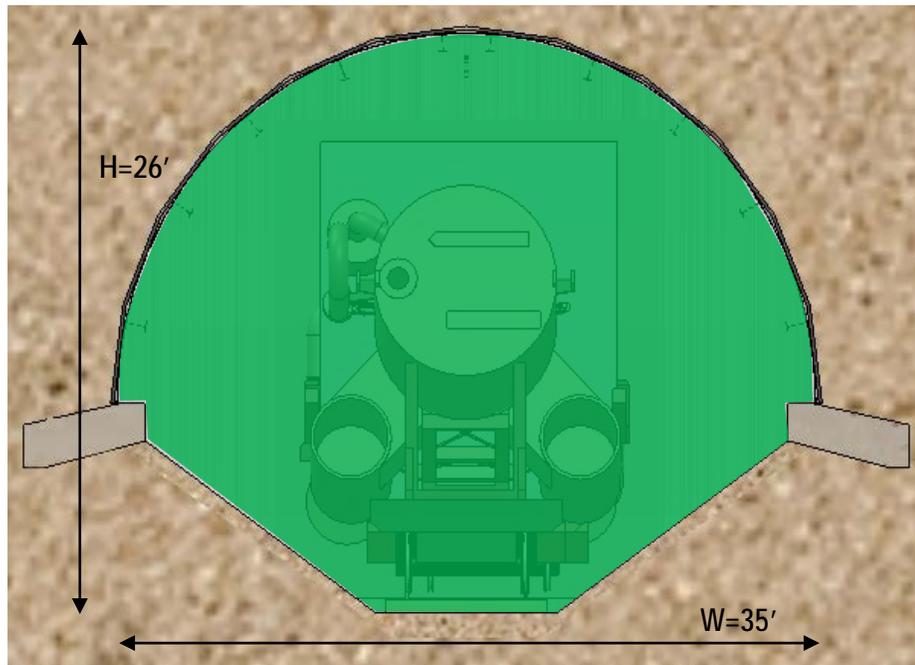

### Purex Tunnel 2 Completion Forecast

