


Section G

Fast Flux Test Facility Closure (RL-0042)

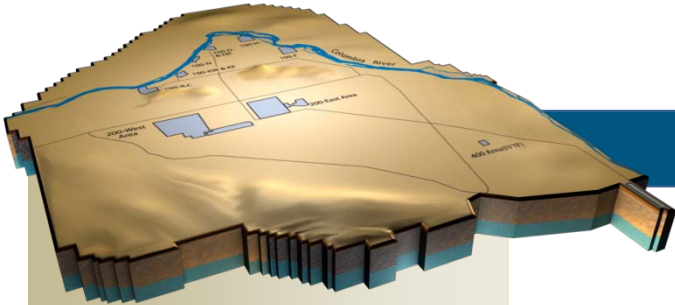

Monthly Performance Report

K. L. Kehler
Vice President and
Project Manager for
D&D Project



Fast Flux Test Facility

December 2010
DOE/RL-2010-126-12, Rev. 0
Contract DE-AC06-08RL14788
Deliverable C.3.1.3.1 - 1

PROJECT SUMMARY

The Fast Flux Test Facility (FFTF) is being maintained in a low-cost surveillance and maintenance condition. The 400 Area water system continues to operate providing service to other occupants of the 400 Area and water for fire protection. Deficiencies identified during the annual surveillance performed in March are being worked to resolution as resources permit.

All scope within the FFTF Closure (RL-0042) project is base funded. There is no funding from the American Recovery and Reinvestment Act.

EMS OBJECTIVES AND TARGET STATUS

EMS Objectives and Target Status for RL-0042 are included as part of the Objectives and Target Status for RL-0040.

TARGET ZERO PERFORMANCE

	Current Month	Rolling 12 Month	Comment
Days Away, Restricted or Transferred	0	0	N/A
Total Recordable Injuries	0	0	N/A
First Aid Cases	0	0	N/A
Near-Misses	0	0	N/A

KEY ACCOMPLISHMENTS

None identified.

MAJOR ISSUES

None identified.

KEY RISKS AND CHALLENGES

None identified.

PROJECT BASELINE PERFORMANCE

Current Month

(\$M)

RL-0042 FFTF Closure	Budgeted Cost of Work Scheduled	Budgeted Cost of Work Performed	Actual Cost of Work Performed	Schedule Variance (\$)	Schedule Variance (%)	Cost Variance (\$)	Cost Variance (%)
Base	0.1	0.1	0.1	0.0	0.0	0.1	64.9%

CM Schedule Performance: (\$0.0M/0.0%)

The current month schedule variance is within reporting thresholds.

CM Cost Performance: (+\$0.1M/+64.9%)

The current month cost variance is within reporting thresholds.

Contract-to-Date

(\$M)

RL-0042 FFTF Closure	Budgeted Cost of Work Scheduled	Budgeted Cost of Work Performed	Actual Cost of Work Performed	Schedule Variance (\$)	Schedule Variance (%)	Cost Variance (\$)	Cost Variance (%)	Budget at Completion (BAC)	Estimate at Completion (EAC)	Variance at Completion (VAC)
Base	10.5	10.5	9.5	0.0	0.0	1.0	9.1%	25.2	23.9	1.3

Numbers are rounded to the nearest \$0.1M.

CTD Schedule Performance (\$0.0M/0.0%)

The schedule variance is within reporting thresholds.

CTD Cost Performance (+\$1.0M /+9.1%)

The cost variance is within reporting thresholds.

Contract Performance Report Formats are provided in Appendix A.

FUNDS vs. SPEND FORECAST (\$M)

FY2011			
RL-0042 FFTF Closure	Projected Funding	Spending Forecast	Variance
Base	2.4	1.2	1.2

Funds Analysis:

Funding includes FY2010 carryover and FY2011 new Budget Authority. The BASE positive variance of \$1.2M reflects a projected PMB under run of \$.5M plus \$.7M of reserve funds.

A CHPRC site integrated work scope prioritization plan is being developed to align work scope with proposed revised funding levels.

Critical Path Schedule

Critical path analysis is not applicable to this project. Remaining contract scope is performance of interim surveillance and maintenance activities.

Estimate at Completion (EAC)

The BAC and EAC now include FY2009 through FY2018, the PRC contract period.

Baseline Change Requests

BCRA-PRC-11-015R0, General Admin & FOC Change for Dec 2010

BCR-PRC-11-010R0, PMB Alignment to Contract Price Adjustment Request

BCR-PRC-11-014R0, MR Adjustment for PRC Baseline, Rev 2 Update

MILESTONE STATUS

None currently identified.

SELF-PERFORMED WORK

The Section H clause entitled, "Self-Performed Work," is addressed in the Monthly Report Overview.

GOVERNMENT FURNISHED SERVICES AND INFORMATION (GFS/I)

None currently identified.
