


HANFORD SITE PERFORMANCE REPORT	PHMC FY 1998 PERFORMANCE AGREEMENT STATUS	APRIL 1998
------------------------------------	---	------------

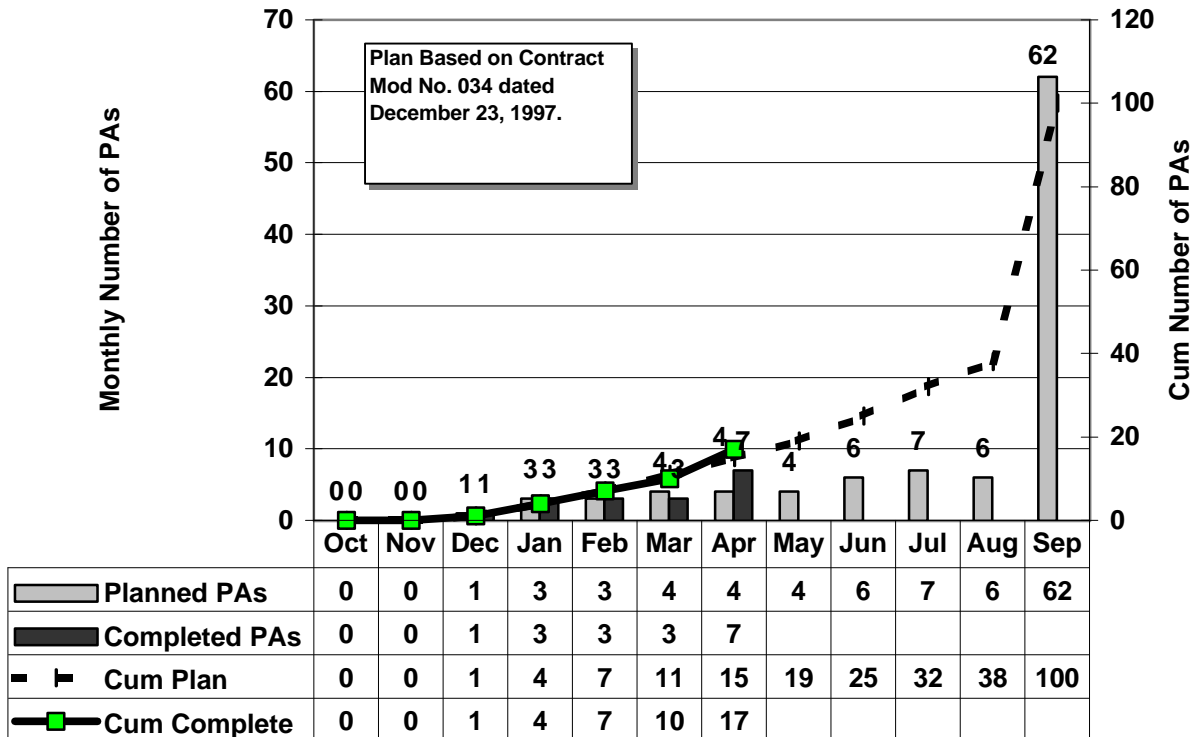

#### Completion Notes and Variance Explanation:

January: TWR3.4.3, "W-030 Vent System," due January 23, 1998; completed March 20, 1998. PA is counted as a January completion.

March: SNF5.1.1, "Establish Technical Baseline," due March 31, 1998. New completion date is August 25, 1998.

April: TWR1.2.1 Authorization Basis due May 1, 1998, complete April 30, 1998.  
 TWR5.1.1 W-464 Validation due July 15, 1998; complete April 15, 1998.  
 TWR1.2.7 DNFSB 93-5 due September 30, 1998; complete April 30, 1998.
