## APR 02 1998 4 STA# 4

### **ENGINEERING DATA TRANSMITTAL**

Page 1 of

1. EDT 623670

Transfer System	2. To: (		iving Orga ON	nization	)	3. From: (Originating Organization) Replacement Cross-Site					on)	4. Related	EDT No.				
Sengrance   Seng												7 Punghasa Ondon No. s					
S. originator Remarks:   See   Section   See   Section   See   Section   See   Section   See	5. Proj./	/Prog.	./Dept./Di	v.:			utho	rity/ D	esign	Agent/	Cog.						
11.   Receiver Remarks:   11A.   Design Baseline Document?     Yes	W-058/	'Star	rtup			GL Parso	ns					N/A					
10. System/Bldg./Facility:   11. Receiver Remarks:   11A. Design Baseline Document?     Yes				•							ŀ	9. Equip./	-				
11. Receiver Remarks: 11A. Design Baseline Document? [] Yes [X] No  12. Major Assm. Dwg. No.:  13. Permit/Permit Application No.:	For Re	leas	e								[		<u>N/</u>	<u> </u>			
13.   Permit/Permit   Application   No.   N/A     14.   Required   Response   Date:   N/A     15.											.	10. System	n/Bldg./F	acility:	1		
13.   Permit/Permit   Application   No.   N/A     14.   Required   Response   Date:   N/A																	
15.   DATA TRANSMITTED   CID	11. Recei	iver (	Remarks:	11A.	Design Ba	seline Docume	ent?	[] \	Yes	[X]	No	12. Major	Assm. Dw	g. No.:			
14. Required Response Date: N/A   15.   DATA TRANSMITTED   (C)   (G)   (H)   (I)   (G)   (H)   (I)											Ī	13. Permit		* -	ion No.:		
15.   DATA TRANSMITTED   CF   CG   CH   CJ											ł	14. Requir		<del></del>			
(C) Sheet No. (E) Title or Description of Data Transmitted (F)							_				]						
(C) Sheet No. (C) Sheet No. (C) Sheet No. (E) Title or Description of Data Transmitted (C) Designator (F) Transmitted (C) Transmitted (C) Designator (F) Transmitted (C) Transmitted (C) Designator (F) Designator (F) Designator (F) Designator (F) Designator (F) Disp. (F)	15				DAT	A TRANSMITTED						(F)	(G)	(H)	(1)		
Read   Reserved   Re				<u> </u>				/C) Title	Dan		4 D-40	Approval	Reason	Origi-	Receiv-		
16. KEY Approval Designator (F) Reason for Transmittal (G) Disposition (H) & (I) E, S, Q, D or N/A (see WHC-CM-3-5, Sec.12.7) Sec.12.7)  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason Disp. (K) Signature (L) Date (M) MSIN Reason Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason Disp. (J) Design Authority (MG Brown Market Date (L-7))  Report, Cross-Site Touristional Test SQ 1 1 1  1		(B) D	ocument/Dra	wing No.	<b>I</b>			(E) TILLE		-	or Data	-	i I		· •		
Report, Cross-Site Transfer System Integrated Test (POTR-007)  16.  Approval Designator (F)  Reason for Transmittal (G)  E, S, Q, D or N/A (see WHC-CM-3-5, 2. Release 5. Post-Review 3. Information 6. Dist. (Receipt Acknow. Required)  17. SIGNATURE/DISTRIBUTION (See Approval Designatures)  (G) (H) (Disposition (H) & (I)  1. Approved 4. Reviewed no/comment 5. Reviewed w/comment 3. Disapproved w/comment 6. Receipt acknowledged  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (G) (H) (G) (H) (G) (G) (G) (G) (G) (G) (G) (G) (G) (G	NO.			No. No.						, ideo							
Report, Cross-Site Transfer System Integrated Test (POTR-007)  16.  Approval Designator (F)  Reason for Transmittal (G)  E, S, Q, D or N/A (see WHC-CM-3-5, Sec.12.7)  1. Approval  2. Release  5. Post-Review  2. Approved w/comment  2. Approved w/comment  3. Disapproved w/comment  5. Reviewed w/comment  5. Reviewed w/comment  3. Disapproved w/comment  6. Receipt acknowledged  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (G) (H) (Disp. (J) Name (K) Signature (L) Date (M) MSIN (K) (K) (K) Signature (L) Date (M) MSIN (K) (K) (K) Signature (L) Date (M) MSIN (K)	1 H	HNF-	2504	0 Preoperational Test						Test	SQ	1	1				
Integrated Test (POTR-007)  16.  KEY  Approval Designator (F) Reason for Transmittal (G) Disposition (H) & (I)  E, S, Q, D or N/A (see WHC-CM-3-5, Sec.12.7)  1. Approval 4. Review 2. Release 5. Post-Review 2. Release 5. Post-Review 3. Information 6. Dist. (Receipt Acknow. Required)  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason Point (K) Signature (L) Date (M) MSIN Son Son Signature (L) Date (M) MSIN Son Signature (L) Date (M) MSIN Son Son Signature (L) Date (M) MSIN Son Son Signature (L) Date (M) MSIN Son Signature (L) Date (M) MSIN Son Signature (L) Date (M) MSIN Son Signature (L) Date (M) MSIN Son Signature (L) Date (M) MSIN Sign					1	-						`.					
(POTR-007)  16. KEY  Approval Designator (F) Reason for Transmittal (G) Disposition (H) & (I)  E, S, Q, D or N/A (see WHC-CM-3-5, Sec.12.7)  1. Approval 4. Review 2. Release 5. Post-Review 3. Information 6. Dist. (Receipt Acknow. Required)  17. SIGNATURE/DISTRIBUTION  (See Approval Designator for required signatures)  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason															}		
Approval Designator (F)  E, S, Q, D or N/A (see WHC-CM-3-5, Sec.12.7)  Reason for Transmittal (G)  1. Approval 1. Approval 2. Review 2. Release 5. Post-Review 3. Information 6. Dist. (Receipt Acknow. Required)  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (H) Rea- Son  (H) Rea- Son  (K) Signature (L) Date (M) MSIN Son  (K) Signature (L) Date (M) MSIN Son  (G) (H) Rea- Son  (G) (H) Rea- Son  (G) (H) Rea- Son  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Son  (K) Signature (L) Date (M) MSIN Son  (G) (H) Rea- Son (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Son										Test							
Approval Designator (F)  Reason for Transmittal (G)  E, S, O, D or N/A (see WHC-CM-3-5, Sec.12.7)  1. Approval 2. Release 5. Post-Review 2. Approved w/comment 5. Reviewed no/comment 5. Reviewed w/comment 6. Receipt acknowledged  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (H) Rea- son  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Rea- son  (K) Signature (L) Date (M) MSIN Rea- son  (G) Rea- son  (K) Signature (L) Date (M) MSIN							<u>(P</u>	OTR-C	007)	<del></del>	<del></del>						
Approval Designator (F)  Reason for Transmittal (G)  E, S, O, D or N/A (see WHC-CM-3-5, Sec.12.7)  1. Approval 2. Release 5. Post-Review 2. Approved w/comment 5. Reviewed no/comment 5. Reviewed w/comment 6. Receipt acknowledged  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (H) Rea- son  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Rea- son  (K) Signature (L) Date (M) MSIN Rea- son  (G) Rea- son  (K) Signature (L) Date (M) MSIN			<u>.</u>								<del></del>		··· <u>-</u> .				
Approval Designator (F)  Reason for Transmittal (G)  E, S, O, D or N/A (see WHC-CM-3-5, Sec.12.7)  1. Approval 2. Release 5. Post-Review 2. Approved w/comment 5. Reviewed no/comment 5. Reviewed w/comment 6. Receipt acknowledged  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (H) Rea- son  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Rea- son  (K) Signature (L) Date (M) MSIN Rea- son  (G) Rea- son  (K) Signature (L) Date (M) MSIN											<u></u>						
Approval Designator (F)  Reason for Transmittal (G)  E, S, O, D or N/A (see WHC-CM-3-5, Sec.12.7)  1. Approval 2. Release 5. Post-Review 2. Approved w/comment 5. Reviewed no/comment 5. Reviewed w/comment 6. Receipt acknowledged  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (H) Rea- Son  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Rea- Son							<u> </u>						<u> </u>	<u> </u>			
E, S, Q, D or N/A (see WHC-CM-3-5, Sec.12.7)  1. Approval 4. Review 2. Release 5. Post-Review 3. Information 6. Dist. (Receipt Acknow. Required)  1. Approved 4. Reviewed no/comment 5. Reviewed w/comment 6. Receipt acknowledged  1. Approved 4. Reviewed no/comment 5. Reviewed w/comment 6. Receipt acknowledged  1. Approved w/comment 6. Receipt acknowledged  1. Approved 4. Reviewed no/comment 5. Reviewed w/comment 6. Receipt acknowledged  1. Approved w/comment 6. Receipt acknowledged								KEY				Di	- 00 ° 0	<u> </u>			
(see WHC-CM-3-5, Sec.12.7)  2. Release 5. Post-Review 3. Information 6. Dist. (Receipt Acknow. Required)  17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN Reason  17. Design Authority WG Brown Manual Results (L) Date (M) MSIN Son  (G) (H) Disp. (K) Signature (L) Date (M) MSIN Reason Son (R) Disp. (K) Signature (L) Date (M) MSIN Son (M) MSIN				1 4 4 4 4 4			(G)			1 An	nroved		<del></del> _	no/comme	ent		
17. SIGNATURE/DISTRIBUTION  (See Approval Designator for required signatures)  (G) (H) Disp. (J) Name (K) Signature (L) Date (M) MSIN  son (K) Signature (L) Date (M) MSIN  1/2 1 Design Authority WG Brown Warren Brown 14-07										2. Ap	proved w/cor	mment 5	. Reviewed	w/comme	nt		
(G) (H) (J) Name (K) Signature (L) Date (M) MSIN Reason Son (K) Signature (L) Date (M) MSIN Reason Son (L) Design Authority WG Brown Manuflum (L-07)	Sec.12.7)			3. Inform	nation 6. Di			<del></del> -			approved w/	comment 6	8. Receipt a	cknowledg	ed		
(G) (H) Rea- son								-			ıres)				ļ		
Rea- son Disp. (J) Name (K) Signature (L) Date (M) MSIN Rea- son 1/2 1 Design Authority WG Brown Manual France (4-07)	(G)	(H)	<del></del>	<del></del>		<del></del>						444			a) Macros		
1/2 1 Design Authority WG Brown Warran France 14-07	Rea- D		(J) Nam	ne (l	() Signature	(L) Date (M) N				Disp.	(J) Name	s (K) Sig	gnature (i	T) Date (I	VI) IVISIN		
	<del></del>	1	Design At	ıthorî tv	WG Brown	Warren Pern	440	_									
N/A N/A Design Agent N/A A A		N/A															
1/2 1 Proj. Startup EA Pacquet 3/31 (3-47			Proj. Sta														
1/2 1 Proj. Mgr. GL Parsons TA (Jana 41-783-47	<del></del>														·		
1/2 1 QA LR Hali & R. Hall & R. L. L. July 3/31/9:55-12				ialio (Socialis)	KHAK	A 4/1/48 2			<del></del> +					· · · · · ·			
1/2 1 Safety OM Jaka 7 1/2 5/31/9:\$5-12  N/A N/A Env. N/A					/···	- V-VIII - 1-117	ا رس								_ <del></del>		
18. 19. 20. 21. DOE APPROVAL (if required)		.,			<del></del>	<u></u>		20.				21. DOE A	PPROVAL (	if requi	red)		
Ctrl. No.	. ا			- 1	i	1			****			Ctrl.	No.	•			
EA Pacedet 3/31/98 EA Pacquet 3/31/98 GL Parsons 4-1-98 [] Approved w/comments	EA Pacarte	et	<u> </u>	1/98	racquet	3/31	<u> </u>	11-1	Par	ons	4-1-98	[] Approv	ed w/comm	nents			
Signature of EDT Date Authorized Representative Date Design Authority/ Date [] Disapproved w/comments Originater for Receiving Organization Cognizant Manager			Date	Au		sentative Date		_		-	Date	[] Disapp	roved w/c	comments			

### PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007)

**EA Pacquet** 

Numatec Hanford Corporation, Richland, WA 99352 U.S. Department of Energy Contract DE-AC06-96RL13200

EDT/ECN: 623670

UC: 2030

Org Code: 8C610

Charge Code: N58U7

B&R Code: 39EW31301 Total Pages: 296

Key Words: Project W-058, Transfer Headers 3150 and 3160, interlocks, slurry booster pumps P3125A and P3125B, variable speed drives, automatic flow control, header venting and draining.

Abstract: This report documents the testing of the booster pump instrumentation and interlocks, performance tesing of the booster pumps and transfer headers using water for Project W-058.

TRADEMARK DISCLAIMER. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

Printed in the United States of America. To obtain copies of this document, contact: Document Control Services, P.O. Box 950, Mailstop H6-08, Richland WA 99352, Phone (509) 372-2420: Fax (509) 376-4989,

HANFORD RELEASE ID:

Release Stamp

Approved for Public Release

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 1 OF 21

**REVISION NO. 0** 

Author

E.A. Pacquet

APPROVAL DESIGNATOR SQ

3/31/98 Date

TEST REPORT APPROVAL BY TEST REVIEW BOARD (TRB)

TER Chair

3/31/93

16/ 1-1-98

WRS Engineering Date

Ocurs Yerken 3/31/98
Startup Engineer Date

hill a lings

MA Parama 4-1-98
Project Management Date

# PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 2 OF 21

### REVISION NO. 0

### **TABLE OF CONTENTS**

1.0	ATTACHMENTS	Page 3
2.0	REFERENCES	Page 3
3.0	INTRODUCTION	Page 3
4.0	OBJECTIVES	Page 3
5.0	SUMMARY OF TEST RESULTS	Page 4
6.0	TESTING CONFIGURATION	Page 5
7.0	RESULTS - DISCUSSION	Page 5
8.0	NOTABLE EVENTS AND TEST EXCEPTIONS	Page 8
9.0	CONCLUSION	Page 10
10.0	LIST OF FIGURES	Page 10

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 3 OF 21

### **REVISION NO. 0**

#### 1.0 ATTACHMENTS

- 1.1 HNF-1857, Rev O-A, with recorded data and test exception reports, and Engineering Change Notice W-058-373
- 1.2 Engineering Change Notice W-058-395
- 1.3 W-058 Interlock Test Listing
- 1.4 NHC letter 9852239

### 2.0 REFERENCES

- 2.1 HNF-SD-W058-SUP-002, Rev. 1, Project W-058 Startup Test Plan
- 2.2 W-058-PI, Rev 2, Procurement Specification, Slurry Transfer Pumps
- 2.3 VI#22798, Supp 28, Slurry Transfer Pumps Factory Acceptance test
- 2.4 Incroporated Engineering Change Notices, W-058-391, W-058-393, W-058-394
- 2.5 NCR W-O58-27
- 2.6 W-058 OAC Part II
- 2.7 FDNW letter LMHC-96W0-0006, CO-98-TWRS-202

### 3.0 INTRODUCTION

This report documents the results obtained during the performance of Preoperational Test POTP-007, from December 12, 1997 to March 27, 1998. Six test exceptions were generated during the performance of this test. One unresolved test exception remained at the time of completion of the test.

### 4.0 OBJECTIVES

The main objectives were to demonstrate the operation of the following Cross-Site Transfer System components:

- Booster pumps P-3125A and P-3125B interlocks and controls, both local and remote.
- Booster pump P-3125A and P-3125B and associated variable speed drives VSD-1 and VSD-2 performance in both manual and automatic modes.
- Water filling, circulation, venting and draining of the transfer headers (supernate and slurry line).

As described in reference 1, the following components of the Cross-Site Transfer System that would normally be used during an actual waste transfer, are not used in this specific test:

- Water Flush System.
- Valving and instrumentation associated to the 241-SY-A valve pit jumpers.
- Valving and instrumentation associated to the 244-A lift station.

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 4 OF 21

### **REVISION NO.\_0\_**

#### 5.0 SUMMARY OF TEST RESULTS

Acceptance criteria were met.

- 5.1 The following interlocks operate properly:
  - I-2: On high pressure shutdown, operating booster pump, P-3125A or P-3125B (Criteria Met)
  - I-6: The operating booster pump, P-3125A or P-3125B will shutdown:
    - A) On high pump bearing temperature (Criteria Met)
    - B) On high motor winding temperature (Criteria Met)
    - C) On high vibration (Criteria Met)
    - D) On pump seal failure (Criteria Met)
    - E) On low oil level (Criteria Met)
  - I-7: The pump will not be permitted to operate if the inlet pressure is lower than
     10 psig (Criteria Met)
  - I-9: Transfer pump P-102-SY-02A will not be permitted to start if operating booster pump is shutdown (Criteria Met)
  - I-10: Upstream transfer pump P-102-SY-02A will be shutdown if inlet pressure reaches 70 psig (**Criteria Met**)
  - I-14: On high discharge pressure, shutdown appropriate operating pump (Criteria Met)
  - I-15: The booster pump will not be permitted to start if the associated vent and drain valves are not closed (**Criteria Met**)
  - I-20: (With respect to supernate line vent only): On high pressure, shutdown transfer pump P-102-SY-02A (**Criteria Met**)
- 5.2 Booster pumps P-3125A and P-3125B operated at the design flowrates of 104 gpm ± 7 gpm and 140 gpm ± 7 gpm, and at a high flow condition of 160 gpm ± 7 gpm, under control of system flow feedback. (Criteria Met)
- 5.3 Transfer headers 3150 and 3160 from the Diversion Box to the Vent Station were filled with water; water was circulated through them by the booster pumps; and the headers were vented and drained. (Criteria Met)

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 5 OF 21

### **REVISION NO. 0**

### 6.0 TESTING CONFIGURATION

Water testing of the headers and the pumps was carried out by connecting the slurry and supernate headers in a temporary loop circuit from the Diversion box to the Vent station. Details of the circuit and its configuration are provided in Attachment 1, Appendix A.

### 7.0 RESULTS - DISCUSSION

### 7.1 Pump Instrumentation and Interlocks

Attachment 3 provides a complete inventory and boundaries of W-058 interlock tests, and associated alarm and/or trip set points. All interlocks were tested when practical from the sensing device.

One set-point worthy of interest is the low-oil level set according to the pump vendor's recommendations:

- Normal oil level in bearing housing:
   2.625 inches below shaft centerline
- Minimum oil level in bearing housing: 3.06 inches below shaft centerline
- Drained oil volume to reach minimum oil level: approximately 175 ml to 250 ml

It was also visually checked that the minimum oil level ensured oil coverage of the sling rings in order to provide adequate bearing lubrication.

### 7.2 Slurry Booster Pumps Performance

Prior to site installation both pumps were submitted to a 48 hour factory acceptance test (reference #2).

Over the complete performance of this preoperational test both pumps have undergone the following cumulative run-in time:

P-3125A: 15.0 Hours P-3125B: 12.0 Hours

Data points were collected at varying flowrates (76 to 173 gpm), speeds (50 to 100%), and back pressures in order to cover the full range of operating conditions for the pumps and variable speed drives. Tables 1A and 1B highlight the selected operating conditions and main results for each pump run.

Figures 1 and 2 illustrate the pump curves established for both pumps. Both curves are above the required performance points: (reference #2)

138 gpm at 2260 feet TDH (Total Dynamic Head) 104 gpm at 1850 feet TDH (Total Dynamic Head)

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 6 OF 21

### **REVISION NO. 0**

Throughout the selected operating conditions drive and thrust end bearing temperatures remained stable:

	Pump	P-3125A	Pump P-3125B			
	Min	Max	Min	Max		
Thrust end Temp.°F	64	75	62	80		
Drive end Temp. °F	66	81	62	90		

Aside from the exception discussed in section 8.5, vibration levels (horizontal velocity measurements from installed vibration sensors) for both pumps remained low throughout the range of operating speeds typically ranging as indicated below:

	Thrust end vibration (Velocity, inch/sec)	Drive end vibration (Velocity, inch/sec)
P-3125A	0.01 to 0.09	0.01 to 0.06
P-3125B	0.01 to 0.13	0.01 to 0.09

### 7.3 Variable Speed Drives

In accordance with the manufacturer's recommendations both variable speed drives (VSD) were set as follows:

- Frequency range: 30 Hz to 60 Hz
- Speed range: 1800 rpm to 3600 rpm (50 to 100%)
- In order to avoid over current or over voltage conditions during acceleration or deceleration, linear ramps were set as indicated below per the manufacturer's recommendations:
  - PCU ramp limit = 60 seconds for a 100% speed change (auto mode)
     VSD Acceleration time = 20 seconds for a 100% speed change (manual mode)
  - VSD Deceleration time = 60 seconds for a 100% speed change (manual mode)

Attachment 1 sections 7 through 10, provide recordings of variable speed drives electrical parameters in all the selected operating conditions. Section 8.4 provides a description of the malfunction experienced during initial testing of one of the drives.

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 7 OF 21

### **REVISION NO. 0**

### 7.4 Transfer Headers Pressure Drop

Figure 3 illustrates the measured, circuit, supernate, and slurry line pressure drops as a function of flow. Although these pressure drops are specific of the test circuit and its boundaries, they can easily be extrapolated to the full length of each header. It is also interesting to note that the measurements match quite well the calculated pressure drops established for the design of the test circuit (figure 4).

### 7.5 Transfer Headers Insulation

No significant temperature drop could be measured across the headers during the first day of testing (Attachment 1, Appendix G, System data) where slightly heated water was used (~64°F), hence confirming the good insulation of the lines.

### 7.6 Automatic Flow Control

Satisfactory and stable pump operation under automatic flow control was obtained by tuning the PID (Proportional, Integral, and Derivative) parameters of the flow control loops as indicated below:

P = 0.8 I = 0.06 1/sec D = 0 sec

These parameters established with water, may possibly need to be readjusted with actual waste slurry.

### 7.7 Transfer Headers Venting and Draining

Venting and draining of both headers was performed without any difficulty at an average flow rate of 35 gpm. It was also verified upon completion of this operation that the vent line filters remained dry.

### 7.8 Pump Long Term Maintenance

Refer to Attachment 4 for booster pump long term and storage recommendations.

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 8 OF 21

#### **REVISION NO. 0**

### 8.0 NOTABLE EVENTS AND TEST EXCEPTIONS

### 8.1 Pump 3125A Failure (TE-001)

One December 20, 1997, pump P-3125A failed to startup. It was determined that the pump had "locked-up". Decision was made to disassemble both pumps under vendor supervision in order to determine the cause of failure. The vendor determined that the pump had lock-up because if was provided with a non protected (non overlaid) surface on the hub side of the impellers. Both pumps were subsequently modified to include a hub side wear ring and all wear rings were overlaid with the same type of material as the eye side wear ring for abrasive service. Further details regarding the mode of failure and corrective actions can be found in attachments to test exception TE001. Testing was resumed on February 11, 1998 upon completion of the corrective work and closeout of the associated nonconformance reports.

### 8.2 Pump Seals Replacement (TE-002)

During the initial run of Pump 3125A, leakage was observed from the pump air seals. All seals were replaced by upgraded "wavy face" technology seals upon the seal vendor's recommendation. Further details can be found in attachments to test exception TE002.

### 8.3 Pump 3125A Vent Valve MOV-3125AK (TE-003)

MOV 3125AK was found to be leaking and was replaced. Pump runs performed on P-3125A prior to the valve replacement were repeated as pump discharge pressure recordings (see Attachment 1, Appendix G System data) were affected by the leak.

### 8.4 Pump 3125B Variable Speed Drive (TE-004)

Refer to test exception TE-004 and its attachments for the details and resolution of the encountered malfunction.

#### 8.5 Pump 3125A and 3125B Vibration (TE-005)

During the pump runs, abnormal vibrations (horizontal velocity from installed vibration sensors) at critical speeds were identified:

P-3125A: 0.6 to 0.8 IPS at 3000 rpm
 P-3125B: 0.2 to 0.3 IPS at 2950 rpm

In the case of P-3125A, the level of vibration is high enough to activate the pump shutdown interlock set at 0.6 IPS. For P-3125B, the pump and motor vendors have determined that these vibration levels are acceptable.

A first diagnosis established by the pump vendor (see vibration analysis report attached to Test Exception 005) seem to attribute the vibration levels to a resonance generated by a motor imbalance. The vibration analysis also identified high overall vertical vibration levels at full speed (3600 rpm) for both pumps. Subsequent attempts to balance both motors by the motor vendor (field report pending) have not allowed any significant

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 9 OF 21

### **REVISION NO. 0**

reduction of the observed vibration levels. At the time of writing of this report, resolution of the problem is being carried as an exception to the W-058 OAC Part II (reference 5 - Facility Testing - Exception 1) and considered a pump warranty item.

Further diagnosis and corrective actions (see reference 7) are still needed.

### 8.6 Pump Stop/Start Signal (TE-006)

It was observed that both pumps restarted automatically after shutdown by a variable speed drive fault. This problem was corrected by ECN W058-391 and W-058-393 and retested accordingly.

### 8.7 Loss of Communication to PCU-2

Upon loss of communication or power to PCU-2, it was noticed that the operating booster pump continues to run. Loss of communication was simulated in this case by disconnecting the input/output fiber optic connections at PCU-2. Loss of power was simulated by disconnecting the fuses to the PCU-2 processor (note: the analog input/output power supply remained energized).

## PREOPERATIONAL TEST REPORT, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST (POTR-007) HNF- 2504 PAGE 10 OF 21

REVISION NO. 0\_

### 9.0 CONCLUSION

Components included in this test procedure have been tested to the engineering requirements established by the design documentation and are deemed to have satisfactorily met their functional design criteria. One exception however subsists (slurry booster pump vibration level) and will need to be resolved.

### 10.0 LIST OF FIGURES AND TABLES

- Table 1A: P-3125A Selected operating conditions and results
- Table 1B: P-3125B Selected operating conditions and results
- Figure 1: P-3125A performance curves
- Figure 2: P-3125B performance curves
- Figure 3: Circuit pressure drops
- Figure 4: Calculated circuit pressure drops

TABLE 1 A

### POTP 007 SELECTED OPERATING CONDITIONS - RESULTS

### SLURRY BOOSTER PUMP P3125A


VSD	MODE	Inlet P	Outlet P	FLOW	TDH	PI 3126B	Pl temp2	DP cicuit	DP SLL	DP SNL	DP1-DP2
rpm		psig	psig	gpm	feet	psig	psig	psig	psig	psig	psig
						404	455	422	102	29	74
1650	Manual	66	287	76	580	184	155	132	103		1 .
2608	Manual	57 .	570	110	1255	404	310	<b>260</b> .	166	94	72
3529	Manual	52	971	148	2192	624	443	528	347	181.	166
3522	Manual	33	871	173	2005	557	310	561	314	247	67
1875	Auto	58	273	110	567	109	13	260	164	96	68
1965	Auto	58	302	110	634	137	45	257	165	92	73
2150	Auto	59	375	110	800	213	120	255	162	93	69
2430	Auto	47	415	140	920	182	20	395	233	162	. 71
2530	Auto	47 .	460	140	1024	227	68	392	233	159	74
2725	Auto	47	555	140	1243	324	163	392	231	161	70
2690	Auto	42	490	155	1105	225	30	460	265	195	70
2745	Auto	42	520	155	1174	254	- 60	460	266	194	72
2850	Auto	42	575	155	1301	306	110	465	269	196	73

### POTP 007 SELECTED OPERATING CONDITIONS - RESULTS

### SLURRY BOOSTER PUMP P3125B

VSD	MODE	Inlet P	Outlet P	FLOW	TDH	PI 3126B	PI temp2	DP cicuit	DP SLL	DP SNL	DP1-DP2
rpm	,	psig	psig	gpm	feet	psig	psig	psig	psig	psig	psig
1820	Manual	65	301	84	615	181	130	171	120	51	69
2200	Manual	60	403	. 97	862	260	. 180	223	143	80	63
2560	Manuai	56	522	110	1146	350	240	282	172	110	62
2915	Manual	51	663	123	1483	460	310	353	203	150	53
3650	Manual	54	1027	147	2317	763	570	457	264	193	71
3650	Manual	54	970	164	2185	660	400	570	310	260	50
2000	Auto	57	295	110	620	120	15	280	175	105	70
2100	Auto	57	330	110	700	156	55	275	174	101	73
2300	Auto	57	410	110	885	. 235	130	280	175	105	70
2610	Auto	46	455	140	1015	202	20	435	. 253	182	71
2710	Auto	46	507	140	1135	262	85	422	245	177	68
2910	Auto	. 46	610	140	1373	366	195	415	244	171	73
2850	Auto	40	525	155	1190	242	25	500	283	217	66
2950	Auto	40	573	155	1301	285	75	498	288	210	78
3150	Auto	40	692	155	1576	404	195	497	288	209	79

T (POTR-007)
PAGE 13 OF :

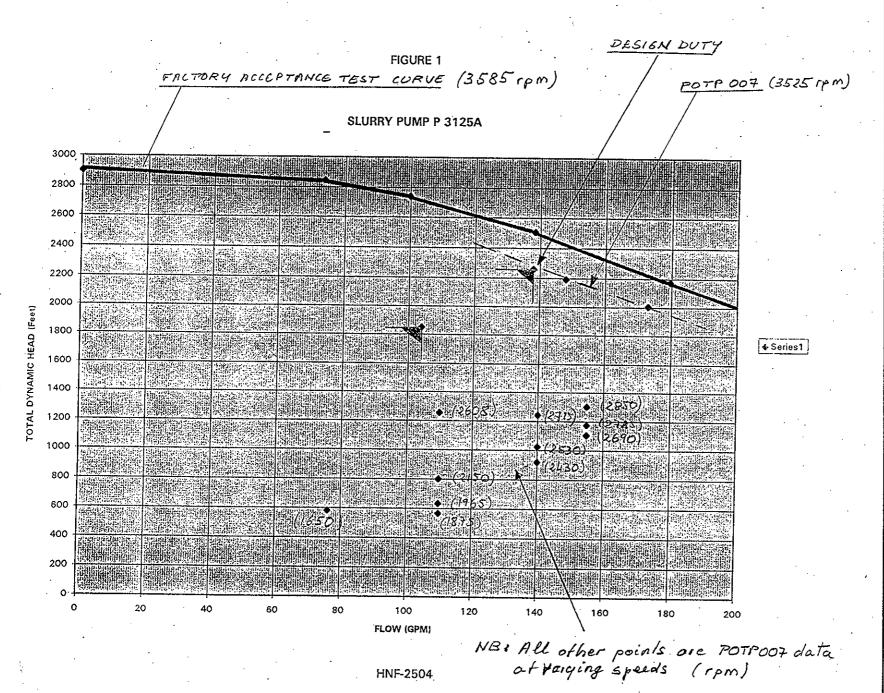

REVISION NO. 0


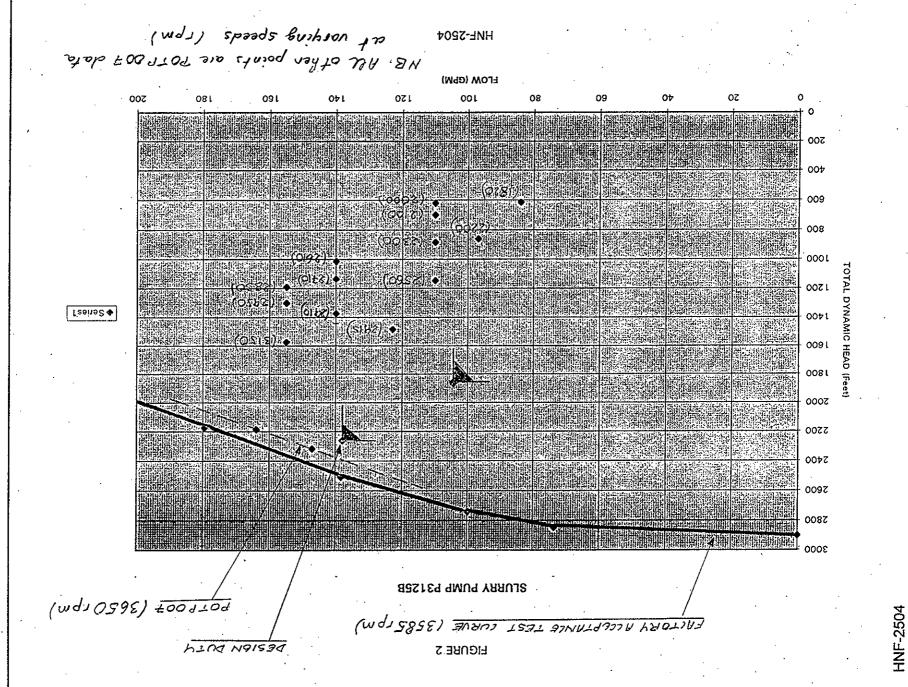


FIGURE 3


### POTP 007 CIRCUIT AND LINE PRESSURE DROP

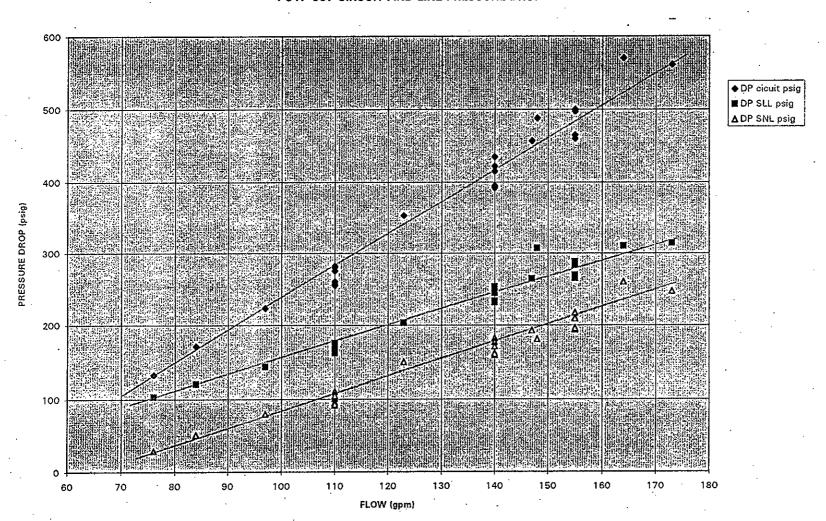

HNF-2504


: 0.866

HNF-2504

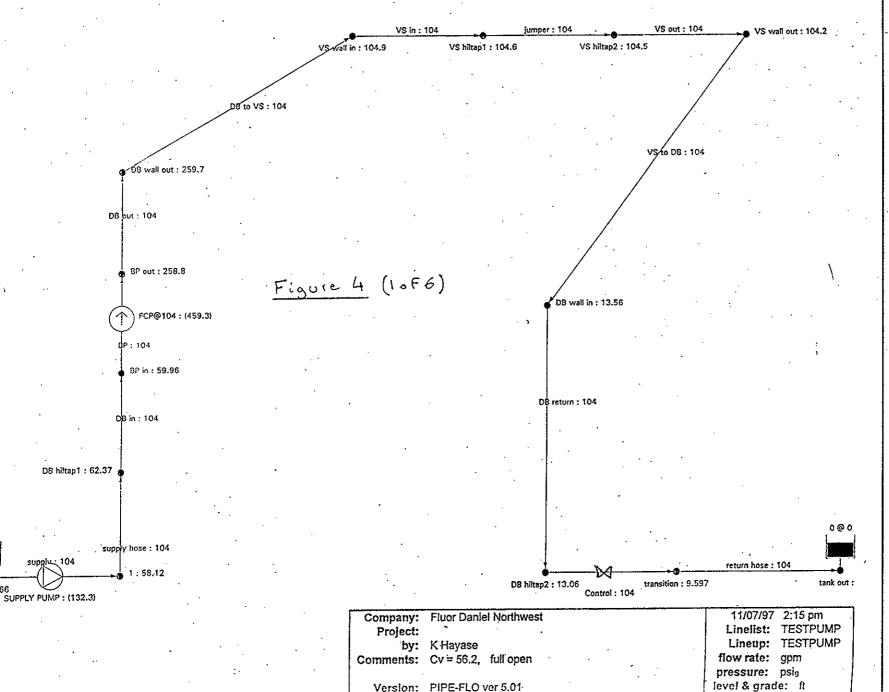



tank out:


0@2

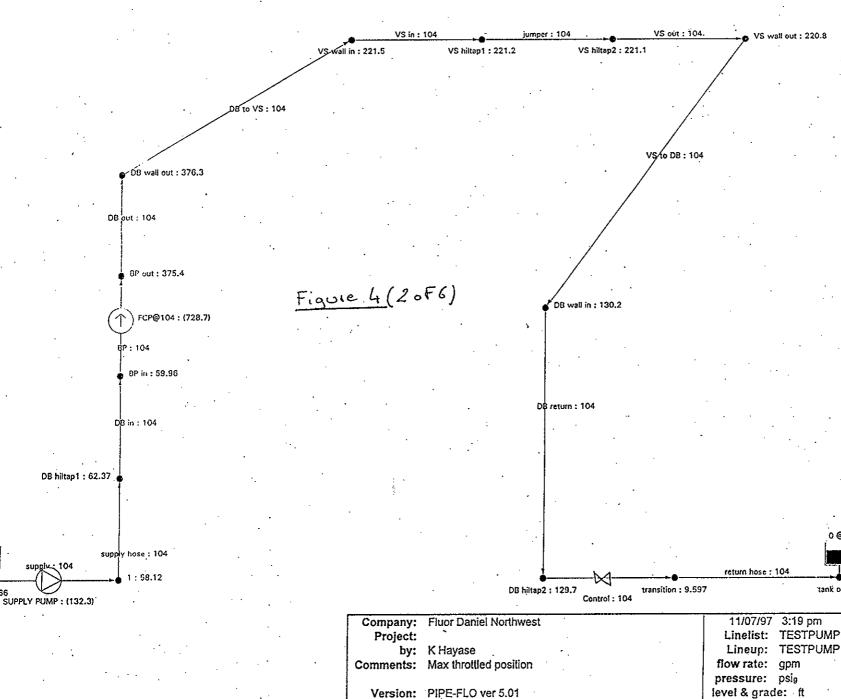


: 0.866

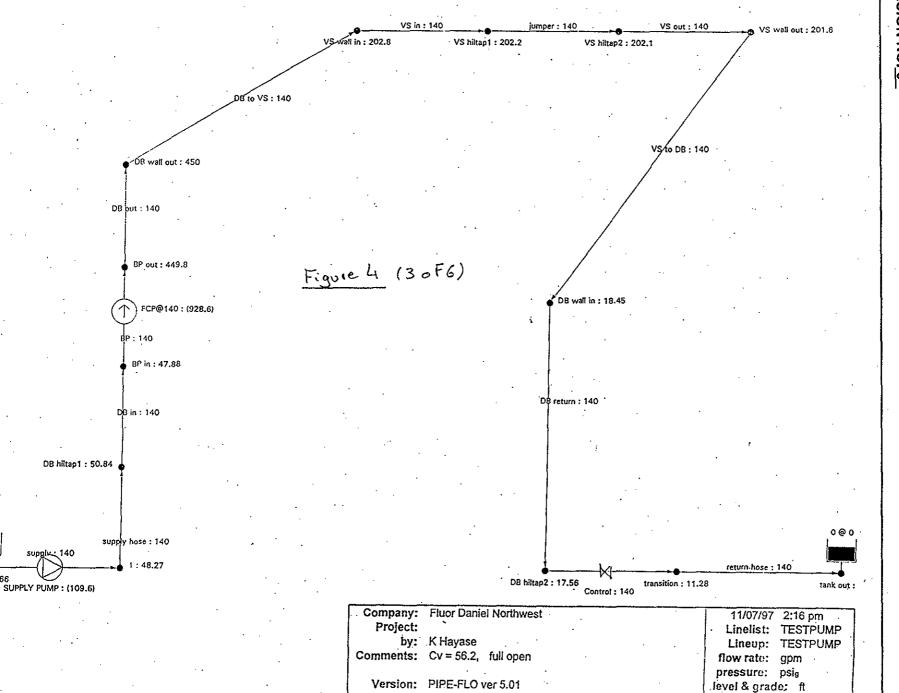




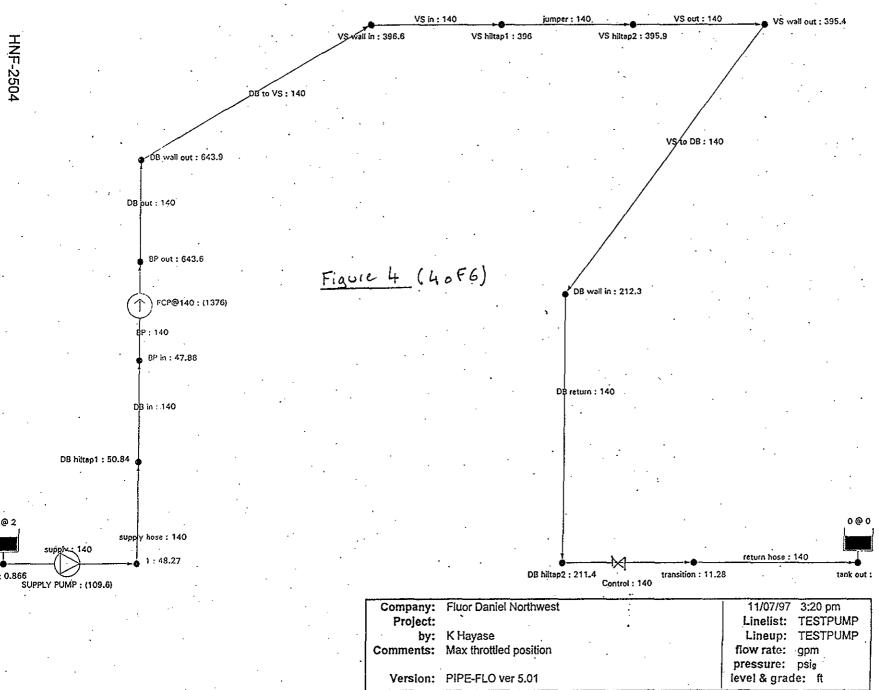


HNF-2504

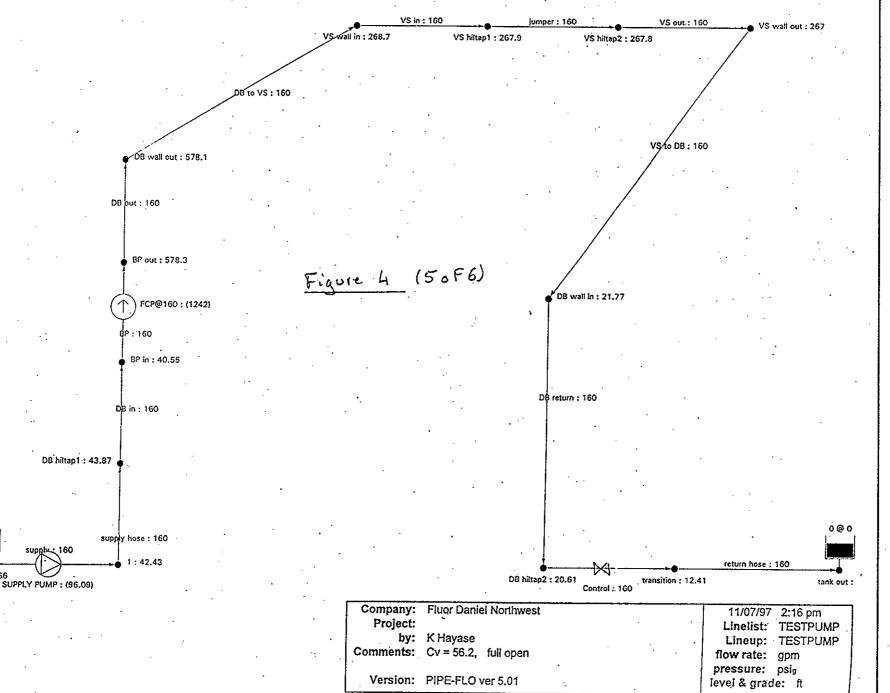

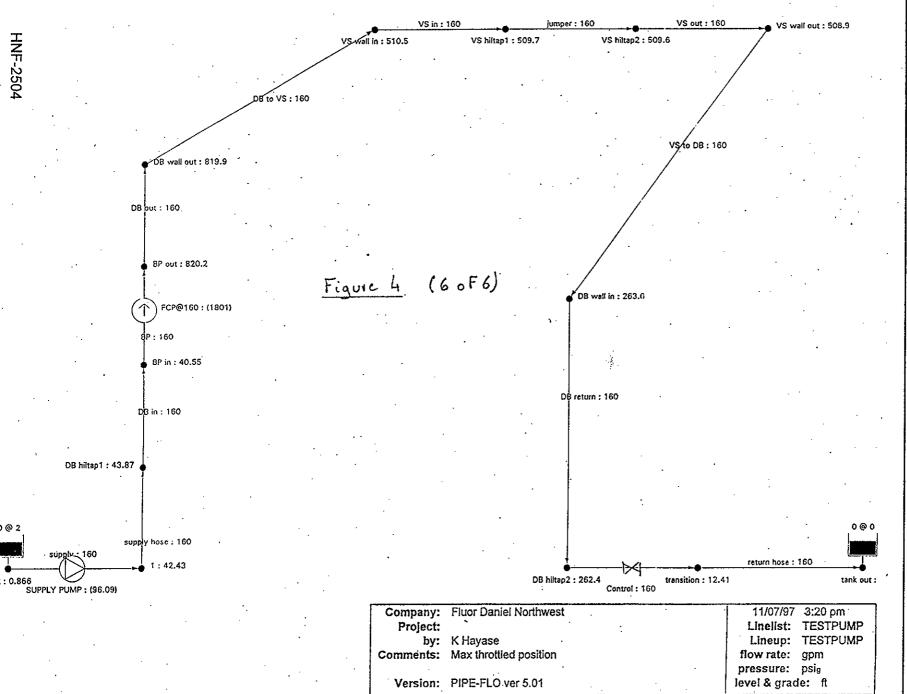

### **ENGINEERING CHANGE NOTICE**



1. ECNL 644614

Proj. W-058-373

2. ECN Category (mark one)	<ol> <li>Originator's Name and Telephone No.</li> </ol>	e, Organization, MSIN,	4. USQ Requi	red?	5. Date
Trologo		SC, S2-24, 373-	[] Yes []	() No	12/15/97
Supplemental Y	4434				
Change ECN [] Temporary []	6. Project Title/No.	_	7. Bldg./Sys	,	8. Approval Designator
Standby [] Supersedure []		ement Cross-Site	624	I-A	SQ .
Cancel/Void []	<del></del>	System/N58U7 Changed by this ECN	10. Related	FCN No(s)-	11. Related PO No.
	(includes sheet r	no. and rev.)			
	<u> </u>	7, Rev. 0	N/		N/A
12a. Modification Work	12b. Work Package No.	12c. Modification Work	Complete		red to Original Condi- , or Standby ECN only)
[] Yes (fill out Blk.	N/A	N/A .		N/A	
12b) [X] No (NA Biks. 12b,					11
12c, 12d)		Design Authority/Cog. Signature & Da	_		uthority/Cog. Engineer ignature & Date
13a. Description of Change	:	13b. Design Baseline	Document? [	Yes [X	(] No
Replace pages 13 am		57, Rev. O.			
	6 3 5 0 0 4 4 0 - 0	150 47 60 of 150	60 of 150	77 70	of 1k0 and 00 00
Replace pages 20 of of 150 in attachmen			161 10 80	), //-/ð (	OL 120 944 98-20
Add pages 49a, 63a	and 63b of 150	) to attachment A o	f HNF-1857	. Rev. 0	
42	, 4,14 005 01 100			,	•
1/2/15/97					í
· ·		•			
		•	•		
		•			
		·			
14a. Justification (mark o	one)	·			·
14a. Justification (mark of Criteria Change []	one) Design Improvement	[] Environmental	[]	Facili	ty Deactivation []
Criteria Change [] As-Found []	Design Improvement Facilitate Const	[] Environmental [] Const. Error/C	£ 7		ty Deactivation [] n Error/Omission [X]
Criteria Change [] As-Found [] 14b. Justification Details	Design Improvement Facilitate Const	[] Const. Error/C	Omission []	Design	Error/Omission [X]
Criteria Change [] As-Found [] 14b. Justification Details Testing of the boos	Design Improvement Facilitate Const s ster pump(s) P-3	[] const. Error/0	omission []	Design	Error/Omission [X] Witches and
Criteria Change [] As-Found []  14b. Justification Details Testing of the book vibration instrument the interlock 6 testing and the content of the content o	Design Improvement Facilitate Const s ster pump(s) P-3 ntation improved st, added test of	Const. Error/C Bl25A and P-3125B b I, eliminated redun of interlock 2, add	mission [] earing oil	Design level sing of in	Error/Omission [X]  Witches and terlock 9 within
Criteria Change [] As-Found []  14b. Justification Details Testing of the book vibration instrume	Design Improvement Facilitate Const s ster pump(s) P-3 ntation improved st, added test of	Const. Error/C Bl25A and P-3125B b I, eliminated redun of interlock 2, add	mission [] earing oil	Design level sing of in	Error/Omission [X]  Witches and terlock 9 within
Criteria Change [] As-Found []  14b. Justification Details Testing of the book vibration instrument the interlock 6 testing and the content of the content o	Design Improvement Facilitate Const s ster pump(s) P-3 ntation improved st, added test of	Const. Error/C Bl25A and P-3125B b I, eliminated redun of interlock 2, add	mission [] earing oil	Design level sing of in pump mo	witches and terlock 9 within tor rotation
Criteria Change [] As-Found []  14b. Justification Details Testing of the book vibration instrumenthe interlock 6 techniques	Design Improvement Facilitate Const s ster pump(s) P-3 ntation improved st, added test of d miscellaneous	[] const. Error/C B125A and P-3125B b I, eliminated redun of interlock 2, add changes.	mission [] earing oil	Design level sing of in	witches and terlock 9 within tor rotation
Criteria Change [] As-Found []  14b. Justification Details Testing of the book vibration instrument the interlock 6 testing and the content of the content o	Design Improvement Facilitate Const s ster pump(s) P-3 ntation improved st, added test of d miscellaneous	[] const. Error/C B125A and P-3125B b I, eliminated redun of interlock 2, add changes.	mission [] earing oil	Design level sing of in pump mo	witches and terlock 9 within tor rotation
Criteria Change []  As-Found []  14b. Justification Details  Testing of the book vibration instrumed the interlock 6 tek direction check and  15. Distribution (include FDNW DISTRIBUTION  LR Hall R3-47	Design Improvement Facilitate Const  ster pump(s) P-3 ntation improved st, added test of d miscellaneous  name, MSIN, and no. of DISTRIBUTION  GA Leshikar, SES	Const. Error/C  3125A and P-3125B b  1, eliminated redun  2, add  3, changes.  3, copies)	mission [] earing oil	Design level sing of in	witches and terlock 9 within tor rotation
Criteria Change []  As-Found []  14b. Justification Details  Testing of the book vibration instrumed the interlock 6 tek direction check and  15. Distribution (include FDNW DISTRIBUTION  LR Hall R3-47 Dowell G3-21	Design Improvement Facilitate Const  ster pump(s) P-3 ntation improved st, added test of d miscellaneous  name, MSIN, and no. of DISTRIBUTION  GA Leshikar, SES EA Pacquet, NHC	Const. Error/C  3125A and P-3125B b  1, eliminated redun  2, add  3, changes.  3, copies)  3, copies  4, copies  6, copies	mission [] earing oil	level song of in pump mo	witches and terlock 9 within tor rotation
Criteria Change [] As-Found []  14b. Justification Details Testing of the book vibration instrument the interlock 6 tek direction check and  15. Distribution (include FDNW DISTRIBUTION  LR Hall R3-47	Design Improvement Facilitate Const  ster pump(s) P-3 ntation improved st, added test of d miscellaneous  name, MSIN, and no. of DISTRIBUTION  GA Leshikar, SES EA Pacquet, NHC C. van Katwijk, MD Gerken, NHC	Const. Error/C  3125A and P-3125B b  I, eliminated redun  of interlock 2, add  changes.  of copies)  CC R3-47 R3-47 R3-47 R3-38	mission [] earing oil	Design level sing of in	witches and terlock 9 within tor rotation
Criteria Change []  As-Found []  14b. Justification Details Testing of the book vibration instrumed the interlock 6 tek direction check and  15. Distribution (include FDNW DISTRIBUTION  LR Hall R3-47 Dowell G3-21 Friedrich G3-14	Design Improvement Facilitate Const  ster pump(s) P-3 ntation improved st, added test of d miscellaneous  name, MSIN, and no. of DISTRIBUTION  GA Leshikar, SES EA Pacquet, NHC C van Katwijk, M MD Gerken, NHC GL Parsons, NHC MJ Sutey, LMHC	Const. Error/C  B125A and P-3125B b  I, eliminated redun  of interlock 2, add  changes.  of copies)  CC R3-47 R3-47 R3-47 R3-38 R3-47 T4-08	mission [] earing oil	level song of in pump mo	witches and terlock 9 within tor rotation
Criteria Change []  As-Found []  14b. Justification Details Testing of the book vibration instrumed the interlock 6 tek direction check and  15. Distribution (include FDNW DISTRIBUTION  LR Hall R3-47 Dowell G3-21 Friedrich G3-14	Design Improvement Facilitate Const  ster pump(s) P-3 ntation improved st, added test of d miscellaneous  name, MSIN, and no. of DISTRIBUTION  GA Leshikar, SES EA Pacquet, NHC C van Katwijk, M MD Gerken, NHC GL Parsons, NHC	Const. Error/C  B125A and P-3125B b  I, eliminated redun  of interlock 2, add  changes.  of copies)  CC R3-47 R3-47 R3-47 R3-38 R3-47 T4-08	mission [] earing oil	level song of in pump mo	witches and terlock 9 within tor rotation

	<u>,</u>							f	, dat	
	 EN	GINEERIN	G CHANG	E NOTIC	E .		Page 2	Elna	de 7. ECN (use no. 1644614 W-1	-
$\perp$							Page Z		18. Schedule Impact	
	l6. Design Verification Required	17. Cost Im	pact NGINEERING	NA		CONSTRU	CTION N		•	A
	I Yes	Additional	[]	8	Additional	-	[] \$_		Improvement	1
	EV2	Savings	1.1	\$	Savings		11 \$		Delay [	1
<b>7</b>	[X] No		- 1	oted decim		than th	o opnine	erina doci	ments identified o	n Side 1)
	that will be af SDD/DD	fected by the	e change des	cribed in	Block 13.     E ress Analysis	inter th	e affect	ed documen	nt number in Block i ank Calibration Manual	20.
		L,	<u> </u>				11		lealth Physics Procedure	
	Functional Design Criteria	1		Stress/Des	· /	•	ΙJ			LJ
-	Operating Specification	. []			ontrol Drawing	٠.	[]		pares Multiple Unit Listin	LJ
(	Criticality Specification	[]	] /	Calibration	Procedure/		[]		est Procedures/Specifica	tion []
-   (	Conceptual Design Repor	t . [	] /		Procedure		[]		component Index	[]
	Equipment Spec.	. [	1/	Maintenan	ce Procedure		[]	A	SME Coded Item	[]
	Const. Spec.	Ī	7	ngineerin	g Procedure	_/	[]	<b>/</b> ⊦	luman Factor Considerati	ion []
ļ	rocurement Spec.	]	1	Operating	Instruction	$\sqrt{}$	řī.	/ 0	Computer Software	ĪΪ
1,	Vendor Information			Operating	Procedure	•	ři /	E	lectric Circuit Schedule	ĨĨ
1	OM Manual	/ t		U	/ I Safety Require	ement		10	CRS Procedure	้ำ
١,	SAR/SAR	/ L.	] / ]	IEFD Draw	ing .	/	[]	P	rocess Control Manual/P	lan []
	Safety Equipment List	Ĺ,	<u>}</u>	- 1	gement Drawing		1.] f7	P	rocess Flow Chart	1.1 []
	Radiation Work Permit	L	<u>]</u> 1	. 1	naterial Specific		[]	P	urchase Requisition	[] []
ŀ	Environmental Impact Sta	toment F	]	_	Samp. Schedul		l] rı		ickler File	[]
- 1		T T		Inspection	•	•	[]			[ ] [ ]
	Environmental Report	Ī	<u> </u>  -	-			LJ			Li
-1-	nvironmental Permit	L	<u> </u>		Adjustment Req		LJ			<u>, LJ</u>
	20. Other Affected indicate that t	Documents:	(NOTE: Docu	uments list has been n	ed below will	ll not b other af	e revise fected d	d by this ocuments i	ECN.) Signatures   listed below.	pelow
		mber/Revision			ment Number/			,	Document Number Re	vision
	N/A									
}	•	. •								
					•					
-;	21. Approvals		·							
		Signature,			Date			Signat	ure	Date
اِ ا	esign Authority W	G Brown Was	gent Br	our	12/15/97	Des	ign Agent	· pl	+	NA_
	Cog Eng. EA Pacqu	et	S. A. Market		12/15/97	PE			•	
	Cog. Mgr. GL Parso		rans		12/15/97	QA		/		
.   (	QA. LR Hall (FOLL)	OF PI	-00		12/15/97	Saf	ety			
		~ 1000 m	Tar.		12/15/92	Des	ign			<del>/</del>
ı	Environ. NA		3	,	NA	Env	iron.			<del>/</del>
- 1	Other NA		•		NA	Oth	er			<del></del>
	, , ,		01		<del></del>			1		<u> </u>
١,		ev MA.	XI.		12-15-9	7				<del>                                     </del>
- [	TWRS OPs				12-15-97	DEP	ARTMENT C	F ENERGY	•	
- 1	Originator GA Lesh		Tislukan		12-15-97			\	l Number that	
-		Ò	11	)	1017/1			lpproval\S		\
.	Informal Review MD		ing Gert	Zen	12/15/9)			. `	\	
		てマ			NA	<u>ADD</u>	ITIONAL			
1		1							1	·
1		1				_			1	
- 1		\	•			-			/	/

### RECORD OF REVISION

(1) Document Number HNF-1857, Rev. 1



(2) Title

Preoperational	Test POTP-007,	Cross-Site	Transfer	System	Integrated	Test

Preoperation	nal Test POTP-007, Cross-Site Transfer System	Integrated Te	st
	CHANGE CONTROL RECORD		
(3) Revision	(4) Description of Change - Replace. Add. and Delete Pages		zed for Release
(5) (2)	(4) Description of Change - Replace, Add, and Delete Pages	(5) Cog Engr.	
1 Rs	(7) Replace pages 13 and 14 of HNF-1857, Rev . 0	12/15/97	MPansone 12/15/97
	Replace pages 20 of 150, 24-43 of 150, 47-63 of 150, 68 of 150, 77-78 of 150 and 88-90 of 150 in attachment A		
	Add pages 49a, 63a, and 63b of 150 to 058- attachment of HNF-1857, Rev. 0/FCN-373	·	
		,	
		•	
			,
,			
		,	
-			
	·		
<del></del>			
			· · · · · · · · · · · · · · · · · · ·
	·		
-			
<del> </del>			
			<u> </u>

# PREOPERATIONAL TEST POTP-007, CROSS-SITE TRANSFER SYSTEM INTEGRATED TEST

G. L. Parsons

Numatec Hanford Corporation, Richland, WA 99352 U.S. Department of Energy Contract DE-AC06-96RL13200

EDT/ECN: W058-373

UC: 2030

Org Code: 8C610

Charge Code: N5847

B&R Code: EW3120071

Total Pages: 154

Key Words: Project W-058, Transfer Header, 3160, P-3125A, P-3125B, Cross-site, transfer system, slurry, Sulzer, P-102-SY, P-102-SY-02A

Abstract: This procedure tests the operability of the Project W-058 Cross-Site Transfer System booster pumps, slurry header 3160, and supernate header 3150, per the criteria given in Project W-058 Startup Test Plan, HNF-SD-W058-SUP-002.

TRADEMARK DISCLAIMER. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

Printed in the United States of America. To obtain copies of this document, contact: Document Control Services, P.O. Box 950, Mailstop H6-08, Richland WA 99352, Phone (509) 372-2420; Fax (509) 376-4989.

Christine Maleil

Release Approval

Release Approval



Release Stamp

**Approved for Public Release** 

Ant	t( )
(2)	

DEC 03 1997

### **ENGINEERING DATA TRANSMITTAL**

				- 1						•			•	
			anization)		3. From: (				on)	4. Related EDT No.:				
Dist	ribut	ion	•		Replacem			ite			N/	A ·		
					Transfer									
5. Pro	j./Pro	g./Dept./D	iv.:		6. Design / Engr.:	Authori	ity/ Design	Agent	/Cog.	7. Purcha	se Order	No.:		
W-05	8/Sta	rtup			GL Parso	ons					N/	Α		
	<del> </del>	r Remarks:		<u>'</u> I						9. Equip.	<u> </u>	<del></del>	,	
	Relea										-	P-312!	5B	
			•							10. System				
					<i>;</i>							6241-V		
11. Re	ceiver	Remarks:	11A.	Design Bas	seline Docum	ent?	[] Yes	[X]	No	12. Major			············	
		1,0,110,1	. •	, , , , , , , , , , , , , , , , , , ,	5011110 5000		[]	r		-	H-2-82		•	
										13. Permi			ion No. 4	
										is. Permi	N/		TON NO.:	
										14. Requi				
	•							•		14. Kequii	N/		•	
			·			-			<u> </u>		11/	<u>^</u>		
15. (A)				(C)	TRANSMITTED (D)	)				(F)	(G)	(H)	(1)	
Item	(B) F	)ocument/Dra	awina No	Sheet	Rev.	(8	E) Title or Des		of Data	Approval Desig-	Reason for	Origi- nator	Receiv- er	
No. (B) Document/Drawing No. No. No. Transmitted								nator	Trans-	Dispo-	Dispo-			
								<del></del>	<u> </u>	mittal	sition	sition		
1	HNF-	1857			0		operation			SQ	1	1	ŀ	
1							P-007, (					ŀ		
_						Ira	nsfer Sy egrated	ys cen			,	•		
. 3-						1110	egrateu	1626	,					
<u> </u>			·	ļ		ļ						· · ·		
·					1	<u> </u>				<u> </u>			<u> </u>	
16.	· ·	. 1571	ı	· ·			KEY							
	D or N/	gnator (F)	1. Approva		for Transmittal	1 (G)		1 1 1		Dispositio				
	1C-CM-3		2. Release		st-Review				proved proved w/co			i no/comme i w/comme		
Sec.12.	.7)		3. Informa	tion 6. Dis	t. (Receipt Ack	now. Re	quired)	3. Di	sapproved w/	comment 6	. Receipt a	cknowledg	ed	
				•	17. SI (See Approval I		RE/DISTRIBUT		uraci			•		
(G)	(H)	<del></del>	<del> </del>			8110	(G)	(H)		•			<del></del>	
Rea-	Disp.	(J) Nan	ne (K)	Signature (	(L) Date _ (M) N	MSIN	Rea-	Disp.	(J) Name	e (K) Sig	nature (l	_) Date (1)	MSIN	
son	11.54	B		144 45			son	···	ļ					
N/A	N/A	Design At 1 of Docu		N/A (FOR A	pprovals, se	ee page	·							
N/A	N/A	Design Ag	gent N/A		يال م	97								
1/2	1 .	Cog. Mgr.		^ *	Burry 12 P	3-47	7					<del></del> -		
1/2	1		i. Startup		quet June	23-47 "	-	<del></del>	<b> </b>		•		· · · · · · · · · · · · · · · · · · ·	
N/A N/A	N/A N/A	QA-HAA S	ha see	RÓGAL APPROV	547. AL 547		+		<b> </b>				<del></del>	
N/A	N/A	Env. N/A		MYTAU	<u> </u>		-	· · · · ·	<del> </del>	<u>· · · · · · · · · · · · · · · · · · · </u>		• • • • • • • • • • • • • • • • • • • •	<del></del>	
18.	,	2 11/1/	. 19.				20.		1	21. DOE A	PROVAL (	if requi	red)	
5 AV 🖝			ļ			- 1				Ctrl,	No.		,	
GA Les	hikar <i>Sustan</i>	Las 12-3		Equal D	- 12-3		GL Parsons IH VONK	M	11/4/57	[] Approve [] Approve		ante		
Signatu	re of ED		Auth		entative Date	,	Design Author		Bale	[] Disapp			•	
Original			[ fa- D	sasiuina Ora:	miration		Ca - a tu - a 4 4			i e			•	

BD-7400-172-2 (05/96) GEF097





G. L. Parsons

Numatec Hanford Corporation, Richland, WA 99352 U.S. Department of Energy Contract DE-AC06-96RL13200

EDT/ECN: 623654

UC: 2030

Org Code: 8C610 B&R Code: EW3120071 Charge Code: N58U7

R Code: EW3120071 Total Pages:/5/

Key Words: Project W-058, Transfer Header, 3160, P-3125A, P-3125B, Cross-Site, transfer system slurry, Sulzer, P-102-SY, P-102-SY-02A, POTP

Abstract: This procedure tests the operability of the Project W-058 Cross-Site Transfer System booster pumps, slurry header 3160, and supernate header 3150, per the criteria given in Project W-058 Startup Test Plan. HNF-SD-W058-SUP-002.

TRADEMARK DISCLAIMER. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

Printed in the United States of America. To obtain copies of this document, contact: Document Control Services, P.O. Box 950, Mailstop H6-08, Richland WA 99352, Phone (509) 372-2420; Fax (509) 376-4989.

etease Approval Date

DEC 03 1997 ID:

**Approved for Public Release** 

A-6400-073 (01/97) GEF321

SION NO.<u>O</u>

Author

G.A. Leshikar/J.L. Dowell Print Name/Signature

APPROVAL DESIGNATOR \_\_\_\_SO\_\_\_\_

PROCEDURE APPROVAL BY TEST REVIEW BOARD (TRB)

Jafet .	12/3/97	Carriellas	12-4-97
TRB Chair	Date	TWRS Operations	Date
TWR\$ Engineering	12/4/97 Date	m. O-m Jalan TWRS Safety	
Startup Engineer	12/3/97 Date	Van R. Hall Quality Assurance	1 <u>2/3/9</u> 7 Date
ML Parsure Project Management	<u>12-3-97</u> Date	FDNW Construction	12/3/97 Date

HNIF-2504, REV 0

ATT 1

P628

1 OF 14

### TABLE OF CONTENTS PAGE

1.0	PURPOSE	3
2.0	INFORMATION	3
	2.1 SCOPE 2.2 TERMS AND DEFINITIONS 2.3 RESPONSIBILITIES 2.4 CHANGE CONTROL 2.5 EXCEPTIONS 2.6 REFERENCES 2.7 ENVIRONMENTAL 2.8 SAFETY 2.9 RADIATION AND CONTAMINATION CONTROL 2.10 QUALITY ASSURANCE 2.11 GENERAL INFORMATION 2.12 LIMITS AND PRECAUTIONS	3 4 4 5 5 5 6 6 7 7 8
3.0	RECORDS	9
	PREREQUISITES PROCEDURE	13
	ACCEPTANCE CRITERIA	13
ATTA	CHMENTS	
	Attachment A Attachment B Attachment C Attachment D Attachment E	15-

### 1.0 PURPOSE

1.1 This procedure tests the operability of the Project W-058 Cross Site Transfer System booster pumps, slurry header 3160, and supernate header 3150.

### 2.0 INFORMATION

### 2.1 SCOPE

- The transfer system will be configured for the slurry line booster pumps to move water from a temporary reservoir located outside 6241-A Diversion Box through a loop which starts at the slurry line inside the Diversion Box, jumpers from the slurry line to the supernate line inside 6241-V Vent Station, and returns thru the supernate line. Utilizing system valves as barriers, the Diversion Box will be isolated from 241-SY-A and 241-SY-B valve pits in 200 West Area, and 6241-V Vent Station will be isolated from Lift Station 244-A in 200 East Area.
- 2.1.2 This test will demonstrate filling, venting, and draining of the transfer headers.
- 2.1.3 This procedure will demonstrate the operation of the following Cross Site Transfer System components:
  - Booster Pump P-3125A and VSD-1
  - Booster Pump P-3125B and VSD-2
- 2.1.4 The following components of the Cross Site Transfer System that would normally be utilized during an actual waste transfer, are not used in this test:
  - Water Flush System
  - Valving and interlocks at 241-SY-A valve pit (jumper not yet installed)
  - Valving and interlocks at 244-A Lift Station (jumpers not yet installed)

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST 4 OF 14 HNF-1857 PAGE

ISION NO.<u>O</u>

This procedure is governed by HNF-PRO-446 which 2.1.5 establishes the requirements for project, program, department, or division testing activities.

#### TERMS AND DEFINITIONS 2.2

2.2.1	HASP	-	Health and Safety Plan
2.2.2	M&TE	_	Measurement and Test Equipment
2.2.3	MCS	-	Monitoring and Control Station
2.2.4	MOV		Motor Operated Valve
2.2.5	ΡI	-	Pressure Indicator
2.2.6	PIC	_	Process Instrument Calibrator
2.2.7	PID	_	Proportional Integral Derivative
2.2.8	PCU	_	Process Control Unit
2.2.9	POTP	-	Pre Operational Test Procedure
2.2.10	SOV	_	Solenoid Operated Valve
2.2.11	VTPS	-	Variable Test Pressure Source
2.2.12			Technical Safety Requirements

#### RESPONSIBILITIES 2.3

- The Construction Forces craft personnel are responsible 2.3.1 for:
  - Providing assistance during the test.

#### Test Director responsiblities: 2.3.2

- Ensures the equipment found in Step 4.10 of this procedure is available.
- Safe and productive accomplishment of the tests necessary to achieve startup.
- Ensure safe working conditions and practices.
- Ensure compliance with test documents and Technical Safety Requirements documents (TSRs) during testing.
- Communicate and coordinate the tests with the Tank Farm Shift Managers.
- Ensure appropriate review/approval of any modifications to test procedures are completed prior to returning to work

- Direct line of communication and centralized point of control.
- Conducts pre-job planning meeting.
- Scheduling/rescheduling of the test as required.
- Delegates any of the above responsibilities as needed to a deputy.

#### 2.3.3 Test Engineer responsibilites:

- Conducting pre-job system walkdown.
- Recording equipment status and data per this procedure.
- Directing preoperational testing
- Providing technical support during testing.
- Providing programming support during testing.
- Forcing data in PLC program during testing.
- Recording data exceptions and other notes as required on the POTP Data Sheets.
- Review test documents to validate acceptance
- Prepare post testing documents

### 2.3.4 Operations Personnel responsibilities:

Observing testing activities for training purposes.

### CHANGE CONTROL

Test procedure administrative or editorial changes 2.4.1 required during testing may be accommodated by the Test Engineer red-lining the controlled copy of the test procedure, if such changes will not affect operating facility safety, function, or performance and will not compromise or influence test data. Requirement changes, changes to acceptance criteria, or changes to Danger, Caution, Special Precautions, or other safety or environmental instructions must be made by engineering change notice. Such changes shall not prevent the running. of another portion of the test unaffected by the change.

### 2.5 EXCEPTIONS

Exceptions to the test results will be given a sequential 2.5.1 number and recorded on Attachment E, Test Exception Log sheet. Errors in the POTP itself shall not be processed as exceptions (see Section 2.4, CHANGE CONTROL). A Test Exception Report, Attachment D, will be filled out to record and disposition each test exception.

#### REFERENCES 2.6

- The following documents were used to write or are 2.6.1 referenced in this procedure:
  - Project W-058 Startup Test Plan, WHC-SD-W058-SUP-002
  - Project W-058 Replacement of Cross Site Transfer System Functional Design Criteria, WHC-SD-W058-FDC-001
  - H-2-822400, Sheet 1,2 & 3, P&ID Legend.
  - H-2-822402, P&ID SY Valve Pits
  - H-2-822403, P&ID Diversion Box 6241-A
  - H-2-822404, P&ID Vent Station 6241-V
  - H-2-822405, P&ID Lift Station 244-A
  - H-2-822505, Electrical One-Line Diversion Box 6241-A
  - H-2-822513. Sheet 1-9, Electrical Elementary Diagrams Diversion Box 6241-A
  - H-6-14009. Electrical One Line Diagram Ventilation Station 6241-V
  - ES-058-Y40 through Y90, Logic Diagrams
  - VI 22798. Supplement 1, Electronic Pressure Transmitter, Ametek Model 88 Series
  - VI 22798, Supplement 33, Air Operated Ball Valves, Herion/Hi-Gear Inc./Hytork
  - VI 22798, Supplement 39, Ultrasonic Flowmeter, Panametrics
  - VI 22798, Supplement 40, Slurry Transfer Pump, Sulzer Bingham Pumps

### 2.7 ENVIRONMENTAL

2.7.1 Spills of hazardous materials should be reported to Environmental Reports group at 373-4942.

### 2.8 SAFETY

- Warning Operators should be aware of the possibility of coming into contact with poisonous snakes and spiders.
- 2.8.1 The following administrative procedures control work performed in this procedure:
  - $\bullet$  / Safety: HNF-PRO-074 thru -096 and HNF-PRO-100 thru 105.
  - Industrial Hygiene: HNF-PRO-110, -111, -115, -119 thru -121.
  - Tank Farm Health and Safety Plan (HASP), WHC-SD-WM-HSP-002

### 2.9 RADIATION AND CONTAMINATION CONTROL

2.9.1 For any work requiring entry into a radiation/ contamination area, comply with the facility requirements. The work covered by this procedure is performed outside of the tank farm and does not require entry into a radiation/contamination control area, except access is required to 241-SY-271 building.

### 2.10 QUALITY ASSURANCE

2.10.1 Quality Assurance shall review and approve the test procedure, the final test report and the disposition of all test exceptions. LMHC QC will witness tests performed under this POTP.

#### 2.11 GENERAL INFORMATION

- 2.11.1 All Measuring and Test Equipment (M&TE) used during performance of this procedure to collect qualitative data with the exception of timing devices shall meet the following requirements:
  - Be within its current calibration cycle as evidenced by an affixed calibration label.
  - Be capable of desired range.
  - Have an accuracy (consistent with state-of-the-art limitations) equal to or greater than the accuracy specified in the procedure.
- 2.11.2 Timing measurements shall be made with commercially available time devices.
- 2.11.3 All readings are to be taken and recorded for each location where the capability exists (i.e. local instrument, PCU, MCS).

### 2.12 LIMITS AND PRECAUTIONS

- 2.12.1 If during performance of this procedure, any of the following conditions are found, **immediately** notify the Test Engineer:
  - Any equipment malfunction which could prevent fulfillment of it's functional requirements.
  - Personnel error or procedural inadequacy which could prevent fulfillment of procedural requirements.

The Test Engineer may choose to stop work and place equipment in a safe condition based on the significance of the malfunction, error or inadequacy.

2.12.2 The Test Engineer has overall control of the testing process and change authorization for this procedure. The Test Engineer is responsible for running the test, data collection, and ensuring compliance with all requirements in this procedure.

- 2.12.3 Contact Test Director for additional instructions if changing plant conditions affect work or delays in work extend past end of shift.
- 2.12.4 If any waste is generated during performance of this instruction consult Facility/Plant/Area Hazardous Waste Coordinator for specific instructions to ensure compliance with HNF and DOE environmental standards, as applicable, for disposal.
- 2.12.5 Comply with FDNW and plant/facility specific lock and tag or over-tagging requirements, as applicable.

#### 3.0 RECORDS

3.1 This procedure as well as all completed attachments/appendices are kept as a permanent record.

### 4.0 PREREQUISITES

The following items are prerequisite actions to be performed before Interlock Testing, Sections 2.0 and 3.0 of Attachment A. Prerequisite actions may be performed in any order.

- 4.1 Perform a walkdown of the system tested by this procedure.

  Test Engineer: <u>III Induction</u>
- 4.2 Perform a pretest briefing for all personnel involved in the performance of this test.

  Test Director:
- 4.3 All personnel who will be involved with this test have provided the required signature verification information in Attachment B.

  Test Engineer: 

  4.3 All personnel who will be involved with this test have provided the required signature verification.
- 4.4 The test engineer has verified that all appropriate components within and including the test boundary have been "blue" tagged.

  Test Engineer:

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE

PAGE 10 OF 14

ISION NO. 0

4.5	The following	equipment	has	been	prepared	for	operation	in
	accordance wi	th vendor m	nanua	ıls:	·			

4.5.1	Booster	Pumps	P-3125A	and	P-3125B	and	${\tt associated}$	variable
	speed dr	rives.						:

Test Engineer

4.6 Communications between personnel in 242-S and field test personnel has been verified.

Test Director

4.7 The official copy of this POTP and all other copies that will be used during the test have been verified to be the latest revision.

Test Engineer

4.8 All open items have been evaluated and verified to not affect the

4.8 All open items have been evaluated and verified to not affect the performance of this POTP (Quality Assurance Nonconformance Reports, Construction Punch Lists, outstanding Engineering or Field Change Notices, Startup-originated Design Change Requests, Test Deficiency Reports, and Master System Punch List items).

Test Director

Test Engineer All Sesluka

The following additional items are prerequisite actions to be performed before Transfer Line Filling, Section 5.0 of Attachment A.

4.9 VERIFY process blanks/are installed on header 3150 at 241-SY-A valve pit, header 3160 at 241-SY-B valve pit, and both headers 3150 and 3160 at 244-A Lift Station.

Test Director

4.10 The HEPA filters in the transfer system vent lines at the Vent Station are NOT installed.

Test Director

The following additional items are prerequisite actions to be performed before Booster Pump P-3125A Startup Testing, Section 7.0 of Attachment A.

4.11 **VERIFY** the system flowmeter FE-3125 is installed on the slurry line pipe in the Diversion Box. (See VI 22798, Supplement #39).

Test Engineer:

4.12 VERIFY correct parameters have been programmed into the Panametrics flowmeter DF868 electronics console, per Test Engineer's direction. (See VI 22798, Supplement #39) Recorded to test logo w 12/17/97 for Test Engineer:

### 4.13 EQUIPMENT/INSTRUMENTS

- 4.13.1 Jumper #1 (connects temporary water reservoir to slurry line upstream of booster pumps). See sketch in Attachment A. Appendix A.
  - 4.13.1.1 Connector to female Hiltap coupling, 3", stainless steel
  - 4.13.1.2 Pressure indicator (local), scale range approximately
    1 to 100 psig

    Manufacturer: Ashcroft Model No. Rangauge

    Serial No. NA Calibration Date 3/19/97

    Calibration Due Date 3/19/98 Cal. code: 950-31-04-067

    MITE Control No. 0041
  - 4.13.1.3 Valve (isolation between supply pump and booster pumps)
  - 4.13.1.4 Piping/hose as required, 100 psig or better
  - 4.13.1.5 Pressure control valve or bypass regulator, 30 to 75 psi adjustment range, return system excess to water reservoir
  - 4.13.1.6 Supply pump, rated to provide approximately 140 gpm, to inlet of booster pump (pressure/head required is dependent on jumper properties, i.e. hose dia., length, component losses, etc).
  - 4.13.2 Jumper #2 (connects slurry line to supernate line at Hiltap connectors in Vent Station). See sketch in Attachment A, Appendix A.
    - 4.13.2.1 Connector to female Hiltap coupling, 3", stainless steel, rated to 1500 psig, quantity (2)

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE

CISTON NO. O	Λ	MΩ	MOTOT

	4.13.	2.2	Hose, rated to 1500 psig
4.13.	3	tempo	er #3 (connects supernate line in Diversion Box to brary water reservoir). See sketch in Attachment A, andix A.
	4.13.	3.1	Connector to female Hiltap coupling, 3", stainless steel, rated to 1500 psig
	4.13.	3.2	Pressure indicator (local), scale range approximately 0 to 600 psig  Manufacturer: Thersea Model No. DG v 95/2 - C  Serial No. 590765 Calibration Date 7/23/99  Calibration Due Date 7/23/98
	4.13.	3.3	Flow control (throttling) valve, sized to avoid cavitation during test conditions, rated to 1500 psig
	4.13.	.3.4	Pressure indicator (local), scale range approximately 0 to 300 psig  Manufacturer: Ashcroft Model No. NA  Serial No. NA Calibration Date 8/8/97  Calibration Due Date 8/8/98 Cal. Code: 950-31-04-103  Mitte Control Na: lozo
,	4.13	.3.5	Flow measuring device, range 0 to 200 gpm
	4.13	.3.6	Piping/hose as required, 100 psig or better
4.13	. 4	Two '	Variable Test Pressure Sources range 0-3000 psig.  Manufacturer: <u>Sensotee</u> Model No. <u>AG813-1000 psig</u> Serial No. <u>\$90765</u> Calibration Date <u>1/27/97</u> Calibration Due Date <u>1/27/98</u>
_		2.	Manufacturer: WIKA Model No. N/A  Serial No. BAT-PG-001 Calibration Date 11/17/987  Calibration Due Date 11/17/98 Range -30 in Hg +0 60 ps 19
4.13	.5	_	p-on Ammeter: 0-40 Ampere.  facturer: Model No

Calibration Date

\_\_\_Calibration\_Due\_Date . ATTACHMENT| PAGE39

HNF-2504, REV. 0

D. G. 3/30/98

regines

12 OF 14

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE

PAGE 13 OF 14

ISION NO. O-A

		4 12 6	Multi-meter 0-600V.
		4.13.6	
			Manufacturer: Model No. Required Serial No. Calibration Date D.G.
•			Serial No Calibration Date 0.4.
			Calibration Due Date
		4.13.7	Process Instrument Calibrator, with 4-20 mA signal
		1.2017	capability and simulating a 100 ohm (type 385) RTD. D. J. 14/17/97
			Manufacturer: Beta Model No. 110
		•	Serial No. 1776 Calibration Date 7/9/97
			Calibration Due Date 7/9/98 Cal. Social No. 817-23-01-002
		4.13.8	Bucket, with volumetric markings on side, to collect oil
			drained from booster pump bearing housings
•		4.13.9	Decade Box
	Let 1	2/17/97	Manufacturer: General Resistance Inc. Model No. DA-74-3X
5.0	PROC	EDÚŘÉ	Serial No.: 723 Calibration Date: 5/97
			Calibration Due Date: 5/98
	5.1	•	tional testing shall be performed using Attachment A of this
		procedure	
			*QC WITNESS OF CIRCUIT DRAIN CAN BE REMOVED FROM POTP-007. CIRCUIT DRAINING IS DESURED, THROUGH THE
			PERDUAL OF THE JUMPED THIS WUMPED LAWSON BY
6.0	ACCE	PIANCE CRI	ITERIA REMOVED WITHOUT DRAINING CIRCUIT. my paid 4/1/98
	<b>د</b> 1	Twincfor	headers 3150 and 3160 from the Diversion Box to the Vent
	0.1		were filled with water; water was circulated through them by
			ter pumps; and the headers were vented and drained.
A DICE VO VITTE	mr WI		IONS (LANDIZ Test Engineer Doug July
HILL POTP WH	1011/19	VERS VENTIN	6 ANDDRANING mg g Benley For K WILLOUGH 4/1/98
- 1-10 North 1911 V	セクシンドン・ナン	I TO DE DIE	TION , AULT QUALITY CONTROL F/ Glamon deal 4,1,98
e this oriter	14 WA	3 NOTVER	E4.1987 REF TE-001, -003, -004, 2005, 9 006.
., ,	•	ি	Eq. (1967)
	6.2	Booster p	oumps/P-3125A and P-3125B operated at the design flowrates
	ok	of <del>104</del> gr	om $\pm \not \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! \! $
	D.W		om $\pm (8)$ gpm, under control of system flow feedback. (Sections
	γ	9.0 and (	10.0).] TOLENANCE IS +7GPM (SEE ECN WOSE-39.
			L7 D.H
			Test Engineer Young Shihe 41
			Tolenance 15 ± 79 pm (SEE ECN WOS8-39.  Test Engineer Doing Links  MHC Quality Control PS Claused 4.1.98  MBaily Fox K WILLOUGHOY 4/1/98
			m Bailes Fox K WILLOUGHOU 4/1/98

6.3 The following interlocks operate properly:

- I-2: On high pressure shutdown operating booster pump, P-3125A or P-3125B.
- I-6: The operating booster pump, P-3125A or P-3125B will shutdown:
  - A) On high pump bearing temperature
  - B) On high motor winding temperature
  - C) On high vibration
  - D) On pump seal failure
  - E) On low oil level
- I-7: The pump will not be permitted to operate if the inlet pressure is lower than 10 psig
- I-9: Transfer pump P-102-SY-02A will not be permitted to operate if operating booster pump is shutdown
- I-10: Upstream transfer pump P-102-SY-02A will be shutdown if inlet pressure reaches 70 psig

I-14: On high discharge pressure, shutdown appropriate START ECN W-058-39 \$ operating pump

I-15: The booster pump will not be permitted to operate if the associated vent and drain valves are not closed.

I-20 (with respect to supernate line vent only); On high pressure, shutdown transfer pump P-102-SY-02A.

Test Engineer Doug Street

REF. TE-002 PJ Glomendon 4.1198

REF. TE-002 my baily fold KWILLOUGHBY 4/1/98

14 OF 14

PREOPERA REVISION NO	TIONAL TEST POTP-007, CROSS SITE TRAI HNF-1857 . <u>O</u> ATTACHMENT A	NSFER SYSTEM INTEGRATED TEST PAGE 1 OF 132
1.0	Initial Conditions / Pre-Interlock	Tests
1.1	VERIFY all system instrumentation in Test	n Appendix B is calibrated. Engineer: <u>#AL</u>
1.2	ALIGN the Instrument Air system values in accordance to the contract of the co	
1.3 D. S., 2/2/98 1.3.1 L	VERIFY system electrical circuit broading aligned in accordance with Appendix  JERIFY ALL FORCES (B3/0) ALE READVEN FORCES NOTED IN STEENS 4.16  PLACE Diversion Box Compressor SA-CI	eakers and disconnects are D.  Engineer: While To STANTING TE
1.5	the ON position.  PLACE Diversion Box Compressor SA-Chithe ON position.	MP-3101A local ON/OFF Switch in
1.6	OPEN the following valves (air suppontrol panels):	ly to the SOV's and pump seal
1) 94 D \$ 2/1/90	1.6.1 IA-V-3105A OPEN Test 1.6.2 IA-V-3106A OPEN Test 1.6.3 IA-V-3106A OPEN 7637	Engineer: La Lukan Engineer: La Lukan Engineer: La Lukan
1.7	After compressor has come up to open 125 to 150 psig), VERIFY air pressum SOV's is greater than 110 psig.	rating pressure (approximately re supplied to Diversion Box
#Adjusted P	1.7.1 PI-3108A <u>IIO</u> psig EV-3100A so that PI-310BA reads 114 psidest	Engineer: <u>All Suchefran</u>
1.8	VERIFY the air pressure supplied to 95 psig per the pressure indicators	the pump seals is greater than

1.8.1 PI-3125A1 113 psig 115 P514

1.8.2 PI-3125A2 118 psig 125 D 118

1.8.3 PI-3125B1 122 psig 14 102 P514

1.8.4 PI-3125B2 125 psig 14 103 P514

1.8.4 PI-3125B2 125 psig 14 103 P514

125 Test Engineer:

	EOPERA	TIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 2 OF 1320 ATTACHMENT A
	1.9	RECORD the instrument air flow rate to each pump seal per the flow indicators on the pump seal control panels:
		1.9.1 FI-3125A1 4.2 scfh 1.4 SCFH 1.9.2 FI-3125A2 1.8 scfh 2.2 SCFH 1.9.3 FI-3125B1 0 scfh 2.05 5 CFH 1.9.4 FI-3125B2 2.8 scfh Test Engineer: A durman
	1.10	PLACE Vent Station Compressor SA-CMP-3101B local Start Switch in the ON position.
	1.11	PLACE Vent Station Compressor SA-CMP-3101B local ON/OFF Switch in the <b>ON</b> position.
	1.12	OPEN the following valve (air supply to SOV's):
	•	1.12.1 IA-V-3101B OPEN Test Engineer: If Luchikan D. J. 21.1/98
	1.13	After compressor has come up to operating pressure (approximately 125 to 150 psig), VERIFY air pressure supplied to the Vent Station SOV's is greater than 110 psig.  1.13.1 PI-3108B 11Z psig 12 Psig 4 9 1
		1.13.1 PI-3108B 112 psig In Psig Lebukan  Test Engineer: If debukan
NOTE:	The fo	ollowing 6 steps require access to 241-SY-271 building.
	1.14	OPEN Transfer Pump 241-SY-02A Main Disconnect. Test Engineer:
	1.15	LOCK & TAG Transfer Pump 241-SY-02A Main Disconnect OPEN.  Test Engineer:
	1.16	DISCONNECT Transfer Pump 241-SY-02A leads from starter.  Test Engineer:
	1.17	INSULATE motor leads.  Test Engineer:
	1.18	REMOVE Lock & Tag from Transfer Pump 241-SY-02A Main Disconnect.  Test Engineer:

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 3 OF 132

KEVISION NO	. <u>0</u> ATTACHMENT A
1.19	CLOSE Transfer Pump 241-SY-02A Main Disconnect. Test Engineer:
1.20	OPEN VSD-1 Main Disconnect.
1.21	LOCK & TAG VSD-1 Main Disconnect OPEN.  Test Engineer:
	DISCONNECT Booster Pump (P-3125A) Motor Leads T1, T2, & T3. Tape the ends and stow within the enclosure.  Test Engineer:  ### Les Links  #### T1, T2, T3 disconnected, Were previously discounted to the enclosure of the enclosure
* Verified lea to complete 1.23	ds T1: T2, T3 disconnected. Were previously disconnected  SECTION OF THE PROPERTY OF THE PROPE
1.24	CLOSE VSD-1 Main Disconnect.  Test Engineer:   ### Hold Publication  Test Engineer: ### Automation  Test Engineer: ###################################
1.25	OPEN VSD-2 Main Disconnect.
1.26	LOCK & TAG VSD-2 Main Disconnect OPEN.  Test Engineer:
1.27	the ends and stow within the enclosure.
* D	isconnected previously per above. Test Engineer:
1.28	REMOVE Lock & Tag from VSD-2 Main Disconnect.  Test Engineer:
1.29	CLOSE VSD-2 Main Disconnect.  Test Engineer:   ### Iff Lefter

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 4 OF 132 HNF-1857

REVISION NO. 0

ATTACHMENT A

1.30 POSITION P-3125A drain valves and vent valve as follows:

FOR RETEST

D.G. 2/12/98

D.G. 2/12/98

Valve No.	Description	MCS Position	Initials
MOV-3125AA	P-3125A Drain Valve	CLOSED	LAL
MOV-3125AB	P-3125A Drain Valve	CLOSED	Hu L
MOV-3125AC	P-3125A Drain Valve	. CLOSED	104
MOV-3125AD	P-3125A Drain Valve	CLOSED	Las
MOV-3125AE	P-3125A Drain Valve	CLOSED	444
MOV-3125AF	P-3125A Drain Valve	CLOSED	Gal
MOV-3125AG	P-3125A Drain Valve	CLOSED	SUF
MOV-3125AH	P-3125A Drain Valve	CLOSED	ZaL
MOV-3125AJ	P-3125A Drain Valve	CLOSED	Sal
MOV-3125AK	P-3125A Vent Valve	CLOSED	199

Test Engineer: <u>In Lishika</u>

### 1.31 POSITION P-3125B drain valves and vent valve as follows:

Valve No.	Description	MCS Position	Initials
MOV-312ŠBA	P-3125B Drain Valve	CLOSED	202
MOV-31258B	P-3125B Drain Valve	CLOSED	201
MOV-3125BC	P-3125B Drain Valve	CLOSED	Mas
MOV-31258D	P-3125B Drain Valve	CLOSED	Staf
MOV-3125BE	P-3125B Drain Valve	CLOSED	SUL
MOV-3125BF	P-3125B Drain Valve	CLOSED	Sal
MOV-3125BG	P-3125B Drain Valve	CLOSED	LAL
MOV-3125BH	P-3125B Drain Valve	CLOSED	Las
MOV-3125BJ	P-3125B Drain Valve	CLOSED	209
MOV-3125BK	P-3125B Vent Valve	CLOSED	2aL

Test Engineer: 41 Jeshika

ATTACHMENT I PAGEYS HNF-2504, REV. 0

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 5 OF 132

REVISION NO. <u>0</u> ATTACHMENT A

1.32	VERIFY	the following on the MCS:
	1.32.1	TRANSFER mode is illuminated on MCS screen PCU-1 for P-102-SY-02A transfer pump.  Test Engineer: D. 4
	1.32.2	PAL-3100A COMPRESSOR PRESSURE LOW is illuminated in GREEN on the display for Diversion Box 6241-A.  Test Engineer:
	1.32.3	PAL-3100B COMPRESSOR PRESSURE LOW is illuminated in GREEN on the display for Vent Station 6241-V.  Test Engineer:
	1.32.4	DA-3160 ENCASEMENT LEAK DETECTION is illuminated in GREEN on the display for Diversion Box 6241-A.  Test Engineer:
	1.32.5	LDA-3150 SUMP LEAK DETECTION is illuminated in <b>GREEN</b> on the display for Diversion Box 6241-A.  Test Engineer:
	1.32.6	LDA-3161 ENCASEMENT LEAK DETECTION is illuminated in GREEN on the display for Vent Station 6241-V.  Test Engineer:
	1.32.7	LDA-3151 SUMP LEAK DETECTION is illuminated in GREEN on the display for Vent Station 6241-V.  Test Engineer:
	1.32.8	LDA-3162 ENCASEMENT LEAK DETECTION is illuminated in GREEN on the display for 244A Lift Station.  Test Engineer:
	1.32.9	Pump P-841 Status OFF is illuminated on the display for 244A Lift Station.  Test Engineer:

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF - 1857 PAGE 6 OF 132

REVISION NO. 0-A

ATTACHMENT A

Signatures Transferred from Rev. O 1918 12/16/97

2.0 Booster Pump P-3125A Interlock Test - Interlocks 2,6,7,9,10,14,15,20

Steps 2.1 through 2.24 must be completed prior to attempting to start the booster pump. THIS IS A SIMULATED START, neither the booster pump shaft nor the transfer pump shaft will rotate because the motor leads have been lifted in Section 1.0.

PRESS the OFF key on VSD-1 keypad. 2.1

VERIFY the OFF key is illuminated on VSD-1 keypad. 2.2

Test Engineer: \_\_\_\_\_\_\_

REVENIFIED FOR RETEST

- PRESS the LOCAL key on VSD-1 keypad. 2.3
- 2.4 **PRESS** the MONITOR key on VSD-1 keypad.

VERIFY the MONITOR and DRIVE READY LEDs are illuminated on VSD-1. Description of the Monitor and DRIVE READY LEDs are illuminated on VSD-1. 2:5

NOTE: The variable speed drive has a minimum frequency output of 2 Hz, corresponding to a minimum motor speed of 120 rpm, which may or may not produce enough torque to cause the pump shaft to rotate. Disconnecting the leads to the motor assures the pump shaft can not rotate. However, the VSD. being a current controlled type, will trip out if it is started without a load unless the NO MOTOR TEST MODE parameter is enabled.

PRESS the Control Speed DOWN arrow until FREQ SET equals 2 Hz. 2.6

- SET-UP VSD-1 for simulated motor operation per the following 2.7 steps.
  - 2.7.1 PRESS the PROGRAM key on VSD-1 keypad.
  - 2.7.2 **SELECT** PARAM and **PRESS** the ENTER key.
  - 2.7.3 SCROLL thru the list of drive parameters using the UP and DOWN arrows until ACCEL TIME is shown.
  - 2.7.4 PRESS the LINE key (moves cursor from upper to lower line).

PREOPERA	TIONAL TEST	F POTP-007, CROSS S HNF-1857	·	EM INTEGRATED TEST PAGE 7 OF 1	<del></del> 32
REVISION NO	) <u> </u>	ATTACHMEN	T A 💉		feve For
	2.7.5 <b>SELE</b>	CHANGED TO ECT 20 and PRESS th	ร อฟ <i>นเปลูง 19.3</i> e ENTER key. Test Engineer:	10 8 1 1	_ 2/2 _ 2/2 _ 2/2
		DLL thru the list o Narrows until DECE	-	s using the UP and	,
	2.7.7 PRES	SS the LINE key	2/,2/60		
	2.7.8 SELE	SS the LINE key. S N/A P. 9. ECT-20 and PRESS th 20	e ENTER key. Test Engineer:	Sa Leshikan	2/97 <u>f</u> — 2
		DLL thru the list o Narrows until NO M	f drive parameter:	s using the UP and	,
	2.7.10	PRESS the LINE k	ey.		
	2.7.11	SELECT YES (unde ENTER key.		ODE) and PRESS the	D. E 2/,2 —
2.8	PRESS the	MONITOR key on VSD	-1 keypad.		
2.9	PRESS the the MCS).	REMOTE key on VSD-	1 keypad (enables Test Engineer:	speed reference from Land Leohukin	om _D.& 2/ <sub>/2</sub>
.2.10	PRESS the from the M	AUTO key on VSD-1 MCS).	keypad (enables s Test Engineer:		19.5 _2//
2.11	VERIFY P-1 MCS screer		Pump DRIVE STOPP	ED is illuminated o	n De

VERIFY ENABLE ENERGIZED, REMOTE, and OFF are illuminated on MCS screen PCU-2 for Booster Pump P-3125A. 
HA FOLL

Test Engineer:

2.13 SELECT the PID MAN Button on MCS screen PCU-2 for Booster Pump P-3125A.

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 8 OF 132 HNF-1857

REVISION NO. 0

ATTACHMENT A

2.14 <b>SET</b> the Fluid FLOW (SP) value to	o O gpm on MCS screen PCU-2 for DA	$\mathcal{Y}_{\perp}$
Rooster Pumn P-3125A	Test Engineer: D (12/12/97) 2/,	2/9
	KS WILL BE FORCED IN MCS SOR	TWAN
NOTE: The following two steps are required	to override Interlock 7. If steps 🖊	
are completed out of sequence, make sure a set at 20 psig or else the booster pump wil		9
2.15 <b>CONNECT</b> a VTPS to the calibrati		>

9) 1/1/20 For refer THIS INTERLOCK WELL BE FORCED IN MCS SOFTWARE NOTE: The following two steps are required to override MCS logic (Ref. ES-058-Y74) requiring at least 50 psig discharge pressure, 10 seconds or more after booster pump start or pump FAILURE will appear on MCS screen PCU-2.

- CONNECT the second VTPS to the calibration port next to PT-3125C.
- 2.18 **SET** the VTPS to approximately 60 psig.

NOTE: Transfer Scheme 2A must be selected and initiated in order for booster pump P-3125A be started remotely.

- 2.19 **SELECT** the Transfer Sequencing **RESET** button.
  - Test Engineer:

2.20 VERIFY Alarm Table on MCS shows no valve positioning failures. Test Engineer: Ha Lulakas

SELECT the Transfer Sequencing INITIATE Button.

2.22 SELECT the Transfer Sequencing TYPE 2A transfer buttop. Test Engineer: <u>Ila Tulmki</u>

NOTE: The boxes on the MCS overview screen that denote PCU-1 thru PCU-5 indicate status of the transfer path. All boxes GRAY and paths GREEN indicates that the transfer path is ready for use. Boxes filled in RED indicates that an alarm associated with the transfer is activated (i.e.

mispositioned valve, leak detected, 200W pump shutdown, etc). The booster pump will not start unless associated alarms are either cleared or over-

ridden.

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 9 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

LEVERIFIED \_ POR ILETEST

- 2.23 IF any of the boxes on the MCS overview screen which denote PCU-1  $D_{4}$ , thru PCU-5 are highlighted in RED, DETERMINE the reason why and perform the following:
  - 2.23.1 Disposition the problem by fixing it and clearing alarm, or by overriding the alarm IF the Test Engineer determines that the problem will not affect the performance of this test. RECORD disposition on the Test Log or on a Test Exception Sheet, at the discretion of the Test Engineer. N/A this step if not performed.

2.24 **VERIFY** the boxes on the MCS overview screen which denote PCU-1 thru PCU-5 are highlighted in GRAY, unless a RED box has been determined to be acceptable per the previous step.

SEE TEST LON Test Engineer: \_ ENTMY 2/12/98 P.W.

Interlock 9:

The transfer pump will not be permitted to operate if the operating booster pump is shutdown.

- 2.25 TEST the Transfer Pump shutoff per the following steps:
  - 2.25.1 SELECT P-3125A Booster Pump START on MCS screen PCU-2.
  - 2.25.2 VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.

    Test Engineer:
  - 2.25.3 VERIFY the RUN LED is illuminated on VSD-1.
    Test Engineer: La Victoria

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 10 OF 132 REVISION NO. 0-A ATTACHMENT A Signatures Transferred from Rev. O Dan 12/16/97 2.25.4 On VSD-1 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data (information only): Motor Freq Z Hz 2.25.4.1 2.25.4.2 Motor Speed 3.3 % 119 RPM 2.25.4.3 Motor RPM BYPASS hi/low level limit alarm on P-102-SY-02A 2.25.4a Transfer Pump (resets after 5 minutes). SELECT P-102-SY-02A Transfer Pump START on MCS screen 2.25.5 PCU-1. VERIFY DRIVE RUNNING is illuminated on MCS screen 2.25.6 PCU-1. Test Engineer: <u>DG</u> **PRESS** the STOP key on VSD-1 keypad. 2.25.7 **VERIFY** the RUN LED is no longer illuminated on VSD-1. 2.25.8 Test Engineer: <u>DG</u> 2.25.8a LOWER pressure provided to PT-3125C by the VTPS to approximately 40 psig. VERIFY FAILURE and OFF are illuminated on MCS screen 2.25.9 PCU-2 for booster pump P-3125A. Test Engineer: <u>DG</u> VERIFY DRIVE STOPPED is illuminated on MCS screen 2.25.10 PCU-1 for transfer pump. Test Engineer: <u>DG</u>

. VERIFY locally that the contactor for P-102-SY-02A has

Test Engineer: <u>DG</u>

HNF-2504, REV. 0 ATTACHMENT | PAGES

OPENED.

2.25.11

	POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 11 OF 132
REVISION NO. <u>0-A</u>	ATTACHMENT A Signatures transferred from Rey, O
2.25.11a	RAISE pressure provided to PT-3125C by the VTPS to approximately 60 psig.
2.25.11b	BYPASS hi/low level limit alarm on P-102-SY-02A Transfer Pump (resets after 5 minutes).
2.25.12	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
2.25.13	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
2.25.14	VERIFY the RUN LED is illuminated on VSD-1.  Test Engineer:
2.25.15	SELECT P-102-SY-02A Transfer Pump START on MCS screen PCU-1.
2.25.16	VERIFY DRIVE RUNNING is illuminated on MCS screen PCU-1.  Test Engineer: D6
2.25.17	PRESS P-3125A Booster Pump STOP on MCS screen PCU-2.
2.25.18	VERIFY the RUN LED is no longer illuminated on VSD-1. Test Engineer:
2.25.19	VERIFY ENERGIZE ENABLED and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A.  Test Engineer: DG
2.25.20	VERIFY DRIVE STOPPED is illuminated on MCS screen PCU-1 for transfer pump.  Test Engineer: D6
2.25.21	VERIFY locally that the contactor for P-102-SY-02A has OPENED.  Test Engineer:
2.25.22	DISCONNECT VTPS's from PT-3125A and PT-3125C.

PREOPERATE REVISION NO		POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 12 OF 132 ATTACHMENT A
	2.25.23	INSTALL software jumper (or "force" bit) to disable Interlocks 7 and 10 (booster pump inlet pressure)  Test Engineer:
	2.25.24	INSTALL software jumper (or "force" bit) to disable minimum discharge pressure requirement ("booster pump is running" in MCS logic, Ref. ES-058-Y74)  Test Engineer:
Interlock 6	Tempe	operating booster pump will shut down on High Bearing erature, High Motor Winding Temperature, High Vibration, Seal Failure, and Low Oil Level.
High Bearing	g Temperatur	THE TSH-3125A1 FILEEZE -320 -780 F COMPANIE
2.26	TEST TSH-31	25A1 per the following steps: (1) 20 0
NOTE:	Measuring [	Due 6/13 Device is a three-wire RTD  CALD 6/13 PTO AT PUMP SE
	2.26.1	CONNECT the temperature calibrator to PCU-2B-TB2-03. PCU-2B-TB2-I3, and PCU-2B-TB2-R3.
then I		t instrument only accepts a two lead RTD connection 33 and PCU-2B-TB2-R3 should be connected together as one rument.
	2.26.2	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
	2.26.3	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
	2.26.4	VERIFY the RUN LED is illuminated on VSD-1.  Test Engineer:

	RATIONAL TEST NO. <u>0-A</u>	POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 13 OF 132 ATTACHMENT A
-	2.26.5	On VSD-1 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data (information only):
		2.26.6 Motor Freq       2       Hz         2.26.7 Motor Speed       33       %         2.26.8 Motor RPM       1/9       RPM
	2.26.9	Step deleted.
	2.26.10	Step deleted. (134.4) $R_{\odot}$
·	2.26.11	Step deleted. $TRIPPCO BT 1910F (134,4)R$ SET the temperature (RTD) simulator to 190°F. (133.9 $R$ )
	2.26.12	VERIFY at the MCS that TSH-3125A1 alarms.  Test Engineer:  TRIPER AT 201°F (136.532)
4	2.26.13	TRIPPED AT $201^{\circ}$ F (136.5 JL) SET the temperature (RTD) simulator to $200^{\circ}$ F. (136 JL)
	2.26.14	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A.  Test Engineer:
·	2.26.15	VERIFY the RUN LED is no longer illuminated on VSD-1.  Test Engineer:
	2.26.16	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer:
	2.26.17	PCU-2B-TB2-03, PCU-2B-TB2-I3, and PCU-2B-TB2-R3. 9.9 13/6/1)
	2.26.18	RECONNECT wire numbers TE3125A1-A, TE3125A1-B, and TE3125A1-C to the correct terminal points.
	2.26.19 .	VERIFY the wires are reconnected properly.

PREOPERATIONAL TE	ST POTP-007, CROSS SITE TRANSFER S HNF-1857 ATTACHMENT A	SYSTEM INTEGRATED TEST PAGE 14 OF 132  MCS Pyroners 21
High Bearing Tempera	ture TSH-3125A2	BIENT 57 (58 OF) CONPA
2.27 TEST TSF	FA -3125A2 per the following steps:	EEZE -10)-11 OF SCALIBR PYROM
NOTE: Measurin	g Device is a three-wire RTD	817-79-09 C410 6/17/98
2.27.1	CONNECT the temperature calibred PCU-2B-TB2-I4, and PCU-2B-TB2-	RTD AT なんぽろ rator to <del>PCU-2B-IB2-04。</del> B4.
NOTE: If this then PCU-2B-TB lead to the in	test instrument only accepts a two 2-04 and PCU-2B-TB2-R4 should be c strument.	o lead RTD connection connected together as one
2.27.2	SELECT P-3125A Booster Pump ST	ART on MCS screen PCU-2.
2.27.3	<b>VERIFY</b> P-3125A Booster Pump ST illuminated on MCS screen PCU- Test Engine	2.
2.27.4	Step deleted.	
2.27.5	Step deleted.	(124 E B)
2.27.6	TRIPPES AT 1 SET the temperature (RTD) simu	1ator to 190°F. (1334)
2.27.7	VERIFY at the MCS that TSH-312	5A2 alarms.
2.27.8	TRIPPED AT ZOI F (1 SET the temperature (RTD) simu	136.5_12) lator to 200°F. (136JC)
2.27.9	<b>VERIFY</b> STATUS UNKNOWN and OFF a screen PCU-2 for booster pump I Test Engine	P-3125A. O.
2.27.10	VERIFY P-102-SY-02A shut down.	(0:7/3 and 0:7/4, PCU1)
2.27.11	DISCONNECT the temperature call PCU-2B-TB2-04, PCU-2B-TB2-I4,	ibrator from アナル ロファクローク and PCU-2B-TB2-R4: ロルノル
2.27.12	RECONNECT wire numbers 7E3125A2 TE3125A2 C to the correct term	<del>2-A, TE3125A2-B, an</del> d
2.27.13 NF-2504. REV. 0 ATTA	VERIFY the wires are reconnected ACHMENT   PAGESS Test Engineer	ed properly. er:

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 15 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

High Motor Winding Temperature TSH-3125A.

2.28 TEST TSH-3125A per the following steps:

NOTE: Temperature sensor is a factory set, normally open temperature switch set to close at 175  $^{\circ}F$ .

	2.28.1	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
	2.28.2	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
	2.28.3	Step deleted.
	2.28.4	Step deleted.
	2.28.5	LIFT wire_TSH-3125A-1 from pump skid junction box. where
	2.28.6	VERIFY at the MCS that TAH-3125A alarms.  Test Engineer:
	2.28.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A.  Test Engineer:
	2.28.8	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer:
•	2.28.9	RE-LAND wire TSH-3125A-1 on pump skid junction box.
	2.28.10	VERIFY TAH-3125A alarm clears at MCS.  Test Engineer: 9.9.

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 16 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

### High Vibration VSH-3125A1

2.29	TEST	VSH-3125A1	per	the	following	steps:
------	------	------------	-----	-----	-----------	--------

L	.5 1 <b>231 1</b> 311 03	izoni per une rorrowing sueps.
I	2.29.1 <del>X</del> 3-21-98	At the pump skid, in the junction box for the 24 volt signals, <b>DISCONNECT</b> wire PS2(+) and connect it to the positive lead of the PIC.
•	2.29.2 * 3-31-98	At the pump skid, in the junction box for the 24 volt signals, <b>DISCONNECT</b> wire VT-3125A1(-) and connect it to the negative lead of the PIC.
	2.29.3	SET the PIC to 4 mA.
·	2.29.4	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
	2.29.5	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2. Test Engineer:
	2.29.6	Step deleted.
l .	2.29.7	Step deleted.  TRIPPED AT ,31"/SEC (819nA)
	2.29.8	SET the PIC to 8.8 mA corresponding to a vibration of 0.30 in/sec $\pm$ 0.05 in/sec.
	2.29.9	VERIFY at the MCS that VSH-3125A1 alarms.  Test Engineer:
<u>.</u>	2.29.10	Tripped at .60 $\text{m/sec}$ SET the PIC to 13.6 mA corresponding to a vibration of 0.60 in/sec $\pm$ 0.05 in/sec.
	2.29.11	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A.  Test Engineer:
1	2.29.12	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)
	2.29.13	DISCONNECT the PIC.
<del>}</del> 3 HNF-2504, REV	C 2.29.14	RECONNECT wire numbers PS2(+) and VT-3125A1(-) to the correct terminal points.

30 OF 150

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 17 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

2.29.15 RAP on the bearing housing adjacent to VE/VT-3125A1 Frences and VERIFY output fluctuates for VI-3125A1 on MCS screen for booster pump P-3125A.

Test Engineer: Delta 2/12/98

### High Vibration VSH-3125A2

2.30 TEST VSH-3125A2 per the following steps:

X 2.30.1 3/31/98	At the pump skid, in the junction box for the 24 volt signals, <b>DISCONNECT</b> wire PS2(+) and connect it to the positive lead of the PIC.
2.30.2	At the pump skid, in the junction box for the 24 volt signals, DISCONNECT wire VT-3125A2(-) and connect it to the negative lead of the PIC.
2.30.3	SET the PIC to 4 mA.
2.30.4	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
2.30.5	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
2.30.6	Step deleted.
2.30.7	Step deleted.
2.30.8	SET the PIC to 8.8 mA corresponding to a vibration of 0.30 in/sec $\pm$ 0.05 in/sec.
2.30.9	VERIFY at the MCS that VSH-3125A2 alarms. Test Engineer:
2.30.10	SET the PIC to 13.6 mA corresponding to a vibration of 0.60 in/sec $\pm$ 0.05 in/sec.
2.30.11	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A.  Test Engineer:

REVISION N	O. <u>O-A</u>	HNF-1857 PAGE 18 OF 132 ATTACHMENT A
	2.30.12	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer:
	2.30.13	DISCONNECT the PIC.
3/3//0	2.30.14 98	RECONNECT wire numbers PS2(+) and VT-3125A2(-) to the correct terminal points.
	2.30.15	, ,
Low Oil Le	vel LAL-3125	<b>A</b> 1
2.31	TEST LAL-31	125A1 per the following steps:
•	2.31.1	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
	2.31.2	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer: 9.9.2/12/98
	2.31.2	illuminated on MCS screen PCU-2.
·		illuminated on MCS screen PCU-2.  Test Engineer: $9.9.2 \frac{12/98}{12}$
	2.31.3	illuminated on MCS screen PCU-2. Test Engineer: $9.99.21/98$ Step deleted.
	2.31.3 2.31.4	illuminated on MCS screen PCU-2. Test Engineer:  Step deleted.  Step deleted.  DRAIN oil from bearing housing A1 into a measurable container until LAL-3125A1 alarms at MCS, THEN
	2.31.3 2.31.4 2.31.5	illuminated on MCS screen PCU-2. Test Engineer:  Step deleted.  Step deleted.  DRAIN oil from bearing housing A1 into a measurable container until LAL-3125A1 alarms at MCS, THEN IMMEDIATELY REPLACE drain plug.  MEASURE and RECORD the amount of oil drained.  20 MCgallons

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 19 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

REVISION NO	J. <u>U-A</u>	ATTACHMENT A
	• <del>2.31.7b</del>	MEASURE and RECORD the total amount of oil drained. 9.91.
	2.31.8	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1) Test Engineer: <u>り. メ. 2/12/98</u>
	2.31.9	REFILL bearing housing Al with oil per manufacturer's instructions.  Test Engineer: D. J. 2/12/98
	2.31.10	Step deleted.
Low Oil Lev	/el LAL-3125/	A2
2.32	TEST LAL-3	125A2 per the following steps:
	2.32.1	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
	2.32.2	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer: D. J. 198
•	2.32.3	Step deleted.
	2.32.4	Step deleted.
	2.32.5	DRAIN oil from bearing housing A2 into a measurable container until LAL-3125A2 alarms at MCS, THEN IMMEDIATELY REPLACE drain plug.
	2.32.6	MEASURE and RECORD the amount of oil drained.  255 gallons $mL$ . $\theta H. \frac{2}{2} \frac{1}{12} \frac{1}{98}$ Test Engineer: $\frac{9 \cdot 9}{2} \frac{2}{12} \frac{1}{98}$

-2.32.7a DRAIN remaining oil from bearing housing Al. 8.9. 2/n/98

screen PCU-2 for booster pump P-3125A.

VERIFY STATUS UNKNOWN and OFF are illuminated on MCS

Test Engineer: 9.

2.32.7

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 20 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

		<del>2.32.7b</del>	MEASURE and RECORD the total amount of oil drained.  ———————————————————————————————————
			<del>Test Engineer:</del>
		2.32.8	Step deleted.
·		2.32.9	REFILL bearing housing A2 with oil per manufacturer's instructions.  Test Engineer: $\frac{\mathcal{P} \cdot \mathcal{H}}{\mathcal{P} \cdot \mathcal{L}/2/9}$
		2.32.10	Step deleted.
PU	MP SEAL F	AILURE FAH-	3125A1
	2.33	TEST FAH-3	125A1 per the following steps:
		2.33.1	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
		2.33.2	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:   ### Test Engineer: T
		2.33.3	Step deleted.
		2.33.4	Step deleted.
		2.33.5	LIFT LEAD from PCU-ZA-TB3-36,  PLACE a jumper between PCU-2A-TB3-36 and PCU-2A-TB3-37. 291/16/97
		2.33.6	VERIFY at the MCS that FAH-3125A1 alarms.  Test Engineer:
		2.33.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A  Test Engineer:
		2.33.8	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer:
		2.33.9	Reconvect LEAD to PCU-ZA-TB3-36.  REMOVE the jumper from between PCU-ZA-TB3-36 and PCU-ZA-TB3-37. Lal 12/16/97
			1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 - 1 -

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 21 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

2.33.10 VERIFY the jumper is removed.

Test Engineer: \_

### PUMP SEAL FAILURE FAH-3125A2

2.34	TEST FAH-31	25A2 per the following steps:
	2.34.1	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
	2.34.2	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:  ##################################
	2.34.3	Step deleted.
	2.34.4	Step deleted.
	2.34.5	PLACE a jumper between PCU-2A-TB3-38 and PCU-2A-TB3-39. Held 12/16/97
	2.34.6	VERIFY at the MCS that FAH-3125A2 alarms.  Test Engineer: 494
	2.34.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A.  Test Engineer:
	2.34.8	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer:
	2.34.9	Reconnect wire to PCU-ZA-TB3-38,  -REMOVE the jumper from between PCU-2A-TB3-38 and -PCU-2A-TB3-39. Mil 12/16/97
	2.34.10	VERIFY the jumper is removed.  Test Engineer:

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 22 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

#### PUMP SEAL FAILURE PAL-3125A1

2.35 TEST PAL-3125A1 per the following steps	2.35	TEST	PAL:	-3125A1	per	the	fol	lowina	steps	:
--	------	------	------	---------	-----	-----	-----	--------	-------	---

2.35.2	VERIFY P-3125A Booster Pump START I	ENERGIZED and ON are
	illuminated on MCS screen PCU-2.	Say 12/16/97
.*	Test Engineer	DUI.

2.35.3	CT	deleted.
7 35 3	· > ( 😝 t)	ne rei en
2.00.0	7,000	acicca.

- 2.35.4 Step deleted.
- 2.35.5 LIFT the lead from PCU-2A-TB3-66.
- 2.35.6 **VERIFY** at the MCS that PAL-3125A1 alarms. Test Engineer:
- 2.35.8 VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1) Test Engineer:  $\mathcal{L}\mathcal{UL}$
- 2.35.9 **RECONNECT** the lead to PCU-2A-TB3-66.
- 2.35.10 **VERIFY** the wires are reconnected properly. Test Engineer:

#### PUMP SEAL FAILURE PAL-3125A2

2.	36	TEST	PAL-3125A2	per	the	fol	lowing	steps:
----	----	------	------------	-----	-----	-----	--------	--------

- 2.36.1 SELECT P-3125A Booster Pump START on MCS screen PCU-2.
- 2.36.2 VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.

  Test Engineer:

2.36.3 Step deleted.

HNF-2504, REV. 0 ATTACHMENT / PAGE

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF - 1857 PAGE 23 OF 132 REVISION NO. 0-A ATTACHMENT A 2.36.4 Step deleted. 2.36.5 LIFT the lead from PCU-2A-TB3-58. 2.36.6 VERIFY at the MCS that PAL-3125A2 alarms. Test Engineer: \_ 2.36.7 VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A. Test Engineer: 2.36.8 VERIFY P-102-SY-02A shut down. (0:7/3 and 0\$7/4, PCU1) Test Engineer: \_\_\_ 2.36.9 **RECONNECT** the lead to PCU-2A-TB3-58. VERIFY the wires are reconnected properly. 2.36.10 Test Engineer: \_\_\_\_\_ Interlock 2: On high pressure, shutdown operating booster pump, P-3125A or P-3125B. PAH-3168 2.37 TEST Interlock 2 for P-3125A per the following steps: SELECT P-3125A Booster Pump START on MCS screen PCU-2. 2.37.1 VERIFY P-3125A Booster Pump START ENERGIZED and ON are 2.37.2 illuminated on MCS screen PCU-2. Test Engineer: \_ CLOSE valve V-3168. 2.37.3 Test Engineer: \_ 2.37.4 CONNECT VTPS to PT-3168 and increase pressure until PI-3168 reads 12 psig at the MCS. **VERIFY** at the MCS that PAH-3168 Alarms. $_{f Q}$ 2.37.5 Test Engineer: \_\_\_\_

	PREOPERATE REVISION NO		POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 24 OF 132 ATTACHMENT A
		2.37.6	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A.  Test Engineer:
		2.37.7	DISCONNECT the VTPS from PT-3168.
	·	2.37.8	OPEN valve V-3168.  Test Engineer:
	Interlock 10	•	eam Transfer Pump P-102-SY-02A will be shutdown if pressure reaches 70 psig.
	Interlock 7:		ooster pump will not be permitted to operate if the pressure is lower than 10 psig.
	PAH-3125A		
	2.38	TEST PAH-31	25A per the following steps:
		2.38.1	CONNECT VTPS to calibration port near PT-3125A and increase pressure until PI-3125A reads 8 psig at the MCS.
		2.38.1a	CONNECT a VTPS to calibration port near PT-3125C and set pressure to approximately 60 psig.
1		2.38.1b	REMOVE software jumper or forced bit disabling Interlocks 7 and 10 (booster pump inlet pressure).
		2.38.1c	REMOVE software jumper or forced bit disabling minimum discharge pressure requirement ("booster pump is running" in MCS logic, Ref. ES-058-Y74).
		2.38.2	SELECT booster pump P-3125A START at the MCS.
		2.38.3 5	VERIFY booster pump P-3125A STOPS after approximately 5 seconds.  Test Engineer: DG
l		2.38.4	From Rev. O Jax 11/97 INCREASE pressure using VTPS until PI-3125A reads 12 psig at the MCS.

PREOPE	RATIONAL TEST	POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 25 OF 132
REVISION	NO. <u>0-A</u>	ATTACHMENT A
	<u></u>	Signatures transferred from Rev. 2
	2.38.5	SELECT P-3125A Booster Pump START on MCS screen PCU-2.
	2.38.6	VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer: DG
,	2.38.6b	BYPASS hi/low level limit alarm on P-102-SY-02A Transfer Pump (resets after 5 minutes).
	2.38.7	SELECT P-102-SY-02A Transfer Pump START on MCS screen PCU-1.
	2.38.8	VERIFY DRIVE RUNNING is illuminated on MCS screen PCU-1.  Test Engineer:
	2.38.9	<pre>INCREASE pressure, using VTPS connected to PT-3125A, until PI-3125A reads 72 psig at the MCS.</pre>
	2.38.10	VERIFY at the MCS that PAH-3125A alarms.  Test Engineer:
	2.38.11	Step deleted.
	2.38.12	VERIFY DRIVE STOPPED is illuminated on MCS screen PCU-1 for transfer pump.  Test Engineer: DG

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 26 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

Signatures transferred from Rev. O

Interlock 14:

On High discharge pressure, shutdown appropriate operating pump.

PAH-3125C

2 30	TFST	PAH_31250	ner	the	following	stens.
۷.۵۶	1521	LAU-2172C	per	ule	TOTTOWING	steps.

- 2.39.1 SET the VTPS that is currently connected to PT-3125A to a pressure between 12 psig and 68 psig.
- 2.39.2 Step deleted.
- 2.39.3 SELECT P-3125A Booster Pump START on MCS screen PCU-2.
- 2.39.4 VERIFY P-3125A Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.

  Test Engineer: DG
- 2.39.4b BYPASS hi/low level limit alarm on P-102-SY-02A Transfer Pump (resets after 5 minutes).
- 2.39.5 SELECT P-102-SY-02A Transfer Pump START on MCS screen PCU-1.
- 2.39.6 **VERIFY** DRIVE RUNNING is illuminated on MCS screen PCU-1.

  Test Engineer: DG
- 2.39.7 **INCREASE** pressure, using VTPS connected to PT-3125C, until PI-3125C reads 1275 psig at the MCS.
- 2.39.9 **VERIFY** STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125A.

  Test Engineer:
- 2.39.10 **VERIFY** DRIVE STOPPED is illuminated on MCS screen PCU-1 for transfer pump.

  Test Engineer:

2.39.11 **DISCONNECT** the second VTPS from PT-3125C.

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 27 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

Signatures transferred from Revio gaf 17/16/97

2.39.12

OPEN valve V-3125C.

Test Engineer: \_\_\_DG

Interlock 15:

The booster pump will not be permitted to operate if the associated bypass work and associated bypass, vent, and drain valves are not closed. RETES > @\_

2.40 TEST Interlock 15 for P-3125A per the following steps:

2.40.1 **OPEN** SOV-3163.

2.40.2 **SELECT** booster pump P-3125A START at the MCS.

VERIFY booster pump P-3125A does NOT start. 12/15/97 2.40.3

D. G 2/1/98

2.40.4 CLOSE SOV-3163.

2.40.5 OPEN each P-3125A motor operated drain valve and vent

valve one at a time from the MCS, VERIFY STATUS UNKNOWN appears on MCS screen for P-3125A, attempt to START P-3125A from the MCS, VERIFY P-3125A does NOT

START, and THEN CLOSE the associated valve.

Valve No.	Description	MCS Position	Pump DID NOT Start
MOV-3125AA	P-3125A Drain Valve	OPEN	DG 12/15/97
MOV-3125AB	P-3125A Drain Valve	OPEN .	DG
MOV-3125AC	P-3125A Drain Valve	OPEN	DG
MOV-3125AD	P-3125A Drain Valve	OPEN	DĠ
MOV-3125AE	P-3125A Drain Valve	OPEN	DG
MOV-3125AF	P-3125A Drain Valve	OPEN	DG
MOV-3125AG	P-3125A Drain Valve	OPEN	DG
MOV-3125AH	P-3125A Drain Valve	OPEN	DĠ
MOV-3125AJ	P-3125A Drain Valve	OPEN	DĠ
MOV-3125AK	P-3125A Vent Valve	OPEN	DG

Test Engineer:

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 28 OF 132

REVISION NO. <u>0-A</u>

HNF-2504, REV. 0 ATTACHMENT | PAGELO

ATTACHMENT A

P-3125A i	nterlock test	ing complete
2.4	1 TAKE VSD-1	out of NO MOTOR TEST MODE per the following steps.
	2.41.1	PRESS the PROGRAM key on VSD-1 keypad.
	2.41.2	SELECT PARAM and PRESS the ENTER key.
	2.41.3	SCROLL thru the list of drive parameters using the U and DOWN arrows until NO MOTOR TEST MODE is shown.
	2.41.4	PRESS the LINE key.
	2.41.5	SELECT NO (under NO MOTOR TEST MODE) and PRESS the ENTER key.  Test Engineer:
	2.41.6	PRESS the MONITOR key on VSD-1 keypad.
,	2.41.7	VERIFY the MONITOR and DRIVE READY LEDs are illuminated on VSD-1.  Test Engineer:
2.4	2 DISCONNECT	the VTPS from calibration port near PT-3125A.
2.4	3 OPEN valve ≶ignat	V-3125A.  we transferred Test Engineer: <u>Igl</u> from Rev. o  sket 12/16/97
Transfer	Pump P-102-SY	-02A Interlock 20
Inte	erlock 20: On	high pressure, shutdown P-102-SY-02A.
PAH	-3185	
NOTE: Trai	nsfer Scheme	1 must be selected and initiated to test Interlock 20.
2.4	4 <b>SELECT</b> the	Transfer Sequencing RESET button. Test Engineer:
2.4	5 <b>VERIFY</b> Ala	rm Table on MCS shows no valve positioning failures.  Test Engineer:

VERIFIED FOR

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 28a OF 132 REVISION NO. 0-A ATTACHMENT A

2.46	SELECT the Transfer Sequencing INITIATE Button.	-
2.47	SELECT the Transfer Sequencing TYPE 1 transfer button. Test Engineer: 少し.	
2.48	IF any of the boxes on the MCS overview screen which denote thru PCU-5 are highlighted in RED, <b>DETERMINE</b> the reason why perform the following:	
•	2.48.1 Disposition the problem by fixing it and clears alarm, or by overriding the alarm IF the Test Edetermines that the problem will not affect the performance of this test. RECORD disposition of Test Log or on a Test Exception Sheet, at the discretion of the Test Engineer. N/A this step performed.  Test Engineer:	Engineer e on the
2.49		
2.50	SELECT P-102-SY-02A Transfer Pump START on MCS screen PCU-1	D
   <del>- 2.51</del>	VERIFY DRIVE RUNNING is illuminated on MCS screen PCU-1.	
5Ec	7857 LOG ENTRY 12/16/98 Engineer:	
2.52	CONNECT VTPS to PT-3185 and increase pressure until PI-3185 12 psig at the MCS.	5 reads
2.53	VERIFY at the MCS that PAH-3185 Alarms.  Test Engineer:	
2.54	P-102-SY-02A SHUTDOWN (0:7/3 AND 0:7/4) PC	.0-1 5
	DT 0405	
2.55	DISCONNECT the VTPS from calibration port near PT-3185.	

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 29 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

Signatures transferred from Rev. D

3.0 Booster Pump P-3125B Interlock Test - Interlocks 2,6,7,9,10,14,15

Steps 3.1 through 3.24 must be completed prior to attempting to start the booster pump. THIS IS A SIMULATED START, neither the booster pump shaft nor the transfer pump shaft will rotate because the motor leads have been lifted in Section 1.0.

3.1 PRESS the OFF key on VSD-2 keypad.

FOR FOR REST

3.2 **VERIFY** the OFF key is illuminated on VSD-2 keypad. (2/12/97 Test Engineer:

D.S. 2/12/98

- 3.3 PRESS the LOCAL key on VSD-2 keypad.
- 3.4 PRESS the MONITOR key on VSD-2 keypad.
- 3.5 **VERIFY** the MONITOR and DRIVE READY LEDs are illuminated on VSD-2.

NOTE: The variable speed drive has a minimum frequency output of 2 Hz, corresponding to a minimum motor speed of 120 rpm, which may or may not produce enough torque to cause the pump shaft to rotate. Disconnecting the leads to the motor assures the pump shaft can not rotate. However, the VSD, being a current controlled type, will trip out if it is started without a load unless the NO MOTOR TEST MODE parameter is enabled.

- 3.6 PRESS the Control Speed DOWN arrow until FREQ SET equals 2 Hz.

  Test Engineer:  $\mathcal{A}\mathcal{A}\mathcal{L}$
- 3.7 **SET-UP** VSD-2 for simulated motor operation per the following steps.
  - $3.7.1\ \text{PRESS}$  the PROGRAM key on VSD-2 keypad.
  - 3.7.2 **SELECT** PARAM and **PRESS** the ENTER key.
  - 3.7.3 **SCROLL** thru the list of drive parameters using the UP and DOWN arrows until ACCEL TIME is shown.
  - 3.7.4 PRESS the LINE key (moves cursor from upper to lower line).

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 30 OF 132

REVISION NO.

ATTACHMENT A

REVENTING

JII 110	FOR
	3.7.5 SELECT 20 and PRESS the ENTER key.  Test Engineer:   [2] 12/12/97 9.96
	3.7.6 <b>SCROLL</b> thru the list of drive parameters using the UP and DOWN arrows until DECEL TIME is shown.
	3.7.7 PRESS the LINE key.
	3.7.8 SELECT 20 and PRESS the ENTER key.  Test Engineer:   Test Engineer: 2/12/2
	3.7.9 <b>SCROLL</b> thru the list of drive parameters using the UP and DOWN arrows until NO MOTOR TEST MODE is shown.
	3.7.10 PRESS the LINE key.
	3.7.11 SELECT YES (under NO MOTOR TEST MODE) and PRESS the ENTER key.  Test Engineer:
3.8	PRESS the MONITOR key on VSD-2 keypad.
3.9	PRESS the REMOTE key on VSD-2 keypad (enables speed reference from the MCS).  Test Engineer:     Maintain   Ma
3.10	PRESS the AUTO key on VSD-2 keypad (enables start/stop control from the MCS).  Test Engineer:     D. St.   Zalan   Zal
3.11	VERIFY P-102-SY-02A Transfer Pump DRIVE STOPPED is illuminated on MCS screen PCU-1.  Test Engineer:     MCS   MCS
3.12	VERIFY ENABLE ENERGIZED, REMOTE, and OFF are illuminated on MCS screen PCU-2 for Booster Pump P-3125B.  Test Engineer: La dusque a 2/p/
3.13	SELECT the PID Manual Button on MCS screen PCU-2 for Booster Pump

P-3125B.

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 31 OF 132

REVISION NO. 0

ATTACHMENT A

ILEVERI)
3.14 SET the Fluid FLOW (SP) value to 0 gpm on MCS screen PCU-2 for portion of the Booster Pump P-3125B.  NOTE: FOR RETEST THESE INTERCOCKS WILL BE FORCED IN THE SOFTWARE TO ALL COW STORY OF LOW OIL LEVEL SENSON  NOTE: The following two steps are required to override Interlock 7. If steps are completed out of sequence, make sure a VTPS is connected to PT-3125B and set at 20 psig or else the booster pump will not start.
3.15 CONNECT a VTPS to the calibration port next to PT-3125B.
3.16 SET the VTPS to approximately 20 psig.
NOTE: The following two steps are required to override MCS logic (Ref. ES-058-Y74) requiring at least 50 psig discharge pressure, 10 seconds or more after booster pump start or pump FAILURE will appear on MCS screen PCU-2.
3.17 <b>CONNECT</b> the second VTPS to the calibration port next to PT-3125D.
3.18 SET the VTPS to approximately 60 psig.
NOTE: Transfer Scheme 2B must be selected and initiated in order for booster pump P-3125B be started remotely.
3.19 SELECT the Transfer Sequencing RESET button.  Test Engineer:
3.20 <b>VERIFY</b> Alarm Table on MCS shows no valve positioning failures. アリデ Test Engineer:
3.21 SELECT the Transfer Sequencing INITIATE Button.

NOTE: The boxes on the MCS overview screen that denote PCU-1 thru PCU-5 indicate status of the transfer path. All boxes GRAY and paths GREEN indicates that the transfer path is ready for use. Boxes filled in RED indicates that an alarm associated with the transfer is activated (i.e. mispositioned valve, leak detected, etc). The booster pump will not start unless associated alarms are either cleared or over-ridden.

3.22 SELECT the Transfer Sequencing TYPE 2B transfer button n

Test Engineer: \_\_\_\_

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 32 OF 132

REVISION NO.	. 0	ATTACHMENT A
3.23	•	he boxes on the MCS overview screen which denote PCU-1 Reviate highlighted in RED, DETERMINE the reason why and following:
	3.23.1	Disposition the problem by fixing it and clearing alarm, or by overriding the alarm IF the Test Engineer determines that the problem will not affect the performance of this test. RECORD disposition on the Test Log or on a Test Exception Sheet, at the discretion of the Test Engineer. N/A this step if not performed.  Test Engineer:
3.24	thru PCU-5	boxes on the MCS overview screen which denote PCU-1 are highlighted in GRAY, unless a RED box has been to be acceptable per the previous step.  Test Engineer:  SEE TEST LOG ESTRY Zlielgs  ransfer pump will not be permitted to operate if the
Interlock 9		ransfer pump will not be permitted to operate if the ting booster pump is shutdown.
3.25	TEST the Tra	ansfer Pump shutoff per the following steps:
	3.25.1	SELECT P-3125B Booster Pump START on MCS screen PCU-2.
	3.25.2	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
	3.25.3	VERIFY the RUN LED is illuminated on VSD-21.  Test Engineer:

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 33 OF 132 HNF-1857 REVISION NO. 0-A ATTACHMENT A Signatures transferred from Rev. O 12/16/97 On VSD-2 keypad, use the LINE key and Programming and 3.25.4 Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as RECORD the following data (information required. only): Motor Freq O Hz 3.25.4.1 3.25.4.2 Motor Speed \_\_\_ Motor RPM 3.25.4.3 BYPASS hi/low level limit alarm on P-102-SY-02A 3.25.4aTransfer Pump (resets after 5 minutes). SELECT P-102-SY-02A Transfer Pump START on MCS screen 3.25.5 PCU-1. VERIFY DRIVE RUNNING is illuminated on MCS screen 3.25.6 PCU-1. Test Engineer: D6 PRESS the STOP key on VSD-2 keypad. 3.25.7 Test Engineer: \_\_\_\_\_DG VERIFY the RUN LED is no longer illuminated on VSD-2. 3.25.8 Test Engineer: DG LOWER pressure provided to PT-3125D by the VTPS to 3.25.8a approximately 40 psig. VERIFY FAILURE and OFF are illuminated on MCS screen 3.25.9 PCU-2 for booster pump P-3125B. Test Engineer: <u>bG</u> VERIFY DRIVE STOPPED is illuminated on MCS screen 3.25.10 PCU-1 for transfer pump. Test Engineer: \_\_\_\_\_\_\_

VERIFY locally that the contactor for P-102-SY-02A has

Test Engineer: DG

3.25.11

OPENED.

PERATIONAL TEST	POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 34 OF 132 ATTACHMENT A
 	Signatures transferred from Rev. C
3.25.11a	RAISE pressure provided to PT-3125D by the VTPS to approximately 60 psig.
3.25.11b	BYPASS hi/low level limit alarm on P-102-SY-02A Transfer Pump (resets after 5 minutes).
3.25.12	SELECT P-3125B Booster Pump START on MCS screen PCU-2.
3.25.13	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
3.25.14	VERIFY the RUN LED is illuminated on VSD-2.  Test Engineer:DG
3.25.15	SELECT P-102-SY-02A Transfer Pump START on MCS screen PCU-1.
3.25.16	VERIFY DRIVE RUNNING is illuminated on MCS screen PCU-1.  Test Engineer:
3.25.17	PRESS P-3125B Booster Pump STOP on MCS screen PCU-2.
3.25.18	VERIFY the RUN LED is no longer illuminated on VSD-2.  Test Engineer: DG
3.25.19	VERIFY ENERGIZE ENABLED and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:
 3.25.20	VERIFY DRIVE STOPPED is illuminated on MCS screen PCU-1 for transfer pump. Test Engineer:
3.25.21	VERIFY locally that the contactor for P-102-SY-02A has OPENED.  Test Engineer:
3.25.22	DISCONNECT VTPS's from PT-3125B and PT-3125D.
0.20.22	DISCONNEST VITO S TI OIL TI OILOB WING TO SEED.

PREOPERATIONAL TEST REVISION NO. <u>0-A</u>	POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST  HNF-1857 PAGE 35 OF 132  ATTACHMENT A	
3.25.23	<pre>INSTALL software jumper (or "force" bit) to disable Interlocks 7 and 10 (booster pump inlet pressure).</pre>	
3.25.24	<pre>INSTALL software jumper (or "force" bit) to disable minimum discharge pressure requirement ("booster pump is running" in MCS logic, Ref. ES-058-Y74).</pre>	MF16D
Tempe	FOR	ess ! 413 /98
High Bearing Temperatur 3.26 TEST TSH-31	e TSH-3125B1 $FREEZE$ $-35°F$ $-35°F$ 25B1 per the following steps: $FREEZE$ $FREEZ$	
	evice is a three-wire RTD 00 6/17/98  [270 97   270 6/17/97	601
3.26.1	CONNECT the temperature calibrator to PCU-2B-TB2-01.  PCU-2B-TB2-I1, and PCU-2B-TB2-R1.  Max 12/16/97	
	t instrument only accepts a two lead RTD connection 1 and PCU-2B-TB2-R1 should be connected together as one ument.	
3.26.2	SELECT P-3125B Booster Pump START on MCS screen PCU-2.	
3.26.3	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:	
3.26.4	VERIFY the RUN LED is illuminated on VSD/2/ Test Engineer:	

PREOPERAREVISION NO		POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 36 OF 132 ATTACHMENT A
	3.26.5	On VSD-2 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data (information only):
	3.26	.5.1 Motor Freq <u>2</u> Hz .5.2 Motor Speed <u>3,3</u> % .5.3 Motor RPM <u>// 9</u> RPM
	3.26.6	Step deleted.
	3.26.7	Step deleted. Step deleted. $191^{\circ} F = (134.45) \Omega$
	3.26.8	SET the temperature (RTD) simulator to 190°F. (133.4)
	3.26.9	VERIFY at the MCS that TSH-3125B1 alarms.  Test Engineer:  202° = 136.8 J.
	3.26.10	
	3.26.11	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:
	3.26.12	VERIFY the RUN LED is no longer illuminated on VSD-2.  Test Engineer:
	3.26.13	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer:
	3.26.14	DISCONNECT the temperature calibrator from RTD DT PUMP PCU-2B-TB2-01, PCU-2B-TB2-II, and PCU-2B-TB2-R1.
	3.26.15	RECONNECT wire numbers TE3125B1-A, TE3125B1-B, and

VERIFY the wires are reconnected properly.

Test Engineer:

3.26.16

PREOPERATIONAL TEST REVISION NO. <u>0-A</u>	POTP-007, CROSS SITE TRANS HNF-1857 ATTACHMENT A	PAGE 37 OF 132 REFERS  PAGE 37 OF 132 REFERS  NOTE FOR PYROMETER 2/13/2  817-79-09-001 PUE 6-17-98
High Bearing Temperatu	•	HEAT GUN 198 OF 194 OF AMBIENT 59 OF 61 OF
•	125B2 per the following ste Device is a three-wire RTD	
3.27.1		calibrator to PCU-2B-TB2-02,
3.27.2	SELECT P-3125B Booster Pu	ump START on MCS screen PCU-2.
3.27.3	illuminated on MCS screen	ump START ENERGIZED and ON are n PCU-2. Engineer: <u>タ.</u> 光
3.27.4	Step deleted.	
3.27:5	Step deleted.	TRIPPED AT 191° F 134.5 D
3.27.6	SET the temperature (RTD)	simulator to 190°F. (133.4 )
3.27.7	VERIFY at the MCS that TS	SH-3125B2 alarms.  Thus $3 = 70.0 F (136.9. R)$
3.27.8	SET the temperature (RTD)	SH-3125B2 alarms.  TRIPPED AT $202^{\circ}F(136,95)$ ) simulator to $200^{\circ}F.(1365)$
3.27.9	VERIFY STATUS UNKNOWN and screen PCU-2 for booster	d OFF are illuminated on MCS
3.27.10	VERIFY P-102-SY-02A shut	down. (0:7/3 and 0:7/4, PCU1)
3.27.11	PCU-2B-TB2-02, PCU-2B-TB2	
3.27.12	RECONNECT wire numbers—The RECONNECT wire numbers—The TE3125B2-C to the correct	97 PU TO P SKIP 9.8 7/6/97 312582-A, TE312582-B, and terminal points.
3.27.13	VERIFY the wires are reco	onnected properly. Engineer:

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 38 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

High Motor Winding Temperature TSH-3125B.

3.28 TEST TSH-3125B per the following steps:

NOTE: Temperature sensor is a factory set, normally open temperature switch set to close at  $175~{}^{\circ}F$ .

3.28.1	SELECT P-3125B Booster Pump START on MCS screen PCU-2.
3.28.2	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
3.28.3	Step deleted.
3.28.4	Step deleted.
3.28.5	LIFT wire TSH-3125B-1 from pump skid junction box. WIRE 2007 232,
3.28.6	VERIFY at the MCS that TAH-3125B alarms.  Test Engineer:  ### PCS
3.28.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:
3.28.8	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer:
3.28.9	RE-LAND wire $\frac{7SH-3125B-1}{8.9}$ on pump skid junction box.
3.28.10	VERIFY TAH-3125B alarm clears at MCS.  Test Engineer:

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 39 OF 132

REVISION NO. <u>0-A</u>

## ATTACHMENT A

Signatures transferred from Rev. C

# High Vibration VSH-3125B1

3.29	TEST	VSH-3125B1	per	the	fol	lowing	steps:
------	------	------------	-----	-----	-----	--------	--------

•		,
	3.29.1 <del>X</del> 3/31/98	At the pump skid, in the junction box for the 24 volt signals, DISCONNECT wire PS2(+) and connect it to the positive lead of the PIC.
	3:29.2 **	At the pump skid, in the junction box for the 24 volt signals, DISCONNECT wire VT-3125B1(-) and connect it to the negative lead of the PIC.
	3.29.3	SET the PIC to 4 mA.
	3.29.4	SELECT P-3125B Booster Pump START on MCS screen PCU-2.
	3.29.5	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
	3.29.6	Step deleted.
	3.29.7	Step deleted.
1	3.29.8	SET the PIC to 8.8 mA corresponding to a vibration of 0.30 in/sec $\pm$ 0.05 in/sec.
	3.29.9	VERIFY at the MCS that VSH-3125B1 alarms Test Engineer:
<b>!</b> !	3.29.10	SET the PIC to 13.6 mA corresponding to a vibration of 0.60 in/sec $\pm$ 0.05 in/sec.
	3.29.11	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:
ļ.	3.29.12	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)
	3.29.13	DISCONNECT the PIC.
HNF-2504, REV. 0	3.29.14 X ATTACHMENTI	RECONNECT wire numbers PS2(+) and VT-3125B1(-) to the correct terminal points. $\frac{3}{3}l/98$

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 40 OF 132 ATTACHMENT A 3.29.15 RAP on the bearing housing adjacent to VE/VT-3125B1 and VERIFY output fluctuates for VI-3125B1 on MCS screen for booster pump P-3125B.

Test Engineer:

# High Vibration VSH-3125B2

3.30 TEST VSH-3125B2 per the following steps:

3.30.1 <del>X</del> 3/31/98	At the pump skid, in the junction box for the 24 volt signals, <b>DISCONNECT</b> wire PS2(+) and connect it to the positive lead of the PIC.
3.30.2	At the pump skid, in the junction box for the 24 volt signals, DISCONNECT wire VT-3125B2(-) and connect it to the negative lead of the PIC.
3.30.3	SET the PIC to 4 mA.
3.30.4	SELECT P-3125B Booster Pump START on MCS screen PCU-2.
3.30.5	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
3.30.6	Step deleted.
3.30.7	Step deleted.
3.30.8	SET the PIC to 8.8 mA corresponding to a vibration of 0.30 in/sec $\pm$ 0.05 in/sec.
3.30.9	VERIFY at the MCS that VSH-3125B2 alarms.  Test Engineer: 9.9.
3.30.10	SET the PIC to 13.6 mA corresponding to a vibration of 0.60 in/sec $\pm$ 0.05 in/sec.
3.30.11	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:

PREOPERATE REVISION NO		POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 41 OF 132 ATTACHMENT A	
	3.30.12	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1) Test Engineer: <u></u> <i>ூ.</i>	
	3.30.13	DISCONNECT the PIC.	
<del>X</del> 3/31/98	3.30.14	RECONNECT wire numbers PS2(+) and VT-3125B2(-) to the correct terminal points.	Ltven, Foa
	3.30.15	RAP on the bearing housing adjacent to VE/VT-3125B2 and VERIFY output fluctuates for VI-3125B2 on MCS screen for booster pump P-3125B.  Test Engineer:	12/13/9 129
Low Oil Leve	el LAL-3125E	31	
3.31	TEST LAL-31	L25B1 per the following steps:	REvent
	3.31.1	SELECT P-3125B Booster Pump START on MCS screen PCU-2.	
	3.31.2	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:	
	3.31.3	Step deleted.	(13/9
	3.31.4	Step deleted.	
	3.31.5	DRAIN oil from bearing housing B1 into a measurable container until LAL-3125B1 alarms at MCS, THEN IMMEDIATELY REPLACE drain plug.	EINAL ETTING 2/13/09
	3.31.6	MEASURE and RECORD the amount of oil drained. 155 / 245 gallons M.  Test Engineer: D. J.	れし。 あ.ಚ. ひ.3/4
	3.31.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:	43/9 2/13/9 0.4
	3.31.7a	- DRAIN remaining oil from bearing housing B1.  ### 12/16/97	U. XI.

3.31.7b 3.31.8	MEASURE and RECORD the total amount of oil drained.  gallons P.Y. 146/97 Test Engineer:  VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)
3.31.8	$\cdot = I I$ .
	Test Engineer: D.Y
3.31.9	REFILL bearing housing B1 with oil per manufacturer's instructions.  Test Engineer:
3.31.10	Step deleted.
el LAL-3125	B2
TEST LAL-3	125B2 per the following steps:
3.32.1	SELECT P-3125B Booster Pump START on MCS screen PCU-2.
3,32.2	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
3.32.3	Step deleted.
3.32.4	Step deleted.
3.32.5	DRAIN oil from bearing housing B2 into a measurable container until LAL-3125B2 alarms at MCS, THEN IMMEDIATELY REPLACE drain plug.
3.32.6	MEASURE and RECORD the amount of oil drained. 250  230 gallons A.  Test Engineer:
3.32.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:
3.32.7a	DRAIN remaining oil from bearing housing B2.
	3.31.10  P1 LAL-3125  TEST LAL-3  3.32.1  3.32.2  3.32.3  3.32.4  3.32.5

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 43 OF 132

REVISION NO. 0-A

ATTACHMENT A

NEVISION I	10. <u>0 A</u>	ATTACIDENT A
	-3.32.7b	MEASURE and RECORD the total amount of oil drained:  gallons D.H. 14/14/9)  Test Engineer:
	3.32.8	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer: 9.9/
	3.32.9	REFILL bearing housing B2 with oil per manufacturer's instructions.  Test Engineer: 99.
	3.32.10	Step deleted.
PUMP SEAL	FAILURE FAH	-3125B1
3.33	B TEST FAH-	3125B1 per the following steps:
	3.33.1	SELECT P-3125B Booster Pump START on MCS screen PCU-2.
	3.33.2	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
	3.33.3	Step deleted.
	3.33.4	Step deleted.
	3.33.5	LIFT the lead from PCU-ZA-TB-40,  PLACE a jumper between PCU-2A-TB3-40 and  PCU-2A-TB3-41. Sull 12/16/97
	3.33.6	VERIFY at the MCS that FAH-3125B1 alarms.  Test Engineer: ###################################
	3.33.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:
	3.33.8	Step deleted.
	3.33.9	Reconnect the lead to PCU-ZA-TB-40, REMOVE the jumper from between PCU-2A-TB3-40 and PCU-2A-TB3-41- Lake 197

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 44 OF 132 HNF-1857 ATTACHMENT A REVISION NO. <u>0-A</u> 3.33.10 **VERIFY** the jumper is removed. Test Engineer: PUMP SEAL FAILURE FAH-3125B2 3.34 TEST FAH-3125B2 per the following steps: SELECT P-3125B Booster Pump START on MCS screen PCU-2. 3.34.1 VERIFY P-3125B Booster Pump START ENERGIZED and ON are 3.34.2 illuminated on MCS screen PCU-2. Test Engineer: Step deleted. 3.34.3 Step deleted. 3.34.4 LIFT the lead from PCU-ZA-TB3-4Z. **PLACE** a jumper between PCU-2A-TB3-42 and 3.34.5 PCU-2A-TB3-43. Had 12/16/97 **VERIFY** at the MCS that FAH-3125B2 alarms. 3.34.6 **VERIFY** STATUS UNKNOWN and OFF are illuminated on MCS 3.34.7 screen PCU-2 for booster pump P-3125B.

# 3.34.8 **VERIFY** P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1) Test Engineer:

Test Engineer: \_\_\_\_

Reconnect the lead to PCU-ZA-TB3-4Z.

3.34.9

REMOVE the jumper from between PCU-ZA-TB3-42-and
PCU-ZA-TB3-43. \*\*Max 12/16/97

3.34.10 **VERIFY** the jumper is removed. Test Engineer:

### PUMP SEAL FAILURE PAL-3125B1

3.35 TEST PAL-3125B1 per the following steps:

3.35.1 SELECT P-3125B Booster Pump START on MCS screen PCU-2. HNF-2504, REV. 0 ATTACHMENT! PAGESY

PREOPER REVISION N		POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 45 OF 1 ATTACHMENT A
	3.35.2	VERIFY P-3125B Booster Pump START ENERGIZED and ON a illuminated on MCS screen PCU-2.  Test Engineer:
•	3.35.3	Step deleted.
	3.35.4	Step deleted.
	3.35.5	LIFT the lead from PCU-2A-TB3-60.
	3.35.6	VERIFY at the MCS that PAL-3125B1 alarms. Test Engineer:
	3.35.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer:
	3.35.8	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCL Test Engineer:
	3.35.9	RECONNECT the lead to PCU-2A-TB3-60.
	3.35.10	VERIFY the wires are reconnected properly.  Test Engineer:
PUMP SEAL	FAILURE PAL-	3125B2
3.36	TEST PAL-3	B125B2 per the following steps:
	3.36.1	SELECT P-3125B Booster Pump START on MCS screen PCU
	3.36.2	VERIFY P-3125B Booster Pump START ENERGIZED and ON a illuminated on MCS screen PCU-2.  Test Engineer:
	3.36.3	Step deleted.
	3.36.4	Step deleted.
	3.36.5	LIFT the lead from PCU-2A-TB3-62.

PREOPERATE PREVISION NO		POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 46 OF 132 ATTACHMENT A
	3.36.7	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.
	3.36.8	VERIFY P-102-SY-02A shut down. (0:7/3 and 0:7/4, PCU1)  Test Engineer:
	3.36.9	RECONNECT the lead to PCU-2A-TB3-62.
	3.36.10	VERIFY the wires are reconnected properly.  Test Engineer:
Interlock 2 P-3125B.	: On high pr	essure, shutdown operating booster pump, P-3125A or
PAH-3168		
3.37	TEST Interl	ock 2 for P-3125B per the following steps:
	3.37.1	SELECT P-3125B Booster Pump START on MCS screen PCU-2.
·	3.37.2	VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.  Test Engineer:
	3.37.3	CLOSE valve V-3168.  Test Engineer: £.J.
	3.37.4	CONNECT VTPS to PT-3168 and increase pressure until PI-3168 reads 12 psig at the MCS.
	3.37.5	VERIFY at the MCS that PAH-3168 Alarms.  Test Engineer:
	3.37.6	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer: カリ
	3.37.7	DISCONNECT the VTPS from PT-3168.
	3.37.8	OPEN valve V-3168. Test Engineer: 9.9.

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 47 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

Signatures transferred from Rev. O

Interlock 10:

Upstream Transfer Pump P-102-SY-02A will be shutdown if

inlet pressure reaches 70 psig.

Interlock 7:

The booster pump will not be permitted to operate if the

inlet pressure is lower than 10 psig.

### PAH-3125B

### 3.38 TEST PAH-3125B per the following steps:

- 3.38.1 CONNECT VTPS to the calibration port next to PT-3125B and increase pressure until PI-3125B reads 8 psig at the MCS.
- 3.38.1a CONNECT a VTPS to calibration port near PT-3125D and set pressure to approximately 60 psig.
- 3.38.1b **REMOVE** software jumper or forced bit disabling Interlocks 7 and 10 (booster pump inlet pressure).
- 3.38.1c REMOVE software jumper or forced bit disabling minimum discharge pressure requirement ("booster pump is running" in MCS logic, Ref. ES-058-Y74).
- 3.38.2 **SELECT** booster pump P-3125B START at the MCS.
- 3.38.3 VERIFY booster pump P-3125B STOPS after approximately 5 seconds.

  Test Engineer: DG

3.38.4 INCREASE pressure using VTPS until PI-3125B reads 12 psig at the MCS.

- 3.38.5 SELECT P-3125B Booster Pump START on MCS screen PCU-2.
- 3.38.6 **VERIFY** P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.

  Test Engineer:
- 3.38.6b **BYPASS** hi/low level limit alarm on P-102-SY-02A Transfer Pump (resets after 5 minutes).

REVISION NO		F POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 48 OF 132 ATTACHMENT A SIANA tras transformed from
	3.38.7	Signatures transferred from Day 12/16/97 SELECT P-102-SY-02A Transfer Pump START on MCS screen PCU-1.
	3.38.8	VERIFY DRIVE RUNNING is illuminated on MCS screen PCU-1.  Test Engineer: DG
	3.38.9	INCREASE pressure, using VTPS connected to PT-3125B, until PI-3125B reads 72 psig at the MCS.
	3.38.10	VERIFY at the MCS that PAH-3125B alarms.  Test Engineer: DG
	3.38.11	Step deleted.
	3.38.12	VERIFY DRIVE STOPPED is illuminated on MCS screen PCU-1 for transfer pump.
		Test Engineer: DG
Interlock 1	<b>4:</b> On H pump	Test Engineer: DG
Interlock 1		Test Engineer: DG
PAH-3125D	pump	Test Engineer: DG
PAH-3125D	pump	Test Engineer: DG
PAH-3125D	pump TEST PAH-3	Test Engineer: DG  High discharge pressure, shutdown appropriate operating  B125D per the following steps:  SET the VTPS that is currently connected to PT-3125B
PAH-3125D	pump TEST PAH-3 3.39.1	Test Engineer: DG  High discharge pressure, shutdown appropriate operating  B125D per the following steps:  SET the VTPS that is currently connected to PT-3125B to a pressure between 12 psig and 68 psig.  Step deleted.
PAH-3125D	pump TEST PAH-3 3.39.1 3.39.2	Test Engineer: DG  High discharge pressure, shutdown appropriate operating  B125D per the following steps:  SET the VTPS that is currently connected to PT-3125B to a pressure between 12 psig and 68 psig.
PAH-3125D	pump TEST PAH-3 3.39.1 3.39.2 3.39.3	Test Engineer:  High discharge pressure, shutdown appropriate operating of the following steps:  SET the VTPS that is currently connected to PT-3125B to a pressure between 12 psig and 68 psig.  Step deleted.  SELECT P-3125B Booster Pump START on MCS screen PCU-2  VERIFY P-3125B Booster Pump START ENERGIZED and ON are illuminated on MCS screen PCU-2.

PREOPERATIO	DNAL TEST F	POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 49 OF 132
REVISION NO	<u>0-A</u>	ATTACHMENT A Signatures transferred from Rev. 0
3.	.39.6	VERIFY DRIVE RUNNING is illuminated on MCS screen PCU-1.  Test Engineer: DG
3.	.39.7	INCREASE pressure, using VTPS connected to PT-3125D, until PI-3125D reads 1275 psig at the MCS.
3.	.39.8	VERIFY at the MCS that PAH-3125D alarms.  Test Engineer:
3.	.39.9	VERIFY STATUS UNKNOWN and OFF are illuminated on MCS screen PCU-2 for booster pump P-3125B.  Test Engineer: DG
3.	.39.10	VERIFY DRIVE STOPPED is illuminated on MCS screen PCU-1 for transfer pump.  Test Engineer:
3.	.39.11	DISCONNECT the second VTPS from PT-3125D.
3.	.39.12	OPEN valve V-3125D.  Test Engineer: DG
Interlock 15:	The b	ECT WOS8-393 DOI START 4//28 ooster pump will not be permitted to <del>operate</del> if the iated bypass, vent, and drain valves are not closed. REVE
3.40 TI	EST Interl	ock 15 for P-3125B per the following steps:
3	.40.1	<b>OPEN</b> SOV-3163.
3	.40.2	SELECT booster pump P-3125B START at the MCS.
3	.40.3	VERIFY booster pump P-3125B START at the MCS.  VERIFY booster pump P-3125B does NOT start.   2
3	.40.4	CLOSE SOV-3163.

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 49a OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

3.40.5 Signatures transferred from Rev. 0 Aay 12/16/97 OPEN each P-3125B motor operated drain valve and vent valve one at a time from the MCS, VERIFY STATUS UNKNOWN appears on MCS screen for P-3125B, attempt to START P-3125B from the MCS, VERIFY P-3125B does NOT START, and THEN CLOSE the associated valve.

Valve No.	Description	MCS Position	Pump DID NOT Start
MOV-3125BA	P-3125B Drain Valve	OPEN	DG 12/15/97
MOV-3125BB	P-3125B Drain Valve	OPEN	DĠ
MOV-3125BC	P-3125B Drain Valve	OPEN	DG
MOV-3125BD	P-3125B Drain Valve	OPEN	DG
MOV-3125BE	P-3125B Drain Valve	OPEN	DG
MOV-3125BF	P-3125B Drain Valve	OPEN	D9
MOV-3125BG	P-3125B Drain Valve	OPEN	DG
MOV-3125BH	P-3125B Drain Valve	OPEN ·	D6
MOV-3125BJ	P-3125B Drain Valve	OPEN	D9
MOV-3125BK	P-3125B Vent Valve	OPEN	DG

Test Engineer.	Test	Engineer:	DG
----------------	------	-----------	----

P-3125B interlock testing complete

3.41	TAKE	VSD-2	out	of	NO	MOTOR	TEST	MODE	per	the	following	steps
------	------	-------	-----	----	----	-------	------	------	-----	-----	-----------	-------

- 3.41.1 PRESS the PROGRAM key on VSD-2 keypad.
- 3.41.2 SELECT PARAM and PRESS the ENTER key.
- 3.41.3 SCROLL thru the list of drive parameters using the UP and DOWN arrows until NO MOTOR TEST MODE is shown.
- 3.41.4 PRESS the LINE key.
- 3.41.5 SELECT NO (under NO MOTOR TEST MODE) and PRESS the ENTER key.

Test Engineer: \( \frac{1}{2} \frac{1}{1} \)

2/13/98

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 49b OF 132 REVISION NO. \_0-A\_ ATTACHMENT A PRESS the MONITOR key on VSD-2 keypad. 3.41.6 **VERIFY** the MONITOR and DRIVE READY LEDs are 3.41.7 illuminated on VSD-2. Test Engineer: \_ 3.42 DISCONNECT the VTPS from calibration port next to PT-3125B. 3.43 OPEN valve V-3125B. Signature transferred Test Engineer:

from Rev. O

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 50 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

4.0	Initi	al Conditions / Pre-Transfer Loop Fill	
Recor	nect V	/SDs to booster pump motors	·
•	4.1	OPEN VSD-1 Main Disconnect.	
•	4.2	LOCK & TAG VSD-1 Main Disconnect OPEN.  Test Eng	neer: A into
	4.3	RECONNECT Booster Pump (P-3125A) Motor Test Eng	
Reverse order	<del>7</del> 4.4	CLOSE VSD-1 Main Disconnect.  Test Eng	neer: De 140
OF STEPS	<b>→</b> 4.5	REMOVE Lock & Tag from VSD-1 Main Disco Test Eng	
	4.6	LOCK AND TAG VSD-2 Main Disconnect OPE	I. Alle
	4.7	REMOVE Lock & Tag from VSD-2 Main Disco Test Eng	
	4.8	RECONNECT Booster Pump (P-3125B) Motor Test Eng	
order of	<del>&gt;</del> 4.9	CLOSE VSD-2 Main Disconnect.  Test Eng	ineer: <u>D.G. 12/5</u>
12-19-97	<b>4</b> .10	REMOVE Lock & Tag from VSD-2 Main Disco Test Eng	onnect. ineer: <u>D.G. 12/15</u>
		orm a check of the data logger. This chart of Section 7.0. STEPS 4.11	eck may be made any time THAU 4.15 ARE DELETED AS OTTON IN RECORDED AT THE DLC
	4.11	DISCONNECT the output leads from system and CONNECT a PIC to the wires going to Test En	m flowmeter FE-3125 to PCU-2 D.B D PCU-2.

4.12 SET the PIC to output a current of 8 mA (nominal).

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 51 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

4.13	CHECK datalo	ogger performance with VSD-1:
	4.13.1	VERIFY the datalogger for the signal to VSD-1 and the flow signal is installed.  Test Engineer:
	4.13.2	REMOVE the rate-of-change (ramp) limit(s) from the control signal logic in the PCU for P-3125A.  Test Engineer:
	4.13.3	SELECT PID MAN on MCS screen PCU-2 for Booster Pump P-3125A.  Test Engineer:
(0-240  gpm)	in PID MANU/ will actual motor via th	AL, setting the Fluid FLOW (SP) to 50% of full scale ly send a 50% of full scale (0-3600 rpm) control signal he VSD.
	4.13.4	SET Fluid FLOW (SP) to 120 gpm (50% of full scale).  Test Engineer:
	4.13.5	BEGIN data logging of the flow signal and the signal to VSD-1. AFTER 1 minute STOP the data logger.
	4.13.6	VERIFY the recorded signal from VSD-1 is 50% of full scale (nominal) and the flow signal is 25% of full scale (nominal).  Test Engineer:
4.14	CHECK datal	ogger performance with VSD-2:
	4.14.1	VERIFY the datalogger for the signal to VSD-2 and the flow signal is installed.  Test Engineer:
	4.14.2	REMOVE the rate-of-change (ramp) limit(s) from the control signal logic in the PCU for P-3125B.  Test Engineer:
·	4.14.3	SELECT PID MAN on MCS screen PCU-2 for Booster Pump P-3125B.  Test Engineer:

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 52 OF 132

REVISION NO. 0

ATTACHMENT A

NETIOION NO	•	, , , , , , , , , , , , , , , , , , ,
	will actua	NUAL, setting the Fluid FLOW (SP) to 50% of full scale Ally send a 50% of full scale (0-3600 rpm) control signal the VSD.
,	4.14.4	SET Fluid FLOW (SP) to 120 gpm (50% of full scale).  Test Engineer:
	4.14.5	BEGIN data logging of the flow signal and the signal to VSD-2. AFTER 1 minute STOP the data logger.
	4.14.6	VERIFY the recorded signal from VSD-2 is 50% of full scale (nominal) and the flow signal is 25% of full scale (nominal).  Test Engineer:
4.15		T the PIC from the wires to PCU-2 and RECONNECT flowmeter to the wires to PCU-2.  Test Engineer:

NOTE: SOV's that block the flow of liquid to 241-SY valve pits and to 244A lift station that are normally OPEN during Transfer Scheme 2A or 2B, must be physically CLOSED during this test. Forcing the affected SOV's OPEN in the MCS software and jumpering out the valve failure alarm for each will allow the transfer to commence.

- 4.16 INSTALL a normally open software jumper in series with N19:2/13 VALVE FAILURE Alarm for SOV-3183A.

  Test Engineer:  $\frac{2}{13/9}$
- 4.17 INSTALL a normally open software jumper in series with N19:2/12 VALVE FAILURE Alarm for SOV-3183B.

  Test Engineer: 2/13/58
- 4.18 INSTALL a normally open software jumper in series with B3/92 VALVE FAILURE Alarm for SOV-3166B.

  Test Engineer: 9.9.2/13/98
- 4.19 FORCE (in the MCS software) the associated bits for the following valves to the MCS position shown. VERIFY position indication given by MCS and actual position (local verification).

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 53 OF 132 HNF-1857

REVISION NO. <u>0</u>

ATTACHMENT A

Valve No.	Description	MCS Position	Verif. Initials	Local Position	Verif. Initials
SOV-3183A	WT-SLL-3160 at Diversion Box	OPEN	D.Y.	CLOSED	Pl n/19
SOV-3183B	WT-SLL-3160 at Diversion Box	OPEN	DY.	CLOSED	Al IV,
SOV-3166B	WT-SLL-3160 at Vent Station	OPEN	29	CLOSED	10 n/g
50V-3182A	WYSNE-3156 AT PINEASION BOX	CLOSCO		CLOSED	
SOU-3/82 B	WT 25.01 - 3150 AT DISEASON BOX	rest Engin	eer:	1. 2/13/98	

NOTE: Certain SOV's in the 3150 supernate line normally CLOSED by master valve reset when initiating Transfer Scheme 2A or 2B, must be physically OPEN to allow circulation thru the Diversion Box / Vent Station loop. Forcing the affected SOV's CLOSED in the MCS software and jumpering out the valve failure alarm for each will allow the transfer to commence.

4.20 INSTALL a normally open software jumper on in series with N19:2/10VALVE FAILURE Alarm for SOV-3184.

Test Engineer:

4.21 INSTALL a normally open software jumper in series with B3/80 VALVE FAILURE Alarm for SOV-3165A. Test Engineer: 9.9.2/3/98

4.22 FORCE (in the MCS software) the associated bits for the following valves to the MCS position shown. VERIFY MCS position indication and actual position (local verification).

					126,0 5
Valve No.	Description	MCS Position	Verif. Initials	Local Position	Verif. Initials
SOV-3184	WT-SNL-3150 at Diversion Box	CLOSED	D.QJ, 2/13/2	OPEN	May
S0V-3165A	WT-SNL-3150 at Vent Station	CLOSED	D. St. 2/13/9	OPEN C	aling

Test Engineer: 1/13/94

NOTE: The pipe jumpers fabricated for the W-058 Project for the 244A pit are not yet installed. Therefore it is necessary to simulate the positions of the motor operated valves on the 244A jumper so that Transfer Schemes 2A and 2B will allow the booster pump to operate. Forcing the affected MOV's to the required position in the MCS software and jumpering out the valve failure alarm for each will allow the transfer to commence.

HNF-2504, REV. 0 ATTACHMENT \ PAGE97

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 54 OF 132 HNF-1857

REVISION NO. 0-A

ATTACHMENT A

INSTALL a normally open software jumper in series with N19:4/9 VALVE FAILURE Alarm for MOV-845. Test Engineer:

4.24 FORCE (in the MCS software) the associated bits for the following valves to the positions shown.

Valve No.	Description	Required Position	Initials
MOV-844	WT-SLL-3160 Motor Operated 3-Way Valve at 244A Lift Station	A ⇒ B	19.91.
MOV-845	WT-SLL-3160 Motor Operated Valve at 244A Lift Station	OPEN	D.H.

el 2/13/98

4.25 VERIFY the SOV's and MOV's are aligned for transfer, loop filling in accordance with Appendix E.

Test Engineer:

Test Engineer:

VERIFY the purge/flush ball valve is CLOSED on eyegy, SOV.

Test Engineer:

AND LOCK "BLUE" TAG the manual valve actuators on the following SOV'S CLOSEO de 12-19-97 Test Director: 4.27.1 SOV-3182A Test Director: 4.27.2 SOV-3182B Test Director:

SOV-3183A 4.27.3 Test Director: SOV-3183B 4.27.4 Test Director: 4.27.5 SOV-3166A

SOV-3166B

Test Director:

M

M

car

HNF-2504, REV. 0 ATTACHMENT | PAGE98

4.27.6

<b>PREOPERATIONAL</b>	TEST	POTP-007,	CROSS	SITE	TRANSFER	SYSTEM	INTEGRATE	D.	TEST	-
		į	HNF - 185	57			PAGE	55	0F	132
TOTON NO O		4.	TT 4 OLD 4	- LIT A						

REVISION	NO.	_0_
----------	-----	-----

ATTACHMENT A

4.28	VERIFY	instrument	air	pressure	to	the	P-3125A	seals	is	greater
	than 95	psig.								

4.28.1 PI-3125A1 psig 4.28.2 PI-3125A2 \_ psig

Test Engineer:



4.29 VERIFY instrument air pressure to the P-3125B seals is greater than 95 psig.

4.29.1 PI-3125B1 128 psig 4.29.2 PI-3125B2 <u>128</u> psig

Test Engineer:

4.30 VERIFY test jumper is installed between Transfer Headers 3160 and 3150 at the Vent Station per Appendix A sketch.

Test Engineer:

4.31 **VERIFY** test jumper is installed between water supply outside Diversion Box and Transfer Header 3160 per Appendix A sketch.

Test Engineer:

4.32 VERIFY test jumper is installed between Transfer Header 3150 and water supply outside Diversion Box per Appendix A stetch.

ر :Test Engineer

4.33 VERIFY test setup is configured per Appendix A sketch

Test Engineer:

SEE TEST L09 ENTR

REVENIFIED FORretest Ra

2/13/98

2/13/98

REVISION NO. 0

ATTACHMENT A

### 5.0 Transfer Loop Fill

NOTE: The following procedure for filling the transfer headers with water before a transfer is tailored to the "loop" test configuration. For an actual waste transfer, the water flush system would be used and the vent valves at the Vent Station would be closed.

- 5.1 OPEN valve V-temp-1.
- 5.2 CRACK OPEN flow control valve V-temp-2.
- 5.3 ADJUST pressure control valve on the water tank recirculation bypass on the supply jumper to the CLOSED position?

15 required to facilitate filling
14 TURN ON supply pump. (60836) 30 12/19/44

NOTE: Assuming the supply pump fills the line at a rate of 150 gallons per minute, it will take approximately 25 minutes to empty a 4000 gallon tank.

NOTE: The transfer line volume between the Diversion Box and Vent Station is approximately 4000 gallons. The fluid volume from the holding tank may not fill up the line to the system high point before it needs to be refilled, in which case no fluid would be detected on the downstream side.

- 5.5 IF fluid is detected at the temporary flowmeter, FI-temp, THEN CLOSE flow control valve V-temp-2. ELSE N/A step.
- Test Engineer: WA

  To REPICE TANKER SH 2/3/98

  5.6 After supply pump breaks suction (truck emptied of fluid), perform the following:
  - 5.6.1 **CLOSE** V-temp-1.

Test Engineer: 12/19

5.6.2 TURN OFF supply pump.

5.6.3 RE-FILL truck with water. DISCONNECT/RECONNECT hose, supply pump, and/or fittings as required to refill tank.

Test Engineer: \_\_

5.7 **TURN ON** supply pump.

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST $$\operatorname{\textsc{HNF}}\xspace-1857}$$ PAGE 57 OF 132

REVISION NO. <u>0</u> ATTACHMENT A

5.8	OPEN	valve	V-temp-1.
-----	------	-------	-----------

5.9 WHEN fluid is detected at the temporary flowmeter, FI-temp, THEN CLOSE flow control valve V-temp-2. N/A step if V-temp-2 already closed per earlier step.

Test Engineer: 20 11/19

NOTE: To completely fill the downhill leg of the loop with water, the rate of fluid addition should be slowed to allow continuous venting of air back up the line to the Vent Station. If the fill rate is too great, spillage will occur out thru vent line SNL-3152. Monitor vent line SNL-3152 for feedback on setting the fill rate.

- 5.10 **OPEN and ADJUST** pressure control valve on the water tank recirculation bypass as necessary to reduce system filling rate.
- 5.11 IF air can no longer be detected venting thru line SNL-3152 at the Vent Station (i.e. fluid is continuously discharging thru vent line(s)), THEN:

5.11.1	CLOSE	valve	V-temp-1.
--------	-------	-------	-----------

- 5.11.2 **OBSERVE** SNL-3152 for a short time to see if any air trapped in line works its way up and vents.
- 5.11.3 THROTTLE OPEN valve V-temp-1 as necessary.
- 5.11.4 IF supply pump breaks suction (holding tank emptied of fluid) before all air is vented from loop, THEN refill holding tank. N/A step if not performed.

  Test Engineer:

- 5.11.5 **CLOSE** valve V-temp-1 upon continuous fluid discharge thru SNL-3152.
- 5.11.6 REPEAT until loop is entirely filled with liquid.

  Test Engineer: /////
- 5.12 CLOSE the isolation SOV's on supernate vent line SNL-3152.

5.12.1 SOV-3185A CLOSED Test Engineer: 12/15
5.12.2 SOV-3185B CLOSED Test Engineer: 12/15

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF - 1857 PAGE 58 OF 132

REVISION NO. 0

ATTACHMENT A

5.13	CLOSE the			· ~		REWERIPION FOR REFEST
	5.13.1	SOV-3163	CLOSED Test	Engineer: 🎉	12/19	ol
5.14	OPEN valve					2/13/98

5.15 OPEN flow control valve V-temp-2.

NOTE: Use supply pump to circulate fluid through the loop and help sweep out any remaining air pockets in the transfer loop.

5.16 **CONTINUE** supply pump operation for approximately 30 minutes. Test Engineer: 1417

5.17 **CLOSE** flow control valve V-temp-2.

Test Engineer: All iving

Test Engineer: All iving

5.18 CLOSE valve V-temp-1.

5:19 TURN OFF supply pump.

### 6.0 Post-Fill Data Recording

- 6.1 **RECORD** static pressures from the temporary pressure indicators:
  - 6.1.1 PI-temp-1 (supply leg) \_\_\_\_ psig
  - 6.1.2 PI-temp-2 (return leg) ic-15 psig
  - 6.1.3 PI-temp-3 (return leg) 15 psig
- RECORD the instrument air flow rate to each pump seal per the flow 6.2 indicators on the pump seal control panels:
  - 6.2.1 FI-3125A1 8 14 scfh 3-1 a region
  - 6.2.2 FI-3125A2 <u>1223</u> scfh
  - 6.2.3 FI-3125B1 🤌 🖧 scfh
  - 6.2.4 FI-3125B2 4.4.5 scfh

Test Engineer: Miliania

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 59 OF 132

REVISION NO. \_O\_

ATTACHMENT A

NOTE: Those parameters with the word "isolated" in parentheses next to them should be indicating a value near zero.

6.3 RECORD initial data from MCS screen PCU-2 for Diversion Box:

```
PI-3125A
6.3.1 P-3125A Inlet pressure
                                           PI-3125C
                                                      50 psig
6.3.2 P-3125A Discharge pressure
6.3.3 P-3125B Inlet pressure
                                           PI-3125B
                                                          psiq
                                         <sub>/gx</sub>PI-3125D
6.3.4 P-3125B Discharge pressure
                                                      50
                                                            psiq
6.3.5 Supernate Line pressure (isolated)
                                                          psiq
                                           PI-3182
6.3.6 Supernate Line pressure (isolated)
                                           PI-3125E
                                                             psiq
6.3.7 Supernate Line temperature
                                           TI-3125B
6.3.8 Slurry Line pressure (isolated)
                                           PI-3183
                                                       psig ک
6.3.9 Slurry Line temperature
                                           TI-3125A
6.3.10 Sump Line pressure (isolated)
                                           PI-3173
                                                           psiq
                               Test Engineer: _
```

6.4 RECORD initial data from MCS screen PCU-3 for Vent Station:

99	T'e					
6.4.1 Supernate Line pressure (isolated)	PI-3126A <u>    8</u> psig					
6.4.2 Supernate Line temperature	TI-3126A <u>\$z</u> °F					
6.4.3 Slurry Line pressure	PI-3126B <u>//2</u> psig					
6.4.4 Slurry Line temperature	TI-3126B <u>73</u> °F					
6.4.5 SNL Vent Line pressure (isolated)	PI-3185 <u>~ ~</u> psig					
6.4.6 SLL Vent Line pressure (isolated)	PI-3168 <u>O</u> psig					
6.4.7 Sump Line pressure (isolated).	PI-3167 psig					
Test Engineer: <u>りり りょり</u>						

Q Q

NOTE: Neglect header pressure and temperature values given on MCS screen PCU-4 for 244A Lift Station. Instrumentation not yet installed, not within scope of this test.

6.5 **RECORD** initial data from MCS screen PCU-2 for Booster Pump P-3125A (PV = Process Variable):

		ม. bA
6.5.1 Pump Thrust End B	Bearing temp TI-3125Al	o <sup>k</sup> 52_ °F
6.5.2 Pump Drive End Be		<u>58</u> °F
6.5.3 Motor speed		<u>-900</u> RPM
6.5.4 Thrust End vibrat	cion VI-3125A1	0.00 mils 185 D.D. 2/1/98
6.5.5 Drive End vibrati	ion VI-3125A2	0.00 mils 185 -0. 41498
6.5.6 Fluid flow	FIC-3125	<u> </u>
6.5.7 Fluid temperature	TI-3125	<u>61</u> °F
6.5.8 Fluid Inlet press	sure PI-3125A	<u>4%</u> psig

HNF-2504, REV. 0 ATTACHMENT 1 PAGE(03)

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST
HNF-1857 PAGE 60 OF 132

REVISION NO. 0

ATTACHMENT A

6.5.9 Fluid Outlet pressure  Test Engineer:  PI-3125C Test Engineer:  PI-3125D Test Engineer:  P				
$(PV = Process \ Variable): \ (with Drive of) \ \frac{9.97}{PV} \ \frac{2}{\sqrt{3}} \ \frac{9}{8} \ \frac{9}{8} \ \frac{1}{8} \ $		<u>.</u>		
6.6.1 Pump Thrust End Bearing temp TI-3125B1 58 °F 6.6.2 Pump Drive End Bearing temp TI-3125B1 60 °F 6.6.3 Motor speed SI-3125B 13 RPM 6.6.4 Thrust End vibration VI-3125B1 0.00 mils 1PS 0.91 2/5/g 6.6.5 Drive End vibration VI-3125B2 0.00 mils 1PS 0.91 2/5/g 6.6.6 Fluid flow FIC-3125 0 0 GPM 6.6.7 Fluid temperature TI-3125 6/ °F 6.6.8 Fluid Inlet pressure PI-3125B 49 psig 6.6.9 Fluid Outlet pressure PI-3125D 50 psig	6.6		NIVE ON) D.D 2/10/98	
rest Lighteer		6.6.2 Pump Drive End Bearing temp 6.6.3 Motor speed 6.6.4 Thrust End vibration 6.6.5 Drive End vibration 6.6.6 Fluid flow 6.6.7 Fluid temperature 6.6.8 Fluid Inlet pressure 6.6.9 Fluid Outlet pressure	TI-3125B1	\$

## 7.0 Booster Pump P-3125A Startup Test

This section verifies initial startup and operation of the installed pump. The booster pump will be operated remotely from the MCS in PID MANUAL mode, under control of input motor speed. Operating speeds are selected for purpose of tuning PID (Proportional, Integral, Derivative) flow control.

The presence of a vendor representative from Panametrics Flowmeters is very desirable, but not absolutely required for this portion of the test. Calibration of the ultrasonic flowmeter was performed at the vendor's facility. The flowmeter does not physically contact the fluid in the pipe.

7.1 **VERIFY** temporary water supply tank is sufficiently full of water to perform this test.

Test Engineer:

7.2 The vendor representative from Sulzer Bingham pump company is

Test Engineer:

7.17

7.17

1.18

1.19

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

1.2.12

HNF=1857...

<del>74 OF 150-</del>

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 61 OF 132

REVISION NO	
Select -50%	VERIFY ENERGIZE ENABLE, REMOTE, and OFF are illuminated on MCS pevens screen PCU-2 for Booster Pump P-3125A.  Test Engineer:  Deeed as first operating point.
9. \$ 7.5 2/18/18/18 7.6	SELECT PID MAN on MCS screen PCU-2 for Booster Pump P-3125A.  For USD RAMP TO 12 (SSECOVE) Test Engineer:  The Control valve V-temp-2 fully open an actual flow of about 110 gpm is expected.)  Test Engineer:  Test Engineer:
7.7	Test Engineer: D.D.
test should	previously "forced" to a position on the MCS for purposes of this not be shown as valve positioning failures because the associated alarms are jumpered out per Section 4.0.
.7.8	ERIFY Alarm Table on MCS shows no valve positioning failures.  Test Engineer:

**SELECT** the Transfer Sequencing **INITIATE** Button.

NOTE: Transfer Scheme 2A sets up for transfer of slurry from the 241-SY-B valve pit to the 241-A-A valve pit.

MANUALLY ROSITION VALUES PER APPENDIX F-1
7.10 SELECT the Transfer Sequencing TYPE 2A transfer by

Test Engineer:

7.11 **VERIFY** proper valve position in accordance with Appendix F-1 Data

Sheet.

7,11,1 Junger A-Pump very value Test Engineer: 12/19

TERMINALS 39 & 40 For RETEST. D. St. 2/13/98 SEE FEST LOG ENTRY

NOTE: The boxes on the MCS overview screen that denote PCU-1 thru PCU-5 indicate status of the transfer path. All boxes GRAY and paths GREEN indicates that the transfer path is ready for use. Boxes filled in RED indicates that an alarm associated with the transfer is activated (i.e. mispositioned valve, leak detected, etc). The booster pump will not start unless associated alarms are either cleared or over-ridden.

HNF-2504, REV. 0 ATTACHMENT | PAGEIOS

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF - 1857 PAGE 62 OF 132

REVISION NO. 0

ATTACHMENT A

thru PCU-5 are highlighted in RED, DETERMINE the reason why and perform the following:

7.12.1 Disposition the problem by fixing it and clearing alarm, or by overriding the alarm IF the Test Engineer determines that the problem will not affect the performance of this test. RECORD disposition on the Test Log or on a Test Exception Sheet, at the discretion of the Test Engineer. N/A this step if not performed.

Test Engineer:

7.13 **VERIFY** the boxes on the MCS overview screen which denote PCU-1 thru PCU-5 are highlighted in GRAY, unless a RED box has been determined to be acceptable per the previous step

SOV-31259 (SEE TEST LOW ENTRY ) OPEN SOV-3125E and SOV-3125C from the MCS.

Test Engineer:

Set booster pump inlet pressure control

- 7.15 **ADJUST** pressure control valve on the supply jumper assembly to an arbitrary OPEN position.
- 7.16 TURN ON supply pump.
- 7.17 **VERIFY** water is being recirculated to holding tank.

Test Engineer: \_

7.18 ADJUST pressure control valve on the supply jumper assembly so that the pressure indicator at the supply pump discharge reads approximately 50 ps ju. 2/14/98

7.18.1 PI-temp-1 psig

Test Engineer:

7.19 **OPEN** valve V-temp-1.

Test Engineer

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 63 OF 132

7.20 -FULLY OPEN flow control valve V-temp-2. appear language of the bassier pump stops during the performance of this test unexpectedly, THEN close V-temp-1 and V-temp-2 and shift of supply pump. Determine the redson for problem! recers on the Test Log. To Restrict Hill test Return to start P-3125A perform stops through skep 7.25 (except for skep 7.21a).  7.21 NOTIFY Sulzer Bingham representative that the booster pump is to be started.  Test Engineer: Problem is to be started.  7.21 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.2a PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.3a VERIFY motor shaft rotated in proper direction. Test Engineer: Pump P-3125A.  7.21.3a VERIFY motor shaft rotated in proper direction. Test Engineer: Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.24 VERIFY locally that P-3125A is operating. Test Engineer: Pump P-3125A.  7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.  Test Engineer: Pump P-3125A received speed to SPEED To SOYO (1206/pm)  7.26 RECORD the following data: (See res r Log 2/o/25) P.S. 2/o/26  7.26 RECORD the following data: (See res r Log 2/o/25) P.S. 2/o/26			<u>0-A</u>	ATTACHMENT A		
7.20 FULLY OPEN flow control valve V-temp-2. Approx (1971)  NOTE: If the booster pump store during the performance of this test unexpectedly, Turent close V-temp-1 and V-temp-2 and shut-off supply ump. Determine the redeon for Prepare to start P-3125A perform steps through step 7.25 (except for step 7.21a).  7.21 NOTIFY Sulzer Bingham representative that the booster pump is to be started.  7.21a "BUMP" the motor to verify proper rotation direction as follows:  7.21.1a PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.2a PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.3a VERIFY motor shaft rotated in propen direction.  Test Engineer:  1.19  IMPORTANT: Be prepared to immediately shut down booster pump if so requested by Sulzer Bingham representative. To shut down the pump, PRESS the OFF key on VSD-1 keypad OR the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  500 Test Log Booster Pump  7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  1/1 Test Engineer:  1/2 Test Engineer:  1/3 Test Engineer:  1/4 Test Eng					Jby 12/17	197
NOTE: If the booker pump stors during the performance of this test unexpectedly, THEW  CLOSE V-temp-1 and V-temp-2 and shift off supply unp. Determine the read on the rest leg. To Restmant the test, Return to Step 7.16 and Prepare to Start P-3125A parform steps through step 7.25 (except for step 7.21a).  7.21 NOTIFY Sulzer Bingham representative that the booster pump is to be started.  Test Engineer: Pump is to be started.  Test Engineer: Pump is to be started.  7.21.1a PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.2a PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.3a VERIFY motor shaft rotated in proper direction.  Test Engineer: Pump P-3125A.  7.21.3b VERIFY motor shaft rotated in proper direction.  Test Engineer: Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.24 VERIFY locally that P-3125A is operating.  Test Engineer: Pump P-3125A VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.  Test Engineer: Pump P-3125A VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.  Test Engineer: Pump P-3125A VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.				Tes	emp-2. approx st Engineer:	DE IZIO
7.21 NOTIFY Sulzer Bingham representative that the booster pump is to be started.  Test Engineer:  7.21a "BUMP" the motor to verify proper rotation direction as follows:  7.21.1a PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.2a PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.3a VERIFY motor shaft rotated in proper direction.  Test Engineer:  11.19  IMPORTANT: Be prepared to immediately shut down booster pump if so requested by Sulzer Bingham representative. To shut down the pump, PRESS the OFF key on VSD-1 keypad OR the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  7.24 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.  Test Engineer:  7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.	Note: 197 Prepare	IF AI CLOSE Proble to S	ve booster pum V-temp-1 and mirecord on tart P-3125		_	test unexpectedly, THEV etermine the reason for URN to Step 7,16 and
7.21a "BUMP" the motor to verify proper rotation direction as follows:  7.21.1a PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.2a PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.3a VERIFY motor shaft rotated in proper direction. Test Engineer:  11.19  IMPORTANT: Be prepared to immediately shut down booster pump if so requested by Sulzer Bingham representative. To shut down the pump, PRESS the OFF key on VSD-1 keypad OR the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  See Test Low Burney 3/3/198  7.25 VERIFY the UP TO SPEED and RUN LEBs are illuminated on VSD 1.		. 21	NOTIFY Sulz	er Bingham representat <sup>.</sup>	ve that the b	oooster pump is to
Pump P-3125A.  7.21.2a PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.21.3a VERIFY motor shaft rotated in proper direction. Test Engineer:  IMPORTANT: Be prepared to immediately shut down booster pump if so requested by Sulzer Bingham representative. To shut down the pump, PRESS the OFF key on VSD-1 keypad OR the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A. Mg 12/1/197 7.23.a FULLY OPEN V-temp-Z per diversion of Sulzer Bingham Representative (or testeng Test Engineer:  Test Engineer:  SEE TEST LOG ESTING 3/3/199 7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.	7	.21a	"BUMP" the		O	
Pump P-3125A.  7.21.3a VERIFY motor shaft rotated in proper direction. Test Engineer:  10.19  IMPORTANT: Be prepared to immediately shut down booster pump if so requested by Sulzer Bingham representative. To shut down the pump, PRESS the OFF key on VSD-1 keypad OR the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A.  7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  See Test Low Entry 3/sings  7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.  Test Engineer:  Test Engineer:  Test Engineer:  Test Engineer:  Test Engineer:			7.21.1a		n on MCS scree	n PCU-2 for Booster
IMPORTANT: Be prepared to immediately shut down booster pump if so requested by Sulzer Bingham representative. To shut down the pump, PRESS the OFF key on VSD-1 keypad OR the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A. Mg 12/19/197  7.23.a FULLY OPEN V-temp-Z per direction of Sulzer Bingham Representative (or testeng 7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  See Test Log Button of Speed and RUN LEDs are illuminated on VSD 1.  Test Engineer:  Test Engineer:  See Test Log Button on VSD 1.  Test Engineer:  Test Engineer:			7.21.2à		on MCS screer	PCU-2 for Booster
by Sulzer Bingham representative. To shut down the pump, PRESS the OFF key on VSD-1 keypad OR the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.  7.22 BEGIN data logging of the flow signal and the signal to the VSD.  7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A. Mat raling?  7.24 FULLY OPEN V-temp-Z par direction of Sulzer Bingham Representative (or testeng Test Engineer:  Test Engineer:  See Test Log Esting 3/31/98  7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.			7.21.3a			( 12 )
7.23 PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125A. Maj 12/11/97 7.23.a FULLY OPEN V-temp-Z per direction of Sulzer Bingham Representative (or testeng 7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  See Test Loa Estry 3/3/198 7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.			<del></del>			
P-3125A. Mag 12/17/97  7.23.a FULLY OPEN V-temp-Z per direction of Sulzer Bingham Representative (or testeng 7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  See Test Loa Estry 3/3/98  7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.	by Sulze	er Bi	ngham repres	sentative. To shut dow	n the pump, P	RESS the OFF key on
7.24 VERIFY locally that P-3125A is operating.  Test Engineer:  See test too estry 3/3/98  7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.	by Sulze VSD-1 ke	er Bi eypad	ngham repres	sentative. To shut dow P button on MCS screen	n the pump, P PCU-2 for Boo	RESS the OFF key on ster Pump P-3125A.
7.25 VERIFY the UP TO SPEED and RUN LEDs are illuminated on VSD 1.	by Sulze VSD-1 ke 7.	er Bi eypad 22	ngham represonable STOI  BEGIN data  PRESS the STOI  D. 21254	sentative. To shut down P button on MCS screen logging of the flow signary button on MCS screen raingles.	n the pump, P PCU-2 for Boo mal and the s een PCU-2 for	RESS the OFF key on ster Pump P-3125A.  ignal to the VSD.  Booster Pump
	by Sulze VSD-1 ke 7. 7. 7.23	er Bieypad 22 23	PRESS the STOPEN VERIFY local	sentative. To shut down P button on MCS screen logging of the flow signal TART button on MCS screen related to the flow of the	on the pump, PPCU-2 for Boomen and the seen PCU-2 for Sulzer Bingham PCS Tes	RESS the OFF key on ster Pump P-3125A.  ignal to the VSD.  Booster Pump  Representative (or lester
	by Sulze VSD-1 ke 7. 7. 7.23 7.	er Bieypad  22  23  .a.  .a.  .a.  .a.  .a.  .a.	ngham representation of the STOI BEGIN data  PRESS the SP-3125A. MARIEY OPEN VICENTY local  VERIFY local  VERIFY the I	sentative. To shut down P button on MCS screen logging of the flow signal TART button on MCS screen TART button on MCS screen respectively of the flow	on the pump, P PCU-2 for Boo gnal and the s een PCU-2 for Exclar Bingham erating. Et Engineer: Os are illumin	RESS the OFF key on ster Pump P-3125A.  ignal to the VSD.  Booster Pump  Representative (or lestent Engineer:

SI-3125A FI-temp-1

FIC-3125

PI-3125A

7.26.1 Motor speed

7.26.4 Pump inlet pressure

7.26.2 Flow rate

7.26.3 Flow rate

GPM

**GPM** 

<u>306</u> psig

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 64 OF 132 REVISION NO. <u>0-A</u> ATTACHMENT A PI-3125C = 30/psiq7.26.5 Pump discharge pressure Test Engineer: <u>9.1.</u> 2/3/98 7.27 VERIFY START ENERGIZED and ON are illuminated on MCS screen PCU-2 for Booster Pump P-3125A. Test Engineer: 94, 2/13/98 7.28 After flow rate as read from FIC-3125 stabilizes, STOP data logging of the flow signal and the signal to the VSD. Test Engineer: Record data from VSD-1 7.29 Use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities on VSD-1 keypad. the RIGHT arrow as required. RECORD the following data: 7.29.1 Motor Freq <u>29.5</u> Hz 7.29.9 Load CA Volts \_**230** V 7.29.10 Line A Amps \_\_\_\_64 A 7.29.2 Motor Speed \_ **49.2** % 7.29.2 Motor Speed 47.2 %
7.29.3 Motor RPM 1270 RPM
7.29.4 Load A Amps 90 Amps
7.29.5 Load B Amps 92 Amps
7.29.6 Load C Amps 90 Amps 7.29.11 Line B Amps \_\_\_\_ 7.29.12 Line C Amps \_\_\_\_ 65 A 7.29.13 Line AB Volts 48 V 490 V 7.29.14 Line BC Volts \_ 7.29.7 Load AB Volts 232 Volts 7.29.15 Line CA Volts \_ 7.29.8 Load BC Volts 230 Volts 7.29.16 Power 25 KWatts Test Engineer: Ol 43/98 7.30 **RECORD** pump and system data on an Appendix G Data Sheet Test Engineer: 7.31 IF during this POTP the audible noise from the motor is excessive (i.e. operating at VSD PWM inverter resonant frequency), adjust the carrier frequency on VSD-1 to minimize audible noise per manufacturer's instructions (VI # 22798, Supplement 40). Test Engineer: \_\_\_\_り…必 7.32 ALLOW pump P-3125A to run for 10 more minutes, THEN RECORD pump and system data on an Appendix G Data Sheet

Test Engineer: D. H. z/s/98

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 65 OF 132

REVISION NO. 0

ATTACHMENT A

	ump operating speed to 60% of full speed
7.33	DECREASE VSD-1 ramp-up time (to aid in determination of PID values) per the following steps. SET $128 \sim \rho$ to 60 (ISECO.
	7 33 1 PRESS the PROGRAM key on VSD 1 keypad.
H.	7.33.2 SELECT PARAM and PRESS the ENTER key.
18/98 18/98 1857	7.33.3 SCROLL thru the list of drive parameters using the UP and DOWN arrows until ACCEL TIME is shown.
rest rohang	7 <del>.33.4 SELECT 1 (i.e. 1 second) and PRESS the ENTER key.</del> Test Engineer:
Kr 1	_7.33.5 PRESS the MONITOR key on VSD-1 keypadTest_Engineer:
7.34	BEGIN data logging of the flow signal and the signal to the VSD.
,	SET Fluid FLOW (SP) to 144 gpm (60% of full scale). (This corresponds to a pump speed of 2160 rpm; with the temporary flow control valve V-temp-2 fully open an actual flow of about 130 gpm is expected.)  Test Engineer:   SEE TEST LOG ENTRY 3/3/98  VERIFY the UP TO SPEED LED on VSD-1 turns off and then illuminates
18. 1.36.	a <del>gain once the new motor speed is achieved</del> .
2/13/98	Test Engineer:
7.37	After flow rate as read from FIC-3125 stabilizes, STOP data Note that a logging of the flow signal and the signal to the VSD.  Test Engineer:
7.38	RECORD the following data:
	7.38.1 Motor speed SI-3125A <u>20%</u> RPM

FIC-3125

PI-3125A

PI-3125C

Test Engineer:

HNF-2504, REV. 0 ATTACHMENT | PAGE/09

7.38.3 Flow rate

7.38.4 Pump inlet pressure

7.38.5 Pump discharge pressure

<u>\$3</u> psig **34)** psig

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 66 OF 132

REVISION NO. 0

ATTACHMENT A

7.39	Use the LINE	key and Pr	ogramming and	1 Monitoring	UP and	d DOWN	arrows
•	to toggle thr	u the disp	layable quant	cities on VS	D-1 kej	ypad.	Use
	the RIGHT arr	ow as requ	ired. RECOF	RD the follow	wing d	ata:	

7.39.1 Motor Freq 7.39.2 Motor Speed	<u>35.5</u> Hz 59.1 %
7.39.3 Motor RPM	2/30 RPM
7.39.4 Load A Amps	<u> 705</u> Amps
7.39.5 Load B Amps	<i>104</i> Amps
7.39.6 Load C Amps	<u>/02</u> Amps
7.39.7 Load AB Volts	<u>277</u> Volts
7.39.8 Load BC Volts	<u> 280</u> Volts
7.39.9 Load CA Volts	<u>276</u> Volts
7.39.10 Line A Amps	<u>65</u> Amps
7.39.11 Line B Amps	<b>65</b> _ Amps
7.39.12 Line C Amps	<u>62_</u> Amps
7.39.13 Line AB Volts	<u>4%</u> Volts
7.39.14 Line BC Volts	<b>566</b> Volts
7.39.15 Line CA Volts	<u>494</u> Volts
7.39.16 Power	Kilowatts <u>ک3</u>

Test Engineer: D. St 2/13/98

7.40 **RECORD** pump and system data on an Appendix G Data Sheet 1 2/3/18

Test Engineer:

7.41 ALLOW pump P-3125A to run for at least 10 more minutes, THEN RECORD pump and system data on an Appendix G Data Sheet  $\frac{9}{3}/\frac{3}{9}$ 

Increase pump operating speed to 70% of full speed

- 7.42 BEGIN data logging of the flow signal and the signal to the VSD.
- 7.43 SET Fluid FLOW (SP) to 168 gpm (70% of full scale). (This corresponds to a pump speed of 2520 rpm; with the temporary flow control valve V-temp-2 fully open an actual flow of about 150 gpm is expected.)

Test Engineer:  $\mathcal{D}.\mathcal{I}$ 

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 67 OF 132

REVISION NO. 0

ATTACHMENT A

7 <del>.44</del>	After flow rate as read from FIC-3125 stabilizes, STOP data NAA logging of the flow signal and the signal to the VSD.  Test Engineer:
7.45	RECORD the following data:
	7.45.1 Motor speed SI-3125A $\frac{2.475}{1.45.2}$ RPM 7.45.2 Flow rate FI-temp-1 $\frac{1.35}{1.45.3}$ GPM FIC-3125 $\frac{1.44}{1.45.4}$ GPM 7.45.4 Pump inlet pressure PI-3125A $\frac{9.3}{1.45.5}$ psig 7.45.5 Pump discharge pressure PI-3125C $\frac{9.3}{1.45.5}$ psig
	Test Engineer: DY 2/3/98
7.46	Use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities on VSD-1 keypad. Use the RIGHT arrow as required. RECORD the following data:
	7.46.1 Motor Freq 7.46.2 Motor Speed 7.46.3 Motor RPM 7.46.4 Load A Amps 7.46.5 Load B Amps 7.46.6 Load C Amps 7.46.7 Load AB Volts 7.46.8 Load BC Volts 7.46.9 Load CA Volts 7.46.10 Line A Amps 7.46.11 Line B Amps 7.46.12 Line C Amps 7.46.13 Line AB Volts 7.46.14 Line BC Volts 7.46.15 Line CA Volts 7.46.16 Power  Test Engineer:  7.46.1 Volts 7.46.16 Power  Test Engineer:  7.46.1 Volts 7.46.16 Power  Test Engineer:  7.46.1 Volts 7.46.16 Power  Test Engineer:
7.47	RECORD pump and system data on an Appendix G Data Sheet  Test Engineer:  1398
7.48	
HNF-2504, REV. 0	ATTACHMENT   PAGE   11

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 68 OF 132

REVISION NO. 0

ATTACHMENT A

Increase pump operating speed to 80% of full speed

- 7.49 BEGIN data logging of the flow signal and the signal to the VSD.
- 7.50 SET Fluid FLOW (SP) to 192 gpm (80% of full scale). (This corresponds to a pump speed of 2280 rpm; with the temporary flow control valve V-temp-2 fully open an actual flow of about 170 gpm is expected.)

  Test Engineer: DD. 2/13/98

rest Engineer. \_\_\_\_\_\_

7.51 After flow rate as read from FIC-3125 stabilizes, **STOP** data logging of the flow signal and the signal to the VSD.

Test Engineer:

H

7.52 **RECORD** the following data:

7.52.1 Motor speed		<u> 7837</u> RPM
7.52.2 Flow rate	FI-temp-1	<u> 158</u> GPM
7.52.3 Flow rate	FIC-3125	<u> 16                                   </u>
7.52.4 Pump inlet pressure		<u>35</u> psig
7.52.5 Pump discharge pressure	PI-3125C	<i>514</i> psig

71-31250 <u>377</u> psig

Test Engineer: D.St. 2/13/98

7.53 Use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities on VSD-1 keypad. Use the RIGHT arrow as required. **RECORD** the following data:

7.53.1 Motor Freq	<u>425</u> Hz
7.53.2 Motor Speed	<u> 79.1</u> %
7.53.3 Motor RPM	<u> 2850</u> RPM
7.53.4 Load A Amps	/ <b>52</b> Amps
7.53.5 Load B Amps	<u> 152</u> Amps
7.53.6 Load C Amps	<u>/5</u> ኒ Amps
7.53.7 Load AB Volts	_ <i>346</i> _ Volts
7.53.8 Load BC Volts	_ <b>340</b> _ Volts
7.53.9 Load CA Volts	<u> <b>340</b></u> Volts
7.53.10 Line A Amps	<u> 152</u> Amps
7.53.11 Line B Amps	<u></u>
7.53.12 Line C Amps	<i>151</i> Amps
7.53.13 Line AB Volts	<b>49)</b> Volts
7.53.14 Line BC Volts	<b>S</b> Volts

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST
HNF-1857 PAGE 69 OF 132

REVISION	NO.	_0_
----------	-----	-----

ATTACHMENT A

		7.53.15 Line CA Volts 7.53.16 Power  495 Volts 7.53.16 Power  Kilowatts
		Test Engineer: D. y 3/13/98
		<b>RECORD</b> pump and system data on an Appendix G Data Sheet  Test Engineer: $Q_{ij} = \frac{2}{100} \frac{1}{900}$
		ALLOW pump P-3125A to run for at least 10 more minutes, THEN DUE 70 RECORD pump and system data on an Appendix G Data Sheet
	DATA	OBTAINED IN STEP 7.54 IS BOAQUATE FOR THIS PUMP S
		RECORD the instrument air flow rate to the pump seals per the flow indicators on the pump seal control panels:
		7.56.1 FI-3125A1 0 scfh@126562 correction FACTON 3.0 7.56.2 FI-3125A2 0.1 scfh@130160  Test Engineer: 99 2/13/98
Stop	P-3125	A .
	7.57	PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.
	7.58	VERIFY locally that P-3125A has stopped.  Test Engineer: $\frac{2}{\sqrt{3/98}}$
	7.59	VERIFY ENABLE ENERGIZED and OFF are illuminated on MCS screen PCU-2 for Booster Pump P-3125A.  Test Engineer: 2/13/9#
	7.60	VERIFY the UP TO SPEED and RUN LEDs are no longer illuminated on VSD-1.  Test Engineer:
	7.61	CLOSE flow control valve V-temp-2  Test Engineer: 9 1/3/98
	7.62	CLOSE V-temp-1 Test Engineer: $\frac{D.H.}{D.J.} \frac{2J/9E}{JJ/9E}$

HNF-2504, REV. 0 ATTACHMENT | PAGE 13

7.63 TURN OFF supply pump.

REVISION NO. 0

#### 8.0 Booster Pump P-3125B Startup Test

This section verifies initial startup and operation of the installed pump. The booster pump will be operated remotely from the MCS in PID MANUAL mode, under control of input motor speed. Operating speeds are selected for the purpose of determining the appropriate PID (Proportional, Integral,

Derivative)	values for flow control.
	e of a vendor representative from Panametrics Flowmeters is very but not absolutely required for this portion of the test.
8.1	VERIFY temporary water supply tank is sufficiently full of water to perform this test.  Test Engineer: $\Theta.\mathcal{Y}$ , $2/17/98$
	tee was used on the supply jumper between V-temp-1 and the Hiltaps and SLL-3164, then N/A the next two steps (and substeps).
8.2	MOVE the water supply feed from P-3125A to P-3125B as follows:
	8.2.1 CLOSE SOV-3125C. Test Engineer: $9.9 \frac{1}{10/98}$
	8.2.2 <b>VERIFY</b> SOV-3125D is CLOSED.  Test Engineer:   2/n/98
	8.2.3 <b>REMOVE</b> supply jumper from Hiltap connector nearest SOV-3125E on transfer line SLL-3163. <b>ATTEMPT</b> to keep as little water as possible from leaking out of the supply jumper during the move.
(	8.2.4 IMMEDIATELY REINSTALL Hiltap connector cap securely. N/A Test Engineer:
	8.2.5 <b>REMOVE</b> cap from Hiltap connector nearest SOV-3125G on

- 3164. AllEMP1 to keep as little water as possible leaking out of the transfer line during the move.
- 8.2.6 IMMEDIATELY CONNECT supply jumper securely to the Hiltap connector. Test Engineer:

ATTACHMENT I PAGE 9,9 417 /g & HNF-2504, REV. 0

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 71 OF 132

REVISION NO. 0

ATTACHMENT A

ulate water thru pump P-3125B vo ft inside pump or supply line d	ent valve to sweep out any air ue to moving the supply jumper.
CIRCULATE water as follows:	•
8.3.1 OPEN valve V-temp-1.	Test Engineer: $9.9 \frac{2}{1}/96$
8.3.2 CLOSE pressure control	valve on the supply jumper assembly.
8.3.3 TURN ON supply pump.	
8.3.4 OPEN SOV-3125D from the	MCS. Test Engineer: $0.11. z/n/98$
8.3.5 <b>OPEN</b> flow control valve	Test Engineer: B. 9. 9. 11/58
8.3.6 After circulating for a SOV-3125D and THEN OPEN	pproximately 10 minutes, <del>CLOSE</del> DY 2/17/98  pump vent valve MOV-3125BK.  Test Engineer: <u>DY 2/17/98</u>
8.3.7 After approximately 10 m	minutes, CLOSE V-temp-2. <u>り. 外. 火ッ/</u> 58 Test Engineer:
8.3.8 <b>CLOSE</b> MOV-3125BK.	Test Engineer: 9.9. 2/1/98
8.3.9 CLOSE valve V-temp-1.	Test Engineer: D. S. 2/17/98
8.3.10 TURN OFF supply p	ump.
present. Gla 12/20/07	m Sulzer Bingham pump company is
	Test Engineer: 9.9. 7/158
PRESS REMOTE and AUTO on VSD- "BUMP" PUMP TREMUSED CONT AND TO VALIDATE LOCAL	2 keypad.  Test Engineer: D. H. 2/11/96  ROL PANEL TO VERIFY PROPER ROTATION  19.9.2.2/1/
TACHMENT   BAGE TEOR LEAVE	RETEST 020 - 31259 CUSE 85 OF 150 9 9 2/7/2
	CIRCULATE water as follows:  8.3.1 OPEN valve V-temp-1.  8.3.2 CLOSE pressure control  8.3.3 TURN ON supply pump.  8.3.4 OPEN SOV-3125D from the  8.3.5 OPEN flow control valve  8.3.6 After circulating for a SOV-3125D and THEN OPEN  8.3.7 After approximately 10  8.3.8 CLOSE MOV-3125BK.  8.3.9 CLOSE valve V-temp-1.  8.3.10 TURN OFF supply p  The vendor representative fro present. SOV 3125G; D  PRESS REMOTE and ANTO on VSD-

PREOPERA	TIONAL T	EST POTP-0	07, CROSS SIT	E TRANSFER SY	STEM INTEGRAT	ED TEST 72 OF 132
REVISION NO	0_		ATTACHMENT	Α	1702	72 0. 102
8.6			RGIZED, REMO Booster Pump		re illuminated er: <b>D.X</b>	on MCS 2/17/96
Select <del>50%</del>	speed as	first ope	erating point.			
D.Y. 8.7.1 2/149x	SET U	D RAM	0 TO 12 (55 168	Test Enginee	ster Pump P-31 er: عند ا scale). (Th	<u> </u>
	corresp	onds to a valve V-t	pump speed of	1 <del>800</del> rpm; wi	ith the temporal flow of abour	ary flow '

NOTE: Valves previously "forced" to a position on the MCS for purposes of this test should not be shown as valve positioning failures because the associated valve failure alarms are jumpered out per Section 4.0.

8.10 **VERIFY** Alarm Table on MCS shows no valve positioning failures.

Test Engineer: 9.9. 2/15/98

Test Engineer:

8.11 SELECT the Transfer Sequencing INITIATE Button.

SELECT the Transfer Sequencing RESET button.

NOTE: Transfer Scheme 2B sets up for transfer of slurry from the 241-SY-B valve pit to the 241-A-A valve pit.

- 8.12 **SELECT** the Transfer Sequencing **TYPE 2B** transfer button.
- 8.13 **VERIFY** proper valve position in accordance with Appendix F-2 Data Sheet.

  Test Engineer:

NOTE: The boxes on the MCS overview screen that denote PCU-1 thru PCU-5 indicate status of the transfer path. All boxes GRAY and paths GREEN indicates that the transfer path is ready for use. Boxes filled in RED indicates that an alarm associated with the transfer is activated (i.e. mispositioned valve, leak detected, etc). The booster pump will not start unless associated alarms are either cleared or over-ridden.

8.9

PREOPERA REVISION NO	FIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 73 OF 132 . 0 ATTACHMENT A
8.14	IF any of the boxes on the MCS overview screen which denote PCU-1 thru PCU-5 are highlighted in RED, <b>DETERMINE</b> the reason why and perform one of the following:
	Disposition the problem by fixing it and clearing alarm, or by overriding the alarm IF the Test Engineer determines that the problem will not affect the performance of this test. RECORD disposition on the Test Log or on a Test Exception Sheet, at the discretion of the Test Engineer. N/A this step if not performed.  Test Engineer:
	VERIFY the boxes on the MCS overview screen which denote PCU-1 thru PCU-5 are highlighted in GRAY, unless a RED box has been determined to be acceptable per the previous step.  Test Engineer:
1	OPEN SOV-3125G and SOV-3125D from the MCS.  Test Engineer:
Set booster	pump inlet pressure control
8.17	ADJUST pressure control valve on the supply jumper assembly to an arbitrary OPEN position.
8.18	TURN ON supply pump.
8.19	VERIFY water is being recirculated to holding tank.  Test Engineer:     D. St 2/17/98
8.20	ADJUST pressure control valve on the supply jumper assembly so that the pressure indicator at the supply pump discharge reads approximately 50 psi
	8.20.1 PI-temp-1 62 psig  Test Engineer: 8.21 3/1/90

8.21 **OPEN** valve V-temp-1.

Test Engineer: 🖰 🗗 🗸 🗸 🗸 🗸

		·
		POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 74 OF 132
REVISION NO	<u>0-A</u> .	ATTACHMENT A
		dax 12/17/97
8.22	<del>-FULLY</del> OPEN	flow control valve V-temp-2. Approx 1/8 OPEN.  Test Engineer: D. 2/11/98
See NOTE	AFTER Stop 7:	20 (page 77 of 150),
Prepare to	start P-3125	BB .
8.23	NOTIFY Sulz	er Bingham representative that the booster pump is to
	be started.	
		Test Engineer: D.M. //7/98
8.23a	"BUMP" the	motor to verify proper rotation direction as follows:
	8.23.1a	PRESS the START button on MCS screen PCU-2 for Booster Pump P-3125B.
	8.23.2a	PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125B.
	8.23.3a	VERIFY motor shaft rotated in proper direction.  Test Engineer:
		•
by Sulzer B	ingham repre	to immediately shut down booster pump if so requested esentative. To shut down the pump, PRESS the OFF key on DP button on MCS screen PCU-2 for Booster Pump P-3125B.
8.24	BEGIN datal	ogging of the flow signal and the signal to the VSD.
J		
8.25	D_2125R #4	START button on MCS screen PCU-2 for Booster Pump
8.25,a	FULLY OPEN (	1-temp-2 per direction of Sulzer Bingham representative for test enginee
8.26	VERIFY loca	Test Engineer: P. 9 2/17/98
l <sub>A</sub>	SEE TEST L	04 EPTMY 3/31/98 UP TO SPEED and RUN LEDS are illuminated on VSD-2.
1.2/98-8.27	VERIFY the	UP-TO SPEED and RUN LEDs are illuminated on VSD-2.

8.28.1 Motor speed

8.28.1 Motor speed

8.28.2 RECORD the following data:

8.28.1 Motor speed

8.28.1 Motor speed

8.28.2 RECORD the following data:

8.28.1 Motor speed SI-3125B 18.28.2 Flow rate SI-3125B 18.28.3 GPM SI-3125B SI-3125B

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 75 OF 132 HNF-1857

REVISION	NO.	<u>0-A</u>
----------	-----	------------

REVISION NO.	. <u>U-A</u> ATTACHMENT A
	8.28.5 Pump discharge pressure PI-3125D $300$ psig Test Engineer: $9.9.2/19/98$
	Test Engineer: 4.2. 119198
8.29	VERIFY START ENERGIZED and ON are illuminated on MCS screen PCU-2 for Booster Pump P-3125B.  Test Engineer: D. J. 7/19/98
8.30	After flow rate as read from FIC-3125 stabilizes, STOP datalogging of the flow signal and the signal to the VSD.  Test Engineer: $9.9 \frac{2/9}{9}$
Record data	from VSD-2
8.31	Use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities on VSD-2 keypad. Use the RIGHT arrow as required. RECORD the following data:
	8.31.1 Motor Freq 30 Hz 7.29.9 Load CA Volts 235 V 8.31.2 Motor Speed 50 % 7.29.10 Line A Amps 30 A 8.31.3 Motor RPM 1802 RPM 7.29.11 Line B Amps 35 A 8.31.4 Load A Amps 90 Amps 7.29.12 Line C Amps 35 A 8.31.5 Load B Amps 90 Amps 7.29.13 Line AB Volts 492 V 8.31.6 Load C Amps 90 Amps 7.29.14 Line BC Volts 496 V 8.31.7 Load AB Volts 243 Volts 7.29.15 Line CA Volts 482 V 8.31.8 Load BC Volts 240 Volts 7.29.16 Power 24 KWatts
	Test Engineer: D. D. 3/19/98
8.32	RECORD pump and system data on an Appendix G Data Sheet 2/19/98  Test Engineer:
8.33	ALLOW pump P-3125B to run for 10 more minutes, THEN RECORD pump and system data on an Appendix G Data Sheet Test Engineer: $\frac{2}{99/98}$
Thomas a num	mn operating speed to 60% of full speed

8.34 DECREASE VSD-2 ramp-up time (to aid in determination of PID values) per the following steps. SET RAMP TO 60(1 SECOND) AT PLE PRESS the PROGRAM key on VSD-2 keypad

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 76 OF 132

REVISION NO. <u>0-A</u>

ATTACHMENT A

Ν	-8.34.2 SELECT PARAM and PRES	S-the ENTER key.
2/18/98	8.34.3 SCROLL thru the list and DOWN arrows until	of drive parameters using the UP ACCEL TIME is shown:
2/18/98		nd) and PRESS the ENTER key. st Engineer:
8 <del>.35</del> .	PRESS the MONITOR key on VSD-2 ke Te	<del>ypad.</del> st Engineer:
8,36	BEGIN datalogging of the flow sig	nal and the signal to the VSD.
8.37 P. 9. 8.38 V 19/98	SEE TEST LOG ENTRY 3/3//9D  VERIFY the UP TO SPEED LED on VSD  again once the new motor speed is	60 rpm; with the temporary flow an actual flow of about 130 gpm st Engineer: Declarate 2/19/9
8.39	After flow rate as read from FIC- of the flow signal and the signal Te	
8.40	RECORD the following data:	·
`	8.40.1 Motor speed 8.40.2 Flow rate 8.40.3 Flow rate 8.40.4 Pump inlet pressure 8.40.5 Pump discharge pressure	SI-3125B

Test Engineer: D. y 2/19/98

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 77 OF 132 REVISION NO. 0 ATTACHMENT A

8.41 Use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities on VSD-2 keypad. Use the RIGHT arrow as required. RECORD the following data:

Test Engineer: Del 2/19/98

8.43 ALLOW pump P-3125B to run for at least 10 more minutes, THEN RECORD pump and system data on an Appendix G Data Sheet Test Engineer:

Increase pump operating speed to 70% of full speed

- 8.44 BEGIN datalogging of the flow signal and the signal to the VSD.
- 8.45 SET Fluid FLOW (SP) to 168 gpm (70% of full scale). (This corresponds to a pump speed of 2520 rpm; with the temporary flow control valve V-temp-2 fully open an actual flow of about 150 gpm is expected.)

Test Engineer: 19 9 19 19

PREOPERATIONAL	TEST			TRANSFER	SYSTEM				
		HNF-189	57			PAGE	78	UF	13
		 <del></del> • • • 1140							

PREUPERA EVISION NO	TIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST  HNF-1857 PAGE 78 OF 133 0_ ATTACHMENT A
8.46	After flow rate as read from FIC-3125 stabilizes, STOP datalogging of the flow signal and the signal to the VSD.  Test Engineer:
8.47	RECORD the following data:
	8.47.1 Motor speed SI-3125B $\frac{2560}{10}$ RPM 8.47.2 Flow rate FI-temp-1 $\frac{110}{10}$ GPM 8.47.3 Flow rate FIC-3125 $\frac{10}{50}$ GPM 8.47.4 Pump inlet pressure PI-3125B $\frac{56}{522}$ psig 8.47.5 Pump discharge pressure PI-3125D $\frac{522}{522}$ psig
8.48	Use the LINE key and Programming and Monitoring UP and DOWN arrow to toggle thru the displayable quantities on VSD-2 keypad. Use the RIGHT arrow as required. RECORD the following data:
	8.48.1 Motor Freq 8.48.2 Motor Speed 8.48.3 Motor RPM 8.48.4 Load A Amps 8.48.5 Load B Amps 8.48.6 Load C Amps 8.48.7 Load AB Volts 8.48.8 Load BC Volts 8.48.9 Load CA Volts 8.48.10 Line A Amps 8.48.11 Line B Amps 8.48.12 Line C Amps 8.48.13 Line AB Volts 8.48.14 Line BC Volts 8.48.15 Line CA Volts 8.48.15 Line CA Volts 8.48.16 Power   42 Hz 20 % 2520 RPM 1/8 Amps 1/2 Amps 22 Volts 328 Volts 327 Volts 328 Volts 329 Volts 48.19 Line C Amps 80
	Test Engineer:
8.49	RECORD pump and system data on an Appendix G Data Sheet 2/19/98

8.50 ALLOW pump P-3125B to run for at least 10 more minutes, THEN RECORD pump and system data on an Appendix G Data Sheet 2 Test Engineer: 9.9

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 79 OF 132

REVISION NO. 0

ATTACHMENT A

Increase pump operating speed to 80% of full speed

- 8.51 **BEGIN** datalogging of the flow signal and the signal to the VSD.
- 8.52 SET Fluid FLOW (SP) to 192 gpm (80% of full scale). (This corresponds to a pump speed of 2280 rpm; with the temporary flow control valve V-temp-2 fully open an actual flow of about 170 gpm is expected.)

  Test Engineer: 9. 2/19/90
- 8.53 After flow rate as read from FIC-3125 stabilizes, STOP datalogging of the flow signal and the signal to the VSD.

  Test Engineer: 2/19/98
- 8.54 **RECORD** the following data:

8.54.1 Motor speed	SI-3125B	29 <i>15</i> RPM
8.54.2 Flow rate	FI-temp-1	<u>_/2O</u> _ GPM
8.54.3 Flow rate	FIC-3125	123 GPM
8.54.4 Pump inlet pressure	PI-3125B	<u><b>51</b></u> psig
8.54.5 Pump discharge pressure	PI-3125D	<u>673</u> psig

Test Engineer: D9. 2/18/88

8.55 Use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities on VSD-2 keypad. Use the RIGHT arrow as required. RECORD the following data:

O FF 1 Matau France	48 11-	
8.55.1 Motor Freq	<u>48</u> Hz	
8.55.2 Motor Speed	<u>_79.9</u> %	
8.55.3 Motor RPM		
8.55.4 Load A Amps	<i>140</i> Amps	, ,
8.55.5 Load B Amps	<i>140</i> Amps	publes
8.55.6 Load C Amps	<i>139</i> _Amps	r
8.55.7 Load AB Volts	<u>384</u> Volts	
8.55.8 Load BC Volts	<u> 323</u> Volts	
8.55.9 Load CA Volts	<u> 323</u> Volts	
8.55.10 Line A Amps	<u></u>	
8.55.11 Line B Amps	Amps	
8.55.12 Line C Amps		
8.55.13 Line AB Volts	<b>493</b> Volts	
8.55.14 Line BC Volts	<u>496</u> Volts	

DDFODEDA	FIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST
REVISION NO	HNF-1857 PAGE 80 OF 132
	8.55.15 Line CA Volts
	Test Engineer: <u>D. 9 2/19/9K</u>
8.56	RECORD pump and system data on an Appendix G Data Sheet $2/19/58$ Test Engineer:
	ALLOW pump P-3125B to run for at least 10 more minutes, THEN RECORD pump and system data on an Appendix G Data Sheet $g$ .  Test Engineer:
	RECORD the instrument air flow rate to the pump seals per the flow indicators on the pump seal control panels:
	8.58.1 FI-3125B1 scfh @ 125 PS14 } connection Factor 3.0 8.58.2 FI-3125B2 o scfh @ 124 PS15 }  Test Engineer: D. D.
Stop P-3125E	3
8.59	PRESS the STOP button on MCS screen PCU-2 for Booster Pump P-3125B.
8.60	VERIFY locally that P-3125B has stopped.  Test Engineer: 9.9. 2/19/98
8.61	VERIFY ENABLE ENERGIZED and OFF are illuminated on MCS screen PCU-2 for Booster Pump P-3125B.  Test Engineer:
8.62	VERIFY the UP TO SPEED and RUN LEDs are no longer illuminated on VSD-2.  Test Engineer:

8.65 **TURN OFF** supply pump.

8.64 CLOSE V-temp-1

8.63 CLOSE flow control valve V-temp-2
Test Engineer:

REVISION NO. 0

ATTACHMENT A

#### 9.0 Booster Pump P-3125A Testing Using Flow Control

This section tests remote operation of P-3125A with pump speed control via the system flowmeter. Operation will be tested at three flows and three back pressures for a total of nine operating points.

NOTE: If a tee was used on the supply jumper between V-temp-1 and the Hiltaps on SLL-3163 and SLL-3164, then N/A the following two steps (and substeps).

N/p	9.1	MOVE the water supply feed from P-3125B to P-3125A as follows:
		9.1.1 CLOSE SOV-3125D.  Test Engineer:
		9.1.2 <b>VERIFY</b> SOV-3125C is CLOSED.  Test Engineer:
		9.1.3 <b>REMOVE</b> supply jumper from Hiltap connector nearest SOV-31256 on transfer line SLL-3164. <b>ATTEMPT</b> to keep as little water as possible from leaking out of the supply jumper during the move.
		9.1.4 IMMEDIATELY REINSTALL Hiltap connector cap securely.  Test Engineer:
		9.1.5 <b>REMOVE</b> cap from Hiltap connector nearest SOV-3125E on SLL-3163. <b>ATTEMPT</b> to keep as little water as possible from leaking out of the transfer line during the move.

9.1.6 IMMEDIATELY CONNECT supply jumper securely to the Hiltap connector.

See rest Loh to the Z/13/98 Def z/26/98 crulate water thru pump P-3125A vent valve to sweep out any air

NOTE: Circulate water thru pump P-3125A vent valve to sweep out any air pockets left inside pump or supply line due to moving the supply jumper.

- 9.2 **CIRCULATE** water as follows:
  - 9.2.1 OPEN valve V-temp-1.

Test Engineer: D. 9 /26/98

9.2.2 CLOSE pressure control valve on the supply jumper assembly.

#### PREOPERATIONAL TEST POTP-007. CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 82 OF 132 HNF-1857

REVISION NO. 0

ATTACHMENT A

9.2.3 TURN ON	supply	pump.
---------------	--------	-------

9.2.4 OPEN SOV-3125C from the MCS.

Test Engineer: <u>D.9.</u> 2/26/98

9.2.5 OPEN flow control valve V-temp-2.

Test Engineer: Dy 2/26/91

9.2.6 After circulating for approximately 5 minutes, CLOSE SOV-3125C and THEN OPEN pump vent valve MOV-3125AK.

Test Engineer: \_\_\_\_

9.2.7 After approximately 5 minutes, CLOSE V-temp-2.

Test Engineer: 9.9.2/26/98

9.2.8 CLOSE MOV-3125AK.

Test Engineer: 19.9. 2/26/98

9.2.9 CLOSE valve V-temp-1.

Test Engineer: D. D. 2/26/94

9.2.10 TURN OFF supply pump.

VERIFY ENABLE ENERGIZED. REMOTE, and OFF are illuminated on MCS 9.3 screen PCU-2 for Booster Pump P-3125A.

Test Engineer: \_

SELECT PID AUTO on MCS screen PCU-2 for Booster Pump\_Pz3125A. 9.4 

NOTE: Test Engineer will determine optimum PID settings by analyzing the contents of the datalogger from the PID MAN testing. TEST ENGINEER MAY RETUNE PID SETTINGS AS REQUIRED DURING THIS TEST.

SET PID-flow parameters for Booster Pump P-3125A to the values 9.5 determined by the Test Engineer:

$$P = 0.9$$

$$I = 06$$

$$D = 0$$
1/sec

Test Engineer: A D 2/16/18

PREOPERATIO	DNAL 7	TEST	POTP-007,	CROSS	SITE	TRANSFER	SYSTEM	INTEGRATE	D	TEST	Γ
			1	HNF - 185	57			PAGE	83	0F	132
REVISION NO	0_		A <sup>-</sup>	TTACHME	ENT A						

9.6 SET Fluid Flow Set Point value to 104 gpm. Test Engineer: D.9 2/26/94

NOTE: Test Engineer will supply rate of acceleration and deceleration that the variable speed drive VSD-1 will implement for all increases/decreases in speed setpoint, and rate-of-change (ramp) limit(s) for the control signal logic in the PCU.

9.7 SET the rate-of-change (ramp) limit(s) in the control signal logic in the PCU for P-3125A, per Test Engineer's direction. RECORD value below. N/A if not performed.

PCU ramp limit = 60 Test Engineer: D. y 2/26/98

SET ACCEL TIME and DECEL TIME parameters on VSD-1 per direction of 9.8 the Test Engineer and to the values determined by the Test Engineer. RECORD values below. N/A if not performed.

ACCEL TIME =  $\frac{10}{20}$ 60 Decel TIME =  $\frac{10}{20}$ 60

Test Engineer:  $9.91^{2}/16/98$ RESET button. Test Engineer:  $9.91^{2}/16/98$ 9.9 SELECT the Transfer Sequencing RESET button. Test Engineer: \_

NOTE: Valves previously "forced" to a position on the MCS for purposes of this test should not be shown as valve positioning failures because the associated valve failure alarms are jumpered out per Section 4.0.

- 9.10 **VERIFY** Alarm Table on MCS shows no valve positioning failures.
- 9.11 **SELECT** the Transfer Sequencing **INITIATE** Button.

NOTE: Transfer Scheme 2A sets up for transfer of slurry from the 241-SY-B valve pit to the 241-A-A valve pit.

9.12 SELECT the Transfer Sequencing TYPE 2A transfer button
Test Engineer: 9.12 Yelge

PREOPERATIONAL	TEST	POTP-007,	CROSS	SITE	TRANSFER	SYSTEM	INTEGRATE	:D	TEST	Ī
		ŀ	HNF - 185	57			PAGE	84	0F	132

REVISION NO. 0

ATTACHMENT A

9.13 **VERIFY** proper valve position in accordance with Appendix F-3 Data Sheet. Test Engineer: \_ D. St. 2/26/98

NOTE: The boxes on the MCS overview screen that denote PCU-1 thru PCU-5 indicate status of the transfer path. All boxes GRAY and paths GREEN indicates that the transfer path is ready for use. Boxes filled in RED indicates that an alarm associated with the transfer is activated (i.e. mispositioned valve, leak detected, etc). The booster pump will not start unless associated alarms are either cleared or over-ridden.

- 9.14 IF any of the boxes on the MCS overview screen which denote PCU-1 thru PCU-5 are highlighted in RED, DETERMINE the reason why and perform one of the following:
  - 9.14.1 Disposition the problem by fixing it and clearing alarm, or by overriding the alarm IF the Test Engineer determines that the problem will not affect the performance of this test. RECORD disposition on the Test Log or on a Test Exception Sheet, at the discretion of the Test Engineer. N/A this step if not performed.

Test Engineer: \_ N/A

9.15 **VERIFY** the boxes on the MCS overview screen which denote PCU-1 thru PCU-5 are highlighted in GRAY, unless a RED box has been 

9.16 OPEN SOV-3125E and SOV-3125C from the MCS.

4 50V-3125G

rom the MCS. Test Engineer: D. y 2/2/9K

See 7est Loa E-1/2/98 2/3/98 9.17 ADJUST pressure control valve on the supply jumper assembly to an arbitrary OPEN position.

- 9.18 TURN ON supply pump.
- 9.19 ADJUST pressure control valve on the supply jumper assembly so that the pressure indicator at the supply pump discharge reads approximately 50 psi. २० याज्य

9.19.1 PI-temp-1

**62** psig

Test Engineer: 0.012/26/98

PREOPERA		CROSS SITE TRANSFER SYSTEM INTEGRATED TEST
REVISION NO		HNF-1857 PAGE 85 OF 132 TTACHMENT A
9.20	OPEN valve V-temp-1.	Test Engineer: D.J. 426/98
9.21	-FULLY OPEN flow conti	Test Engineer: D.J. 426/98  Sat 12/17/27  rol valve V-temp-2. Approx 1/2 open.  Test Engineer: 9-9 1/26/98
Prepare to	start P-3125A	
To shut dow	•	ately shut down booster pump if so requested. her the OFF key on VSD-1 keypad or STOP button A.
9.22	BEGIN datalogging of	the flow signal and the signal to the VSD.
9.23	PRESS the START butto P-3125A.	on on MCS screen PCU-2 for Booster Pump
<b>9.23.</b> 9.24	Fully open V-temp-z per VERIFY locally that f	P-3125A is operating. Test Engineer: D. 9 2/26/98 Test Engineer: D. 9 2/26/98
9.25	VERIFY START ENERGIZE for Booster Pump P-33	ED and ON are illuminated on MCS screen PCU-2 125A.  Test Engineer: 9.9 2/26/98
NOTE: If P-	3125A does not keep a	steady flow, perform the following step.
	exit PID AUTO and entinstructions and reco	FIC-3125 is oscillating more than 8 gpm, THEN ter PID MAN. Re-tune PID per Test Engineer's ord the new PID-flow settings below. N/A step
÷	P = 1/sec D = Sec	Test Engineer: D. H. 7/26/98  valve full open
Point #1, -1	o 9 <u>भ</u> ियाः 84 gpm, flow control v	valve full open  10 $\frac{9}{7}$ $\frac{2}{4}$ $\frac{1}{98}$ data. VERIFY FIC-3125 reads $\frac{194 \pm 8}{9}$ gpm  SI-3125A $\frac{1875}{104}$ RPM EL town 1 $\frac{194}{104}$ GPM
9.27	RECORD the following	data. VERIFY FIC-3125 reads 104 ± 8 gpm
	9.27.1 Motor speed 9.27.2 Flow rate	SI-3125A <u>/875</u> RPM FI-temp-1 <u>/04</u> GPM

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 86 OF 132

REVISION NO. 0

ATTACHMENT A

9.27.3 Flow rate FIC-3125 1/0 GPM 9.27.4 Pump inlet pressure PI-3125A 58 psig 9.27.5 Pump discharge pressure PI-3125C 23 psig

Test Engineer: D. St 2/26/8/8

9.28 On VSD-1 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data:

9.28.1 Motor Freq	<u>30.6</u> Hz
9.28.2 Motor Speed	<u> </u>
9.28.3 Motor RPM	<u>184/</u> RPM
9.28.4 Load A Amps	<u>'73</u> Amps
9.28.5 Load B Amps	<u>9/</u> Amps
9.28.6 Load C Amps	<u>92</u> Amps
9.28.7 Load AB Volts	<u>240</u> Volts
9.28.8 Load BC Volts	<u> 243</u> Volts
9.28.9 Load CA Volts	<u>294</u> Volts
9.28.10 Power	<u>2)</u> Kilowatts

Test Engineer: <u>0.9</u> 2/26/98

9.29 **RECORD** pump and system data on an Appendix G Data Sheet  $\frac{2}{16}$ 

9.30 ALLOW pump P-3125A to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix 9 Data Sheet Test Engineer:

CAUTION: Flow Control Valve V-temp-2 should never be fully closed while the booster pump is operating, to prevent "deadheading" of the booster pump. Deadheading (no flow) for a significant time could result in damage to the booster pump. Constant surveillance during this test is required.

110 54.726/98

Point #2, 104 gpm, increase back pressure on pump to verify flow control feedback increases pump motor speed and horsepower to meet the required flow.

9.31 THROTTLE flow control valve V-temp-2 to increase motor speed approximately 100 rpm per SI-3125A.

Test Engineer: 99 926/98

PREOPERA	ATIONAL TEST POTP-007, CROSS SITE HNF-1857	TRANSFER SYSTE	M INTEGRATED TEST PAGE 87 OF 132
REVISION NO		i	17.GE 07 01 13E
9.32	RECORD the following data. VER	IFY FIC-3125 re	ads 104 ± 15 gpm
·	9.32.1 Motor speed 9.32.2 Flow rate 9.32.3 Flow rate 9.32.4 Pump inlet pressure 9.32.5 Pump discharge pressure	SI-3125A FI-temp-1 FIC-3125 PI-3125A PI-3125C	1976 RPM 105 GPM 10 GPM 58 psig 302 psig
		Test Engineer: .	D. St 2/26/98
9.33	On VSD-1 keypad, use the LINE k UP and DOWN arrows to toggle th the RIGHT arrow as required.	ru the displaya	ble quantities. Use
	9.33.2 Motor Speed 9.33.3 Motor RPM 9.33.4 Load A Amps 9.33.5 Load B Amps 9.33.6 Load C Amps 9.33.7 Load AB Volts 9.33.8 Load BC Volts 9.33.9 Load CA Volts 252	Hz  RPM Amps Amps Amps Volts Volts Kilowatts	
		Test Engineer: .	D. St 2/26/98
9.34	RECORD pump and system data on	an Appendix G Da Test Engineer:	ata Sheet 7/26/98

9.35 ALLOW pump P-3125A to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix G Data Sheet
Test Engineer: 2/16/98

Point #3, 104 gpm, further increase in back pressure

9.36 THROTTLE flow control valve V-temp-2 to increase motor speed approximately 200 rpm per SI-3125A. (Back off rpm if cavitation is found to occur at the flow control valve) Test Engineer: \_

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 88 OF 132 HNF-1857

<b>REVISION</b>	NO.	0
-----------------	-----	---

EA1210	N NU.	. <u>U</u> ATTACHMENT A	<b>A</b> .
9	.37	RECORD the following data. VERIFY R	FIC-3125 reads 104 ± \$ gpm
		9.37.1 Motor speed 9.37.2 Flow rate 9.37.3 Flow rate 9.37.4 Pump inlet pressure 9.37.5 Pump discharge pressure	SI-3125A <u>21/0</u> RPM FI-temp-1 <u>/6/</u> GPM FIC-3125 <u>1/</u> GPM PI-3125A <u>59</u> psig PI-3125C <u>365</u> psig
		Test	Engineer: $9.4 \frac{3}{z/98}$
g	9.38	On VSD-1 keypad, use the LINE key an UP and DOWN arrows to toggle thru the RIGHT arrow as required. RECOM	he displayable quantities. Use
		9.38.1 Motor Freq 9.38.2 Motor Speed 9.38.3 Motor RPM 9.38.4 Load A Amps  2/30 Amps	M ips
		9.38.5 Load B Amps 9.38.6 Load C Amps 9.38.7 Load AB Volts 9.38.8 Load BC Volts 9.38.9 Load CA Volts 9.38.10 Power  2	ps lts lts
		Test	Engineer: $P = \frac{3}{2} \frac{3}{2} \frac{98}{98}$
g	9.39	RECORD pump and system data on an A Test	Appendix G Data Sheet. 3/2/97
Ç	9.40	ALLOW pump P-3125A to run for at le intervals, RECORD pump and system d Test	east 30 minutes. At 10 minute data on an Appendix G Data Sheet Engineer: D. 3/2/98
oint a	#4, 1	140 gpm, flow control valve full open	1
Ġ	9.41	FULLY OPEN flow control valve V-tem Test	np-2. t Engineer: <u>9.0 3/2/98</u>
9	9.42	SET Fluid Flow Set Point value to 1 Test	np-2. t Engineer: <u>9.0/3/2/96</u> 140 gpm. t Engineer: <u>9.0/3/2/9</u> 6

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 89 OF 132

<b>REVISION</b>	NO.	_0
-----------------	-----	----

ATTACHMENT A

9.43	RECORD	the	following	data.	VERIFY	FIC-3125	reads	140	<u>±</u>	7	gpm
------	--------	-----	-----------	-------	--------	----------	-------	-----	----------	---	-----

9.43.1 Motor speed	SI-3125A	2424 RPM
9.43.2 Flow rate	FI-temp-1	<u>/3/</u> GPM
9.43.3 Flow rate		<u> 140</u> GPM
9.43.4 Pump inlet pressure	PI-3125A	<u>42</u> psig
9.43.5 Pump discharge pressure	PI-3125C	415 psig

Test Engineer: **D.H** 3/2/98

9.44 On VSD-1 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data:

9.44.1 Motor Freq	<u>40.4</u> Hz
9.44.2 Motor Speed	<u> </u>
9.44.3 Motor RPM	<u>2422</u> RPM
9.44.4 Load A Amps	<u> 118</u> Amps
9.44.5 Load B Amps	<u> 176</u> Amps
9.44.6 Load C Amps	Amps
9.44.7 Load AB Volts	<u>3</u> 9 Volts
9.44.8 Load BC Volts	<u>3/4</u> Volts
9.44.9 Load CA Volts	315 Volts
9.44.10 Power	_ <i>54</i> _ Kilowatts

Test Engineer: 9.9.3/z/98

9.45 **RECORD** pump and system data on an Appendix G Data Sheet, 3/2/98

9.46 ALLOW pump P-3125A to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix G Data Sheet Test Engineer:

Point #5, 140 gpm, increase back pressure on pump to verify flow control feedback increases pump motor speed and horsepower to meet the required flow.

9.47 THROTTLE flow control valve V-temp-2 to increase motor speed approximately 100 rpm per SI-3125A. Test Engineer:  $2\sqrt{3/4}$ 

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 90 OF 132

REVISION NO. 0

ATTACHMENT A

9.48	RECORD	the following dat	a. <b>VERIFY</b>	FIC-3125 re	ads 140 ± 7 gpm
	9.48.2 9.48.3 9.48.4	Motor speed Flow rate Flow rate Pump inlet pressu Pump discharge pr		SI-3125A FI-temp-1 FIC-3125 PI-3125A PI-3125C	2529 RPM /3/ GPM /40 GPM 4) psig 458 psig
			Test	Engineer:	D.H 3/2/98
9.49	UP and		oggle thru t	he displaya	ing and Monitoring ble quantities. Use owing data:
	9.49.2 9.49.3 9.49.4 9.49.5 9.49.6 9.49.7 9.49.8	Motor Freq Motor Speed Motor RPM Load A Amps Load B Amps Load C Amps Load AB Volts Load BC Volts Load CA Volts ) Power	41.8 Hz 69.7 % 280) RF 123 Am 120 Am 121 Am 330 Vo 320 Vo 326 Vo	PM nps nps nps olts	
			Test	Engineer:	D. St 3/2/98
9.50	RECORD	pump and system d	lata on an A Test	appendix G D Engineer:	ata Sheet 3/2/98
9.51		•	and system o		tes. At 10 minute ppendix G Data Sheet 9.2) 3/2/98

Point #6, 140 gpm, further increase in back pressure

9.52 THROTTLE flow control valve V-temp-2 to increase motor speed approximately 200 rpm per SI-3125A. (Back off rpm if cavitation is found to occur at the flow control valve)

Test Engineer: \_

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 91 OF 132

REVISION NO. \_0\_

ATTACHMENT A

9.53	RECORD the following data. VERIFY FIC-3125 reads 140 ± 7 gpm
	9.53.1 Motor speed SI-3125A
	Test Engineer: D.J. 3/2/98
9.54	On VSD-1 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data:
	9.54.1 Motor Freq       45.1 Hz         9.54.2 Motor Speed       25.2 %         9.54.3 Motor RPM       2700 RPM         9.54.4 Load A Amps       13.5 Amps         9.54.5 Load B Amps       13.3 Amps         9.54.6 Load C Amps       13.3 Amps         9.54.7 Load AB Volts       345 Volts         9.54.8 Load BC Volts       345 Volts         9.54.9 Load CA Volts       348 Volts         9.54.10 Power       20 Kilowatts
	Test Engineer: $9.4.3/2/98$
9.55	RECORD pump and system data on an Appendix G Data Sheet.  Test Engineer: $8.9/3/2/98$
	ALLOW pump P-3125A to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix G Data Sheet Test Engineer:
	55 DD 3/198 60 gpm, flow control valve full open
9.57	
9.58	FULLY OPEN flow control valve V-temp-2.  Test Engineer:  155 D.9 $3/2/98$ SET Fluid Flow Set Point value to $\frac{160}{160}$ gpm.  Test Engineer:  Test Engineer:  D.9 $3/2/98$

PREOPERA REVISION NO	04 3/2/9
9.59	RECORD the following data. VERIFY FIC-3125 reads $\frac{160}{160} \pm 8$ gpm.,
	9.59.1 Motor speed       SI-3125A       2688 RPM         9.59.2 Flow rate       FI-temp-1       195 GPM         9.59.3 Flow rate       FIC-3125 J55 GPM         9.59.4 Pump inlet pressure       PI-3125A 42 psig         9.59.5 Pump discharge pressure       PI-3125C 490 psig
	Test Engineer: <u>O.Y.3/198</u>
9.60	On VSD-1 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data:
	9.60.1 Motor Freq       44.6 Hz         9.60.2 Motor Speed       74.4 %         9.60.3 Motor RPM       2674 RPM         9.60.4 Load A Amps       135 Amps         9.60.5 Load B Amps       133 Amps         9.60.6 Load C Amps       135 Amps         9.60.7 Load AB Volts       350 Volts         9.60.8 Load BC Volts       348 Volts         9.60.9 Load CA Volts       390 Volts         9.60.10 Power       72 Kilowatts
	Test Engineer: D. 9 3/2/98
9.61	<b>RECORD</b> pump and system data on an Appendix G Data Sheet. Test Engineer: $9.9/3/2/98$
	ALLOW pump P-3125A to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix G Data Sheet Test Engineer:
Point #8, 1	55 DH3/2/98 60 gpm, increase back pressure on pump to verify flow control creases pump motor speed and horsepower to meet the required flow.

9.63 THROTTLE flow control valve V-temp-2 to increase motor speed approximately 100 rpm per SI-3125A.

Test Engineer:

REVISION NO. 0

ATTACHMENT A

9.64	RECORD the following data. VER	953 کی RIFY FIC-3125 reads <del>160</del> ± 8
	9.64.1 Motor speed 9.64.2 Flow rate 9.64.3 Flow rate 9.64.4 Pump inlet pressure 9.64.5 Pump discharge pressure	SI-3125A
		Test Engineer: D. S.
9.65	On VSD-1 keypad, use the LINE k UP and DOWN arrows to toggle th the RIGHT arrow as required.	nru the displayable quantiti
	9.65.2 Motor Speed 9.65.3 Motor RPM 9.65.4 Load A Amps 9.65.5 Load B Amps 9.65.6 Load C Amps 9.65.7 Load AB Volts  7.5. 7.5. 7.5. 7.5. 7.5. 7.5. 7.5. 7.	Amps Amps Amps Volts Volts Volts Kilowatts
9.66	RECORD pump and system data on	Test Engineer: 9.9
9.00	NECOND pump and system data on	Test Engineer:
9.67	ALLOW pump P-3125A to run for a intervals, RECORD pump and syst	
	55 D <b>Y                                  </b>	<pre>c pressure</pre>
9.68	D. 8 3 / 198	cemp-2 to increase motor spe L25A. (Back off rpm if cavi

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 94 OF 132

REVISION NO. 0

ATTACHMENT A

9.69	RECORD the following data. VERIFY FIC-3125 reads 160 ± 8 gpm 7 8.4.
	9.69.1 Motor speed $SI-3125A$ $2845$ RPM $9.69.2$ Flow rate $FI-temp-1$ $142$ GPM $9.69.3$ Flow rate $FIC-3125$ $155$ GPM $9.69.4$ Pump inlet pressure $PI-3125A$ $42$ psig $9.69.5$ Pump discharge pressure $PI-3125C$ $523$ psig
	Test Engineer: <u>日.リ 3/2/98</u>
9.70	After flow rate as read from FIC-3125 stabilizes, STOP datalogging of the flow signal and the signal to the VSD.  Test Engineer: $9.9 3/2/98$
9.71	On VSD-1 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. <b>RECORD</b> the following data:
	9.71.1 Motor Freq 9.71.2 Motor Speed 78.5 % 9.71.3 Motor RPM 9.71.4 Load A Amps 9.71.5 Load B Amps 9.71.6 Load C Amps 9.71.7 Load AB Volts 9.71.8 Load BC Volts 9.71.9 Load CA Volts 9.71.10 Power  47./ Hz 2828 RPM 147 Amps 146 Amps 147 Amps 149 Amps 141 Amps 142 Volts 1342 Volts 1343 Volts 1343 Volts 1343 Volts 1343 Volts 1343 Volts 1344 Volts 1345 Volts 1345 Volts 1346 Volts 1347 Volts 1348 Vo
	Test Engineer: D.H 3/198
9.72	RECORD pump and system data on an Appendix G Data Sheet.  Test Engineer: 9.19 3/198
9.73	ALLOW pump P-3125A to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix G Data Sheet Test Engineer:
	·

Stop P-3125A

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 95 OF 132

REVISION NO. 0

ATTACHMENT A

9.74 RECORD final PID-flow parameters for Booster Pump P-3125A.

P = .60 I = .60 D = .60 1/sec sec

Test Engineer:  $9.9 \frac{3}{2/98}$ 

9.75 **PRESS** the STOP button on MCS screen PCU-2 for Booster Pump P-3125A.

9.76 **VERIFY** locally that P-3125A has stopped.

Test Engineer:

Q. J 3/2/98

9.77 VERIFY ENABLE ENERGIZED and OFF are illuminated on MCS screen PCU-2 for Booster Pump P-3125A.

Test Engineer: D. H. 3/2/98

9.78 CLOSE flow control valve V-temp-2

Test Engineer: Del 3/2/98

9.79 **CLOSE** V-temp-1

Test Engineer: D.J. 3/2/98

9.80 **TURN OFF** supply pump.

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 96 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

#### 10.0 Booster Pump P-3125B Testing Using Flow Control

This section tests remote operation of P-3125B with pump speed control via the system flowmeter. Operation will be tested at three flows and three back pressures for a total of nine operating points.

NOTE: If a tee was used on the supply jumper between V-temp-1 and the Hiltaps on SLL-3163 and SLL-3164, then N/A the following two steps (and substeps).

10.1 MOVE the water supply feed from P-3125A to P-3125B as follows:

10.1.1	CLOSE SOV-3125C. Test Engineer: $\frac{99/3/24/98}{24/98}$
10.1.2	VERIFY SOV-3125D is CLOSED.  Test Engineer: D9 / 3-24-98
10.1.3	REMOVE supply jumper from Hiltap connector nearest SOV-3125E on transfer line SLL-3163. ATTEMPT to keep as little water as possible from leaking out of the supply jumper during the move.
10.1.4	IMMEDIATELY REINSTALL Hiltap connector cap securely.  Test Engineer: 9.9.3-24-98
10.1.5	REMOVE cap from Hiltap connector nearest SOV-3125G on SLL-3164. ATTEMPT to keep as little water as possible from leaking out of the transfer line during the move.
10.1.6	IMMEDIATELY CONNECT supply jumper securely to the Hiltap connector.  Test Engineer: 9.2./3-29-98

NOTE: Circulate water thru pump P-3125B vent valve to sweep out any air pockets left inside pump or supply line due to moving the supply jumper.

10.2 CIRCULATE water as follows:

10.2.1 **OPEN** valve V-temp-1.

.. Test Engineer: <u>9.9/3-24-98</u>

	OPERATIONAL TES	T POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 97 OF 132 ATTACHMENT A
	10.2.2	CLOSE pressure control valve on the supply jumper assembly.
او	10.2.3	TURN ON supply pump.
129/98	10.2.3	OPEN SOV-3125D from the MCS.  Test Engineer: 9.9/3-24-98
	10.2.5	OPEN flow control valve V-temp-2.  Test Engineer: 9-9/3-24-98
	10.2.6	After circulating for approximately 5 minutes, CLOSE- $9^{3/24}$ SOV-3125D and THEN OPEN pump vent valve MOV-3125BK.  Test Engineer: $9.3/3-24-98$
	10.2.7	After approximately 5 minutes, CLOSE V-temp-2.  Test Engineer: D.J. 3-24-98
	10.2.8	CLOSE MOV-3125BK.  Test Engineer: 9.9/3-24-98
	10.2.9	CLOSE valve V-temp-1. Test Engineer: D. 9/3-24-98
	10.2.10	TURN OFF supply pump.
1		ABLE ENERGIZED, REMOTE, and OFF are illuminated on MCS U-2 for Booster Pump P-3125B.

Test Engineer: 9.9/3-24-9810.4 SELECT PID AUTO on MCS screen PCU-2 for Booster Pump P-3125B.

Test Engineer: 9.9/3-24-98

NOTE: Test Engineer will determine optimum PID settings by analyzing the contents of the datalogger from the PID MAN testing. Test Engineer may retune

PID settings as required during this test.

PREOPERATIONAL	TEST	POTP-007,	CROSS	SITE	TRANSFER	SYSTEM	INTEGRATI	ED .	TEST	_
•		i	HNF - 18	57			PAGE	98	0F	132
REVISION NO. <u>0</u>		A <sup>-</sup>	TTACHME	ENT A						

10.5 **SET** PID-flow parameters for Booster Pump P-3125B to the values determined by the Test Engineer:

$$P = 0.80$$
  
I = 0.06 1/sec

 $D = \bigcirc$  sec

Test Engineer: 9.9./3-24-98

10.6 SET Fluid Flow Set Point value to  $\frac{100}{104}$  gpm.

Test Engineer:  $\frac{9.9}{100}$ 

NOTE: Test Engineer will supply rate of acceleration and deceleration that the variable speed drive VSD-2 will implement for all increases/decreases in speed setpoint, and rate-of-change (ramp) limit(s) for the control signal logic in the PCU.

10.7 **SET** the rate-of-change (ramp) limit(s) in the control signal logic in the PCU for P-3125B, per Test Engineer's direction. RECORD value below. N/A if not performed.

PCU ramp limit = <u>60</u>

Test Engineer: 9.9/3-24-98

10.8 SET ACCEL TIME and DECEL TIME parameters on VSD-2 per direction of the Test Engineer and to the values determined by the Test Engineer. RECORD values below. N/A if not performed.

ACCEL TIME = 20 DECEL TIME = 60

Test Engineer:  $\frac{D.9/3-24-98}{1}$ 

10.9 **SELECT** the Transfer Sequencing **RESET** button.

Test Engineer: D. \$\frac{3-24-98}{3}\$

NOTE: Valves previously "forced" to a position on the MCS for purposes of this test should not be shown as valve positioning failures because the associated valve failure alarms are jumpered out per Section 3.0.

10.10 **VERIFY** Alarm Table on MCS shows no valve positioning failures. Test Engineer:  $9 \cdot 9 / 3 - 24 - 9 \checkmark$ 

10.11 **SELECT** the Transfer Sequencing **INITIATE** Button.

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF - 1857 PAGE 99 OF 132

REVISION NO. 0

ATTACHMENT A

NOTE: Transfer Scheme 2B sets up for transfer of slurry from the 241-SY-B valve pit to the 241-A-A valve pit.

10.12 SELECT the Transfer Sequencing TYPE 2B transfer button/3/24-98

10.13 VERIFY proper valve position in accordance with Appendix F-4 Data Sheet. Test Engineer: 9.9/3424-96

NOTE: The boxes on the MCS overview screen that denote PCU-1 thru PCU-5 indicate status of the transfer path. All boxes GRAY and paths GREEN indicates that the transfer path is ready for use. Boxes filled in RED indicates that an alarm associated with the transfer is activated (i.e. mispositioned valve, leak detected, etc). The booster pump will not start

10.14 IF any of the boxes on the MCS overview screen which denote PCU-1 thru PCU-5 are highlighted in RED, DETERMINE the reason why and perform the following:

10.14.1 Disposition the problem by fixing it and clearing alarm, or by overriding the alarm IF the Test Engineer determines that the problem will not affect the performance of this test. RECORD disposition on the Test Log or on a Test Exception Sheet, at the discretion of the Test Engineer. N/A this step if not performed.

Test Engineer: 7/2 0.9 3/24/98

10.15 **VERIFY** the boxes on the MCS overview screen which denote PCU-1 thru PCU-5 are highlighted in GRAY, unless a RED box has been determined to be acceptable per the previous step.

Test Engineer:

10.16 OPEN SOV-3125G and SOV-3125D from the MCS. Test Engineer: 9.9/3-24-98

unless associated alarms are either cleared or over-ridden.

10.17 ADJUST pressure control valve on the supply jumper assembly to an arbitrary OPEN position.

10.18 TURN ON supply pump.

PREOPERATIONAL	TEST	POTP-007,	CROSS	SITE	TRANSFER	SYSTEM	INTEGRAT	ED	TEST	-
		ŀ	INF-189	57			PAGE	100	OF	132

REVISION NO. 0

ATTACHMENT A

	ADJUST pressure control valve on the supply jumper assembly so that the pressure indicator at the supply pump discharge reads approximately 50 psi slag 44
	10.19.1 PI-temp-1 60 psig Test Engineer: $\frac{D.\mathcal{Y}}{3-24-98}$
10.00	ODEN 3 No. 4
10.21.	Test Engineer: D.J./3-24-8  Hat 14/1/97  FULLY OPEN flow control valve V-temp-2. Approx 1/8 OPEN.  Test Engineer: D.J./3-24-98

Prepare to start P-3125B

IMPORTANT: Be prepared to immediately shut down booster pump if so requested. To shut down the pump, PRESS either the OFF key on VSD-2 keypad or STOP button on PCU-2 for Booster Pump P-3125B.

- 10.22 **BEGIN** datalogging of the flow signal and the signal to the VSD.
- 10.23 PRESS the START button on MCS screen PCU-2 for Booster Pump

10.23. a FULLY OPEN V-temp-2 per direction of Test Engineer. (local)

- 10.24 VERIFY locally that P-3125B is operating. Test Engineer"\_ Test Engineer: D. St /3/24/98
- 10.25 VERIFY START ENERGIZED and ON are illuminated on MCS screen PCU-2 for Booster Pump P-3125B. Test Engineer: \_P. 91/3-24-98

NOTE: If P-3125B does not keep a steady flow, perform the following step.

10.26 IF flow as read from FIC-3125 is oscillating more than 8 gpm, THEN exit PID AUTO and enter PID MAN. Re-tune PID per Test Engineer's instructions and record the new PID-flow settings below. N/A step if not performed.

$$P = 0.90$$
  
 $I = 0.06$  1/sec  
 $D = 0$  Sec

Test Engineer: 9.9/3-29-98

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 101 OF 132

REVISION N	NO. <u>0</u> ATTACHMENT A
Point #1,	100 3/23/98 104 gpm, flow control valve full open
10.2	27 RECORD the following data. VERIFY FIC-3125 reads $1.04 \pm 8$ gpm
· .	10.27.2 Flow rate 10.27.3 Flow rate 10.27.4 Pump inlet pressure 10.27.5 Pump discharge pressure  FI-temp-1 FIC-3125 FIC-
	Test Engineer: D.S. 3/24/98
10.2	28 On VSD-2 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data:  10.28.1 Motor Freq 22.5 Hz 10.28.2 Motor Speed 59 % 10.28.3 Motor RPM 10.28.4 Load A Amps 10.28.4 Load A Amps 10.28.5 Load B Amps 10.28.5 Load B Amps 10.28.6 Load C Amps 10.28.7 Load AB Volts 10.28.8 Load BC Volts 10.28.9 Load CA Volts 10.28.10 Power  26 Kilowatts
	Test Engineer: D. 9 / 3/24/48
10.2	9 <b>RECORD</b> pump and system data on an Appendix G Data Sheet, Test Engineer: <u>9</u> الكورة كالمراكبة كالمراكب
10.3	30 ALLOW pump P-3125B to run for at least 30 minutes. At 10 minute

RECORD pump and system data on an Appendix G Data Sheet Test Engineer: 🔊 🗗

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 102 OF 132

REVISION NO. 0

ATTACHMENT A

CAUTION: Flow Control Valve V-temp-2 should never be fully closed while the booster pump is operating, to prevent "deadheading" of the booster pump. Deadheading (no flow) for a significant time could result in damage to the booster pump. Constant surveillance during this test is required.

110 8.8.3/23/48

Point #2, 104 gpm, increase back pressure on pump to verify flow control feedback increases pump motor speed and horsepower to meet the required flow.

10.31 THROTTLE flow control valve to increase motor speed approximately 100 rpm per SI-3125B.

Test Engineer:  $\frac{9\cancel{\cancel{3}}/\cancel{3} - \cancel{24} - \cancel{\%}}{\cancel{10}}$  10.32 **RECORD** the following data. **VERIFY** FIC-3125 reads  $\frac{\cancel{9}\cancel{3}}{\cancel{3}\cancel{2}\cancel{3}\cancel{9}\cancel{8}}$ 

10.32.1 Motor speed	SI-3125B	2110 RPM
10.32.2 Flow rate	FI-temp-1	<u> 109</u> GPM
10.32.3 Flow rate	FIC-3125	GPM
10.32.4 Pump inlet pressure	PI-3125B	<u>57</u> psig
10.32.5 Pump discharge pressure	PI-3125D	331_ psig

Test Engineer: <u>D.J / 3</u>-24-98

10.33 On VSD-2 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. **RECORD** the following data:

10.33.1 Motor Freq	34.5 Hz
10.33.2 Motor Speed	<u> </u>
10:33.3 Motor RPM	<u>2074</u> RPM
10.33.4 Load A Amps	<u></u>
10.33.5 Load B Amps	<u> 100</u> Amps
10.33.6 Load C Amps	<u>100</u> Amps
10.33.7 Load AB Volts	<u> 284</u> Volts
10.33.8 Load BC Volts	<u> 279</u> Volts
10.33.9 Load CA Volts	<u>275</u> Volts
10.33.10 Power	<u>44</u> Kilowatts

Test Engineer: <u>8.99 / 3-24-98</u>

10.34 RECORD pump and system data on an Appendix G Data Sheet.

Test Engineer:  $\cancel{9}$   $\cancel{3}$   $\cancel{4}$   $\cancel{98}$ 

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 103 OF 132 HNF-1857

REVISION NO

ATTACHMENT A

NEVISION I	10. <u> </u>		ATTACHHEN	II A			
	interv	als; RECOR	5B to run fo D pump and s ncrease in b	ystem d	ata on an A	Appendix G	
	200 rp	m per SI-31	ntrol valve 125B. (Back w control va	off rp	m if cavita	ition is fo	
10.3	10.37. 10.37. 10.37. 10.37.	1 Motor spe 2 Flow rate 3 Flow rate 4 Pump inle	eed .	ure	SI-3125B FI-temp-1 FIC-3125 PI-3125B	2360 RP 104 GP 110 GP 57 ps 409 ps	M M M ig ig
10.3	UP and	DOWN arrow	use the LIN ws to toggle as required.	thru t	ne displaya	ble quanti	ties. Üse

10.38.1 Motor Freq	<u> 32,2</u> Hz
10.38.2 Motor Speed	<u>62,9</u> %
10.38.3 Motor RPM	<u> 2265</u> RPM
10.38.4 Load A Amps	<u> 110</u> Amps
10.38.5 Load B Amps	<u> 110</u> Amps
10.38.6 Load C Amps	<u>109</u> Amps
10.38.7 Load AB Volts	_300 Volts
10.38.8 Load BC Volts	<u> 300</u> Volts
10.38.9 Load CA Volts	<u> 300</u> Volts
10.38.10 Power	_ <i>50</i> Kilowatts

Test Engineer: 99,

10.39 RECORD pump and system data on an Appendix G Data Sheet. Test Engineer: 9.99

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 104 OF 132

REVISION NO. 0

ATTACHMENT A

10.40 ALLOW pump P-3125B to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix 6 Data Sheet Test Engineer:

Point #4, 140 gpm, flow control valve full open

10.41 FULLY OPEN flow control valve V-temp-2.

Test Engineer: <u>D. J / 3-24-98</u>

10.42 SET Fluid Flow Set Point value to 140 gpm.

Test Engineer: 9.9/3-24-98

10.43 RECORD the following data. VERIFY FIC-3125 reads 140  $\pm$  7 gpm.

10.43.1 Motor speed	SI-3125B	<u> 2620</u> RPM
.10.43.2 Flow rate	FI-temp-1	<u> 140</u> GPM
10.43.3 Flow rate	FIC-3125	<u> 140</u> GPM
10.43.4 Pump inlet pressure	PI-3125B	<b>46</b> psig
10.43.5 Pump discharge pressure	PI-3125D	

Test Engineer: <u>£9.91. 3/24/98</u>

10.44 On VSD-2 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data:

10.44.1 Motor Freq	<u><b>43</b></u> Hz
10.44.2 Motor Speed	<u>71.5</u> %
10.44.3 Motor RPM	<u> 2525                                  </u>
10.44.4 Load A Amps	<u> 127</u> Amps
10.44.5 Load B Amps	<u> 127</u> Amps
10.44.6 Load C Amps	<u> 12.2</u> Amps
10.44.7 Load AB Volts	<u>354</u> Volts
10.44.8 Load BC Volts	<u>350</u> Volts
10.44.9 Load CA Volts	<u>390</u> Volts
10.44.10 Power	65 Kilowatts

Test Engineer: 9.9./3.29-98

10.45 RECORD pump and system data on an Appendix G Data Sheet,

Test Engineer:  $\sqrt{3}$  / 3 - 24 - 98

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 105 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

10.46 ALLOW pump P-3125B to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix G, Data Sheet Test Engineer:  $\mathcal{PQ}$  / 3-24-98

Point #5, 140 gpm, increase back pressure on pump to verify flow control feedback increases pump motor speed and horsepower to meet the required flow.

10.47 THROTTLE flow control valve to increase motor speed approximately 100 rpm per SI-3125B. 

10.48 **RECORD** the following data. **VERIFY** FIC-3125 reads  $140 \pm 7$  gpm

10.48.1	Motor	^ speed	SI-3125B	2720	RPM
10.48.2	Flow	rate	FI-temp-1	138	GPM
10.48.3	Flow	rate	FIC-3125	140	GPM
10.48.4	Pump	inlet pressure	PI-3125B	46	psig
10.48.5	Pump	discharge pressure	PI-3125D	505	psiq

Test Engineer: <u>D</u>

10.49 On VSD-2 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data:

10.49.1 Motor Freq	44.9 Hz
10.49.2 Motor Speed	<u>74.5</u> %
10.49.3 Motor RPM	<u>2673</u> RPM
10.49.4 Load A Amps	<u>/33</u> Amps
10.49.5 Load B Amps	<u> 133</u> Amps
10.49.6 Load C Amps	<u> 133</u> Amps
10.49.7 Load AB Volts	<u>365</u> Volts
10.49.8 Load BC Volts	<u>350</u> Volts
10.49.9 Load CA Volts	<u>350</u> Volts
10.49.10 Power	<u>76</u> Kilowatts

Test Engineer:  $Q.\mathcal{Y}/3-24-98$ 

10.50 **RECORD** pump and system data on an Appendix G Data Sheet. Test Engineer:  $\frac{2J}{J} + \frac{3}{3} - \frac{29-99}{2}$ 

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 106 OF 132

REVISION NO. 0

ATTACHMENT A

10.51 **ALLOW** pump P-3125B to run for at least 30 minutes. At 10 minute intervals, **RECORD** pump and system data on an Appendix G Data Sheet Test Engineer:  $\cancel{D}$   $\cancel{3}$   $\cancel{24/98}$ 

Point #6, 140 gpm, further increase in back pressure

10.52 **THROTTLE** flow control valve to increase motor speed approximately 200 rpm per SI-3125B. (Back off rpm if cavitation is found to occur at the flow control valve)

Test Engineer: <u>0.4. 3/24/98</u>

10.53 **RECORD** the following data. **VERIFY** FIC-3125 reads  $140 \pm 7$  gpm

10.53.1 Motor speed	SI-3125B	<u>2900</u> RPM
10.53.2 Flow rate	FI-temp-1	<u> 127</u> GPM
10.53.3 Flow rate	FIC-3125	<u> 140</u> GPM
10.53.4 Pump inlet pressure	PI-3125B	<u>46</u> psig
10.53.5 Pump discharge pressure	PI-3125D	<u>616</u> psig

Test Engineer: 9.4/3-29-98

10.54 On VSD-2 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. **RECORD** the following data:

10.54.1 Motor Freq	48,1	Hz
10.54.2 Motor Speed	<u>80</u> %	
10.54.3 Motor RPM	2883 RPM	
10.54.4 Load A Amps	<u> 146</u> Amps	
10.54.5 Load B Amps	<u> 144</u> Amps	
10.54.6 Load C Amps	<u> 145</u> Amps	
10.54.7 Load AB Volts	<u>388</u> Volts	
10.54.8 Load BC Volts	<u>324</u> Volts	
10.54.9 Load CA Volts	<u>374</u> Volts	
10.54.10 Power	<u>&amp;&amp;_</u> Kilowa	tts

Test Engineer: 9.99 / 3-24-98

10.55 **RECORD** pump and system data on an Appendix G Data Sheet.  $\frac{D.6.}{3-24-98}$ 

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 107 OF 132

REVISION NO	. <u>O</u> ATTACHMENT A
	ALLOW pump P-3125B to run for at least 30 minutes. At 10 minute intervals, RECORD pump and system data on an Appendix G Data Sheet Test Engineer: カリノューション・フェック・フェック・フェック・フェック・フェック・フェック・フェック・フェック
Point #7, 16	60 gpm, flow control valve full open
	FULLY OPEN flow control valve V-temp-2.  Test Engineer:    Sold 3/2/98     3-24-98
10.50	Tost Engineer: 1991 / 3-24-98
10.59	RECORD the following data. VERIFY FIC-3125 reads $160 \pm 8$ gpm.
	$\begin{array}{cccccccccccccccccccccccccccccccccccc$
	Test Engineer: $9.9/3-24-98$
10.60	On VSD-2 keypad, use the LINE key and Programming and Monitoring UP and DOWN arrows to toggle thru the displayable quantities. Use the RIGHT arrow as required. RECORD the following data:
	10.60.1 Motor Freq 10.60.2 Motor Speed 10.60.3 Motor RPM 2299 RPM 10.60.4 Load A Amps 10.60.5 Load B Amps 10.60.6 Load C Amps 10.60.7 Load AB Volts 10.60.8 Load BC Volts 10.60.9 Load CA Volts 10.60.10 Power  46.6 Hz 299 RPM 2299 RPM  Amps 140 Amps 141 Amps 142 Amps 150 Volts 160.60.8 Load BC Volts 170 Volts
	Test Engineer: $\frac{9 \times 1/3-24-90}{1}$
10.61	<b>RECORD</b> pump and system data on an Appendix G Data Sheet.  Test Engineer: $\frac{3}{24/98}$

HNF-2504, REV. 0 ATTACHMENT | PAGE |

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 108 OF 132

**REVISI** 

REVISION	NO. <u>0</u>		ATTACHMENT A	·		
10		W pump P-3125B rvals, <b>RECORD</b> p	ump and syste		ppendix G D	ąta Sheet
	, <del>160</del> gpr	1 <sup>3</sup> /23/98 m, increase bac es pump motor s	•	• •	···	
10	.63 <b>THRO</b> 100 r	TTLE flow contr rpm per SI-3125 RD the followin	ol valve to i B.	ncrease motor est Engineer:	speed appro	ximately
10.	.64 <b>RECO</b> F	RD the followin	g data. <b>VER</b> I	FY FIC-3125 re	ads 160 ± 8	': '723/98' gpm 7
	10.64 10.64 10.64	4.1 Motor speed 4.2 Flow rate 4.3 Flow rate 4.4 Pump inlet 4.5 Pump discha	pressure rge pressure	FI-temp-1· FIC-3125 PI-3125B		g g
10.	UP ar	SD-2 keypad, us nd DOWN arrows RIGHT arrow as	to toggle thr	u the displaya	ble quantit	
	10.65	5.1 Motor Freq	48.1	Hz		

10.65.1 Motor Freq	<u>48.1</u> Hz
10.65.2 Motor Speed	<u>80.1</u> %
10.65.3 Motor RPM	<u> 2885</u> RPM
10.65.4 Load A Amps	<u> 1<b>4</b>6</u> Amps
10.65.5 Load B Amps	<u> 146</u> Amps
10.65.6 Load C Amps	<u> 196</u> Amps
10.65.7 Load AB Volts	<u>386</u> Volts
10.65.8 Load BC Volts	<u> 38/</u> Volts
10.65.9 Load CA Volts	<u>376</u> Volts
10.65.10 Power	<u>93</u> Kilowatts

Test Engineer: 9.9/3-24-9810.66 RECORD pump and system data on an Appendix G Data Sheet
Test Engineer: 9.9/3-24-98

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 109 OF 132

REVISION NO	). <u>U</u> ATTACHN	IENI' A	
	ALLOW pump P-3125B to run intervals, RECORD pump and 55 日ようない。 60 gpm, further increase in	system data on an Ap	pendix G Data Sheet
	THROTTLE flow control valve 200 rpm per SI-3125B. (Ba occur at the flow control	ck off rpm if cavitat valve) Test Engineer:	ion is found to $\beta. \mathcal{Y}.  \frac{3}{24} / 98$
10.69	RECORD the following data.	VERIFY FIC-3125 read	ds 160 ± 8 gpm
	10.69.1 Motor speed 10.69.2 Flow rate 10.69.3 Flow rate 10.69.4 Pump inlet pressur 10.69.5 Pump discharge pre	e	145 GPM 15€ GPM 40 psig ~ 68€ psig
		Test Engineer: _	D.G. 3/29/98
10.70	After flow rate as read fr of the flow signal and the		
10.71	On VSD-2 keypad, use the L UP and DOWN arrows to togg	INE key and Programmin	ng and Monitoring

the RIGHT arrow as required. RECORD the following data:

10.71.1 Motor Freq	<u></u>
10.71.2 Motor Speed	<u>85,9</u> %
10.71.3 Motor RPM	<u>3095</u> RPM
10.71.4 Load A Amps	<u>163</u> Amps
10.71.5 Load B Amps	<u>169</u> Amps
10.71.6 Load C Amps	<u> 163</u> Amps
10.71.7 Load AB Volts	<u>4/0</u> Volts
10.71.8 Load BC Volts	<u>409</u> Volts
10.71.9 Load CA Volts	<u>40/</u> Volts
10.71.10 Power	<u>_/00</u> _ Kilowatts

Test Engineer:  $D.G. \frac{3}{24/98}$ 

PREOPERATIONAL	TEST	POTP-007,	CROSS	SITE	TRANSFER	SYSTEM	INTEGRAT	ED	TEST	-
		. [	INF - 18	57			PAGE	110	OF	132

REVISION NO. 0

ATTACHMENT A

10.72 **RECORD** pump and system data on an Appendix G Data Sheet. Test Engineer:  $\frac{3}{24/98}$ 

10.73 **ALLOW** pump P-3125B to run for at least 30 minutes. At 10 minute intervals, **RECORD** pump and system data on an Appendix G Data Sheet Test Engineer:  $\frac{D \cdot G}{3/24/98}$ 

Stop P-3125B

10.74 RECORD final PID-flow parameters for Booster Pump P-3125B.

 $P = \underline{0.90}$   $I = \underline{0.06}$  1/sec  $D = \underline{0}$  sec

Test Engineer: D.S. 3/24/98

10.75 **PRESS** the STOP button on MCS screen PCU-2 for Booster Pump P-3125B.

10.76 **VERIFY** locally that P-3125B has stopped.

Test Engineer: Dy. 3/24/98

10.77 VERIFY ENABLE ENERGIZED and OFF are illuminated on MCS screen PCU-2 for Booster Pump P-3125B.

Test Engineer: 9.993/24/98

10.78 CLOSE flow control valve V-temp-2

Test Engineer: <u>9.9. 3/24/98</u>

10.79 CLOSE V-temp-1

Test Engineer: 0.9.3/24/98

10.80 TURN OFF supply pump.

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 111 OF 132

REVISION NO. 0

ATTACHMENT A

### 11.0 Transfer Loop Vent and Drain

The transfer loop will be vented and the water will be allowed to drain back to the temporary water reservoir. The water that remains in the piping at a lower elevation than the water reservoir will be drained to the Diversion Box sump by removing the temporary jumpers and pumping out.

11.1 **RECORD** the line pressures at each vent line:

NOTE: Sulzer Bingham has recommended the booster pumps remain filled with water. Therefore the pump isolation SOV's will be closed and the pump bypass SOV opened to allow drainage.

11.2 **POSITION** the following SOV's as indicated.

11.2.1	SÖV-3125E	CLOSED .	Test Engineer:	D.29	3/27/98
11.2.2	SOV-3125C		Test Engineer:		3/27/98
11.2.3	SOV-3125G	CLOSED	Test Engineer:	<u>D</u> . D.	3/27/18
11.2.4	SOV-3125D	CLOSED 7	Test Engineer:	D.V.	3/27/48
11.2.5	SOV-3163	OPEN :	Test Engineer:	D. H.	3/27/98

11.3 **POSITION** the following SOV's to manual mode by turning the lever at each valve actuator to **ENGAGE**.

11.3.1	SOV-3125E	ENGAGE Test Engineer	D.Y	3/27/98
11.3.2	SOV-3125C	ENGAGE Test Engineer	B.S.	3/27/98
11.3.3	SOV-3125G	ENGAGE Test Engineer	Ort	3/27/18
11.3.4	SOV-3125D	ENGAGE Test Engineer	Delf.	3/27/98
11.3.5	SOV-3163	ENGAGE Test Engineer	: <u>0.1/</u>	3/27/98

11.4 CREATE a clear flow path for water to drain back thru the supply jumper by either disconnecting or bypassing supply pump, or removing pressure control valve.

Test Engineer: 94 3/2>/98

11.5 **REMOVE** the submerged end of the discharge jumper from the water

reservoir.

Test Engineer:  $\mathcal{B}$ .  $\mathcal{Y}$   $\mathcal{Y}_{2}$ / $\mathcal{Y}_{3}$ 

PREOPERA		HNF	OSS SIT -1857 CHMENT	E TRANSFER SYS		TED TEST 112 OF 132
11.6	OPEN the	temporary supp	ly valv	e and flow con	trol valve.	
	11.6.1 11.6.2	V-temp-1 V-temp-2	OPEN OPEN	Test Engineer Test Engineer	: <u>D</u> . <b>D</b> . <b>D</b> .	3/27/98
11.7	VERIFY th	e line pressur	es at e	ach vent line	are O psig	or less:
	11.7.1 PI 11.7.2 PI	-3126A <u>- /2</u> -3126B <u>-2/</u>	psig psig	2 psig }	during di	aining E.f
				vious step are e vent valves		
11.8	OPEN the	vent valves fo	r both	the slurry lin	e and super	nate line:
	11.8.2 11.8.3	SOV-3185A SOV-3185B SOV-3168A SOV-3168B	OPEN OPEN	Test Engineer Test Engineer Test Engineer Test Engineer	: <u>D.M.</u> : D.M.	3/27/98 3/27/98 3/27/98 3/27/98
NOTE: Assum take approx	ing each l	うし ine drains at nours to drain	a rate ( the tr	of 35 gallons ansfer loop. <i>(</i> <i>o</i> flow stops.	per minute, Record +	it will @ ine) 13:3
11.9	ALLOW the	lines to drai	n until	flow stops.	(RECOND T	me 15:52
11.10		the supply and	discha	iping to the D rge jumpers fr Test Engineer	om the Hilt	
11.11	PUMP resi	dual water out	of the	transfer line Test Engineer	s. <u>D. J</u>	3/30/98
				the Diversion Test Engineer	: <u> </u>	
11.13	3 Remov	re tempos	sary	filter asse	mblies	D.G 3/26/
	1	y INSPECT FOR	ANY -	SIGN OF	HUMINITY	
Yote: mea - FI-Temp		_		Obser	rua tion	
,	. P	SNL fil	TER	OR	<del>Y</del>	

SLL FILTER

(\*)

HNF-2504, REV. 0 ATTACHMENT | PAGE/St.

<del>126 0F 15</del>0

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 113 OF 132

REVISION NO. \_0\_

ATTACHMENT A

### 12.0 Post-Test Conditions

12.1 **REINSTALL** Hiltap connector caps in accordance with manufacturer's instructions. **TIGHTEN** set screws on those with that feature.

Test Engineer:

12.2 **REMOVE** the "blue tags" from the manual valve actuators on the following SOV's:

12.2.1	SOV-3182A	Test Director:	E.P	3/30/98
12.2.2	SOV-3182B	Test Director:	Ε. Ρ	
12.2.3	SOV-3183A	Test Director:	,	
12.2.4	SOV-3183B	Test Director:	E.P	
12.2.5	SOV-3166A	Test Director:	E.P	
12.2.6	SOV-3166B	Test Director:	FP	7

12.3 RE-CONNECT the air supply hose to the following SOV's. AIR LINES WERE DAY 3/2/2019

12.3.1	SOV-3182A SOV-3182B SOV-31 <del>83</del> A	Test Engineer:	
12.3.3 12.3.4 12.3.5	SOV-3183B SOV-3166A	Test Engineer: Test Engineer: Test Engineer:	
12.3.6	SOV-3166B	Test Engineer:	

12.4 IF directed by Test Director, reattach P-102-SY-02A motor leads per normal plant procedure.

Test Director: Not we

12.5 **REMOVE** the normally open software jumper in series with N19:2/13 VALVE FAILURE Alarm for SOV-3183A.

Test Engineer: 9.9 3/27/98

- 12.6 **REMOVE** the normally open software jumper in series with N19:2/12 VALVE FAILURE Alarm for SOV-3183B.

  Test Engineer: 94. 3/2>/58
- 12.7 **REMOVE** the normally open software jumper in series with B3/92 VALVE FAILURE Alarm for SOV-3166B.

Test Engineer: 9.4 3/1/98

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 114 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

12.8 REMOVE the FORCE (in the MCS software) of the associated bits for the following valves.

Valve No.	Description	Forced Position	Initial (Verify Removed)
S0V-3183A	WT-SLL-3160 at Diversion Box	OPEN	D. A 3/11/18
SOV-3183B	WT-SLL-3160 at Diversion Box	OPEN	D. G.
SOV-3166B	WT-SLL-3160 at Vent Station	OPEN	·D. 4

Test	Engineer:	D. St.	3/27/48
1401	Lugincei.		7.

12.9 **REMOVE** the normally open software jumper on in series with N19:2/10 VALVE FAILURE Alarm for SOV-3184.

Test Engineer: D. H. 1/1/98

12.10 **REMOVE** the normally open software jumper in series with B3/80 VALVE FAILURE Alarm for SOV-3165A.

12.11 **REMOV**E the FORCE (in the MCS software) of the associated bits for the following valves.

Valve No.	Description	Forced Position	Initial (Verify Removed)
S0V-3184	WT-SNL-3150 at Diversion Box	CLOSED	D. 4.
SOV-3165A.	WT-SNL-3150 at Vent Station	CLOSED	D. 4

Test Engineer: D. y 3/27/90

12.12 **REMOVE** the normally open software jumper in series with N19:4/9 VALVE FAILURE Alarm for MOV-845.

Test Engineer: 9.8. /27

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST
HNF-1857 PAGE 115 OF 132

REVISION NO. 0

ATTACHMENT A

12.13  $\mbox{REMOVE}$  the FORCE (in the MCS software) of the associated bits for the following valves.

Valve No.	Description	Forced Position	Initial (Verify Removed)
MOV-844	WT-SLL-3160 Motor Operated 3-Way Valve at 244A Lift Station	A ⇒ B	DG.
MOV-845	WT-SLL-3160 Motor Operated Valve at 244A Lift Station	OPEN	D. G.

12.14 **REMOVE** any software jumpers or forced bits in the MCS software placed into service as a result of a RED box when initiating a Transfer Scheme. **RECORD** in Test Log.

Test Engineer: D. 9 727/9

12.15 REMOVE THE TWO JUMPERS IN UB-1 AT 244A WHICH

SIMULATE AS RUPTURE DISCS PSE-841 & PSE-842 ARE

D.D. INSTALLED. D. J 3/27/98


7/2/98

12.16 REMOVE ALL FORCES FROM MCS SOFTWARE (200E MASTER SHUTDOWN) D. S. 3/2/98

REVISION NO. 0

ATTACHMENT A

APPENDIX A - TEST SETUP

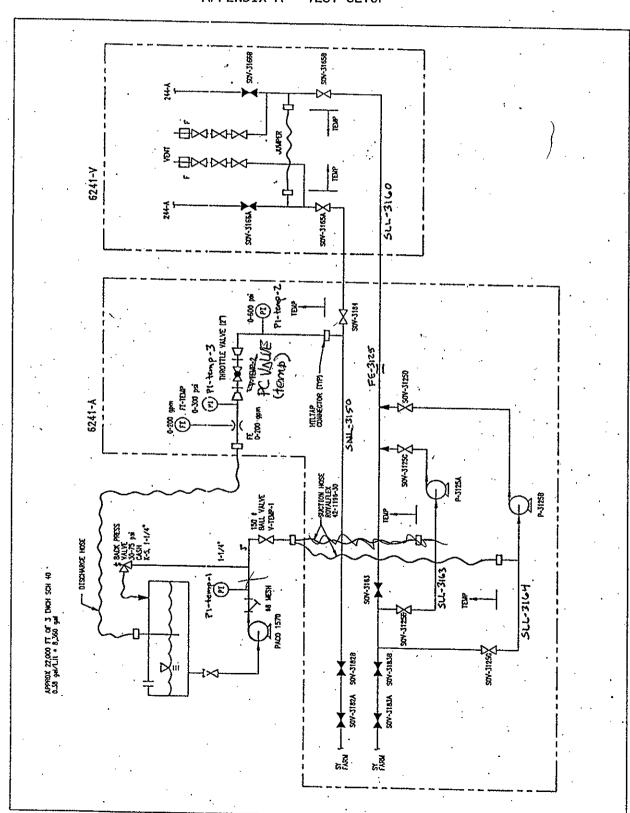

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 117 OF 132

REVISION NO. 0

ATTACHMENT A

	APPENDIX B - Instrumentation Requiring Calibration Verification*						
Equipment Number	Functional Description	Calibration Calibration Date Due		Signature & Date			
FE-3125	Slurry Line 3160 Flow Element (comprised of FE-3125R receiver and FE-3125T transmitter)	11/17/97	None *	GaL			
FI-3125A1	Booster pump P-3125A outboard seal supply flow indicator	8-12-97		June Ornel			
FI-3125A2	Booster pump P-3125A inboard seal supply flow indicator	8-12-97	8-12-98	Jours Ornd			
FI-3125B1	Booster pump P-3125B outboard seal supply flow indicator	8-12-97	8-12-98 6	12-12-97			
FI-3125B2	Booster pump P-3125B inboard seal supply flow indicator	8-12-97	8-12-98	Janel Alert 12-12-87			

<sup>\*</sup>see continuation page for list of instruments whose calibration has been previously verified.

THE FOLLOWING VIBRATION TRANSMITTERS WERE CALIBRATED ON 1/16/98
ATO THE MANUFACTURER'S FACILITY METRIX INSTRUMENT CO.

VT-3125A1 SERIAL # 15192

VT-3125B1 SERIAL # 15191

VT-3125B2 SERIAL # 15193

<sup>\*</sup> Per ultrasonic flowmeter vendor, PANAmetrics, FE-3125 requires no future "calibration"

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 118 OF 132

REVISION NO. \_0\_

### ATTACHMENT A

### APPENDIX B (CONTINUED)

All remaining instrumentation requiring calibration for the performance of this test have been previously verified in earlier pre-operational test procedures. The instrument and the test where verification occurred is listed below.

EQUIPMENT NUMBER	TEST WHERE VERIFICATION OCCURRED	ALTERNATE REFERENCE
PI-3108A	HNF-1553	POTP-002
PI-3125A1	HNF-1553	POTP-002
PI-3125A2	HNF-1553	POTP-002
PI-3125B1	HNF-1553	POTP-002
PI-3125B2	HNF-1553	POTP-002
PI-3108B	HNF-1554	POTP-003
PT-3125A	HNF-1555	POTP-004
PT-3125B	HNF-1555	POTP-004
PT-3125C	HNF-1555	POTP-004
PT-3125D	HNF-1555	POTP-004
PT-3126B	HNF-1555	POTP-004
PT-3168	HNF-1555	POTP-004
PT-3125E	HNF-1556	POTP-005
PT-3126A	HNF-1556	POTP-005
PT-3173	HNF-1556	POTP-005
PT-3167	HNF-1556	POTP-005
PT-3185	HNF-1556	POTP-005

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 119 OF 132

REVISION NO. 0

ATTACHMENT A

REVERIFED -

APPENDIX	C - Loop Test Initial Instrument Air and Man	ual Valve Alig	nment
VALVE NUMBER	DESCRIPTION	REQUIRED POSITION	INITIALS
	Diversion Box Instrument Air System Valve	S	
IA-V-3101A	SOV air supply isolation valve	OPEN	HUL
IA-V-3102A	Booster pump seal air supply isolation valve	CLOSED	LgL.
IA-V-3103A	Future supply isolation valve	CLOSED	HUL
IA-V-3104A	PI-3104A instrument isolation valve	OPEN	Hal
IA-V-3105A	PCV-3100A inlet isolation valve	CLOSED	SIAL
IA-V-3106A	PCV-3100A outlet isolation valve	OPEN	Hal
IA-V-3108A	PI-3108A instrument isolation valve	OPEN	GaL
IA-V-3113A	Pump seal control panel WT-PNL-3125A1 inlet isolation	OPEN	Had
IA-V-3107A	Pump seal control panel WT-PNL-3125A2 inlet isolation	OPEN	LaL
IA-V-3114A	Pump seal control panel WT-PNL-3125B1 inlet isolation	OPEN	LaL.
IA-V-3109A	Pump seal control panel WT-PNL-3125B2 inlet isolation	OPEN	LaL
IA-V-1/115A	Pump seal control panel WT-PNL-3125A1 exit valve	OPEN	LaL
IA-V-2/1164	Pump seal control panel WT-PNL-3125A2 exit valve	OPEN	2aL
IA-V-2/117A	Pump seal control panel WT-PNL-3125B1 exit valve	OPEN	212
IA-V <sup>3</sup> /118A	Pump seal control panel WT-PNL-3125B2 exit valve	OPEN	LaL_
DR-3100A	Air Receiver drain valve	CLOSED	Ha.L.
	Vent Station Instrument Air System Valve	S	
IA-V-3101B	SOV air supply isolation valve	OPEN	Jak_
IA-V-3102B	Future supply isolation valve	CLOSED	Sal
IA-V-3103B	Future supply isolation valve	CLOSED	<i>394</i>
IA-V-3104B	PI-3104B instrument isolation valve	OPEN	Ja L
IA-V-3105B	PCV-3100B inlet isolation valve	CLOSED	JUL .
IA-V-3106B	PCV-3100B outlet isolation valve	OPEN	Ja L
IA-V-3107B	PI-3108B instrument isolation valve	OPEN	142
DR-3100B	Air receiver drain valve	CLOSED	103
	Slurry Line Manual Valves AS 1	MES AND ALL OF	MCS DON RETER
	Sturry Line Hanual valves As /-	V7 ENLOYES ARE OPEN	Las
V-3183 V-3125A	PT-3183 isolation valve, SLL-3160, Diversion Box PT-3125A isolation valve, Pump P-3125A intake, SLL-3163, Diversion Box	CLOSED	29L

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 120 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

APPENDI	X C - Loop Test Initial Instrument Air and Mar	nual Valve Aligr	nment
VALVE NUMBER	DESCRIPTION	REQUIRED POSITION	INITIALS
V-3125B	PT-3125B isolation valve, Pump P-3125B intake, SLL-3164, Diversion Box	CLOSED	Las
V-3125C	PT-3125C isolation valve, Pump P-3125A discharge, SLL-3163, Diversion Box 6421-A	CLOSED	4a.L
V-3125D	PT-3125D isolation valve, Pump P-3125B discharge, SLL-3164, Diversion Box 6241-A	CLOSED	\$9L
V-3126B	PT-3126B isolation valve, SLL-3160, Vent Station	OPEN	Stark
V-3168	PT-3168 isolation valve, Vent Line SLL-3160, Vent Station	OPEN	Sal
V-3157G	HEPA filter isolation valve, Vent Line VTL-3160, Vent Station	OPEN	LaL
			DJ 2/1/9
	Supernate Line Manual Valves — S	EE NOTE ON S	LURAY LINE V
V-3182	PT-3182 isolation valve, SNL-3150, Diversion Box	OPEN	Sal
V-3125E	PT-3125E isolation valve, SNL-3150, Diversion Box	CLOSED	La L
V-3173	PT-3173 isolation valve, Sump Line SNL-3151, Diversion Box	OPEN	Gal
V-3126A	PT-3126A isolation valve, SNL-3150, Vent Station	CLOSED	Lay
V-3185	PT-3185 isolation valve, Vent Line SNL-3152, Vent Station	CLOSED	gay
V-3167	PT-3167 isolation valve, Sump Line SNL-3153, Vent Station	OPEN	Gas
V-3157H	HEPA filter isolation valve, Vent Line VTL-3152, Vent Station	OPEN	Sal
		<u> </u>	<u> </u>

Performed by: Lovuic J STeadman 20 12/12/97
PRINT NAME INITIALS DATE

Verified by: GA Leshikar GAL 12/12/97
PRINT NAME INITIALS DATE

QC. ROWALD ARNOT RG 1212-97

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 121 OF 132

REVISION NO. 0

ATTACHMENT A

	APPENDIX D - Electrical Alignment		
BREAKER NUMBER	BREAKER NAME AND LOCATION	REQUIRED POSITION	INITIALS
CB-6 DG	Diversion Box Panelboard PP-3 supply breaker in Switchboard SB-1	CLOSED	WAJ
15 CB25	Diversion Box Air Compressor supply breaker in Switchboard SB-1	CLOSED	thw
CB-2	Vent Station Panelboard PP-3 supply breaker in Distribution Panelboard DP-1	CLOSED	PLD PLD
CB-3	Vent Station Air Compressor supply breaker in Distribution Panelboard DP-1	CLOSED	PLD
-eB-4-	Diversion Box Switchboard breaker in SB-1 for VSD-1.	CLOSED	TAC.
CB-5 CB 1~ Z	Diversion Box Switchboard breaker in SB-1 for VSD-2.	CLOSED	WAJ
CB-2-6	Diversion Box Switchboard breaker in SB-1 for Sump Pump P-3115	CLOSED	MAJ
-CB-7- CB-9	Vent Station Distribution Panel breaker in DP-1 for Sump Pump P-3116	CLOSED	WAS
N/A	Vent Station Disconnect for Sump Pump P-3116.	CLOSED	WAJ
N/A (	Diversion Box Disconnect for Sump Pump P-3115.	CLOSED	TAK

Performed by: William Shason WAT 12/12/97
PRINT NAME INITIALS DATE

PRINT NAME PRINT NAME 15/12/97

Verified by: Haul Schust Phy 15/12/97

PRINT NAME INITIALS DATE

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 122 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	SOV LEVER POSITION	LOCAL POSITION	INITIALS
CLOSED: Green.	valve position is given by co designates OPEN, Red, design ndicator on SOV's. Lever pos	ates FAILED. ition ENGAGE p	Local indicat laces valve in	ion (OPEN/CLOSE n manual mode,	D) is given b DISENGAGE al	by valve lows MCS
	Solenoid (	Operated Valve	s in Diversio	LBOX— (reven)	fied for ile	TEST
SOV-3182A	SNL-3150	CLOSED	D. H. 103	ENGAGE-11-11-11	CLOSED	192
SOV-3182B	SNL-3150	CLOSED	0.98,0	ENGAGE-MAP	CLOSED	82
SOV-3184	SNL-3150	CLOSED	D. QD BY	*DISENGAGE	OPEN	GE .
SOV-3173A	Sump Line SNL-3151	CLOSED	D. Selve	DISENGAGE	CLOSED	8E
SOV-3173B	Sump Line SNL-3151	CLOSED	D. S. By	DISENGAGE	CLOSED	SE
SOV-3183A	SLL-3160	OPEN	D. S. 24	ENGAGE- MAP	CLOSED	EE.
SOV-3183B	SLL-3160	OPEN	29	ENGAGE:-mañ	CLOSED	SE
SOV-3163	Pump Bypass SLL-3160	OPEN	D. Y. B	DISENGAGE	OPEN	AE
SOV-3125E	P-3125A Intake SLL-3163	OPEN	0.0 29	DISENGAGE	OPEN	SE
SOV-3125C	P-3125A Discharge SLL-3163	OPEN	D.S. 99	DISENGAGE	OPEN	SE
SOV-3125G	P-3125B Intake SLL-3164	OPEN	D. S. 93	DISENGAGE	OPEN	g E
SOV-3125D	P-3125B Discharge SLL-3164	OPEN	D. H.M	DISENGAGE	OPEN	ga
	Solenoid	Operated Valve	es in Vent Sta	LENGALE	 	5 <del>/</del>
SOV-3165A	SNL-3150	CLOSED	1 () () ()	* DISENGAGELA	OPEN	291
SOV-3166A	SNL-3150	CLOSED	9.218	ENGAGE NO	CLOSED	DB
SOV-3185A	Vent Line SNL-3152	OPEN	D. 91 D	DISENGAGE	OPEN	牙.对.
SOV-3185B	Vent Line SNL-3152	OPEN	D. Y.O.	DISENGAGE	OPEŅ	711
SOV-3167A	Sump Line SNL-3153	CLOSED	D. J. D.	DISENGAGE	CLOSED	THA
SOV-3167B	Sump Line SNL-3153	CLOSED	D. Y AS	, DISENGAGE	CLOSED	710
SOV-3165B	SLL-3160	OPEN	D. D. D.	DISENGAGE	OPEN	211
.0V-3166B	SLL-3160	OPEN	D. H. n.	ENGAGE-MA	CLOSED	711
SOV-3168A	Vent Line SLL-3160	CLOSED	D. D. D9	DISENGAGE	CLOSED	78/

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 123 OF 132

REVISION NO. 0

ATTACHMENT A

D. 2/13/98

PREVENTION FOR RETEST						
	APPENDIX E -	Loop Fill SO	OV and MOV A	lignment		
VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	SOV LEVER POSITION	LOCAL POSITION	INITIALS
SOV-3168B	Vent Line SLL-3160	CLOSED	D. I	DISENGAGE	CLOSED	2/1
	Pump F	9-3125A Motor O	perated Valve	S		
MOV-3125AA	P-3125A Drain Valve	OPEN	D. 8/29	N/A	OPEN	29
MOV-3125AB	P-3125A Drain Valve	OPEN	D. 91, 09	N/A	OPEN	12
MOV-3125AC	P-3125A Drain Valve	OPEN	D. A. D.J	N/A	OPEN	42
MOV-3125AD	P-3125A Drain Valve	OPEN	D. A. D.)	N/A	OPEN	GE.
MOV-3125AE	P-3125A Drain Valve	OPEN	D. S. S. D	N/A	OPEN ,	SE
MOV-3125AF	P-3125A Drain Valve	OPEN	lake a	N/A	OPEN	4z
MOV-3125AG	P-3125A Drain Valve	OPEN	D. D. D.	J. N/A	OPEN	经
MOV-3125AH	P-3125A Drain Valve	OPEN	D. Y. D.J.	N/A	OPEN	GE
MOV-3125AJ	P-3125A Drain Valve	OPEN	9. Y. D	N/A	OPEN	SE
MOV-3125AK	P-3125A Vent Valve	OPEN	D. 9 2	<b>9</b> ), N/A	OPEN	A2
	P-3	125B Motor Ope				
MOV-3125BA	P-3125B Drain Valve	OPEN	0.21 22	N/A	OPEN	RE .
MOV-3125BB	P-3125B Drain Valve	OPEN	9. 89 RJ	N/A	OPEN	47
MOV-3125BC	P-3125B Drain Valve	OPEN	99, DQ	N/A	OPEN .	JE
MOV-3125BD	P-3125B Drain Valve	OPEN	D. D. D.	N/A	OPEN	RE
MOV-3125BE	P-3125B Drain Valve	OPEN	D. S. D.)		OPEN	99
MOV-3125BF	P-3125B Drain Valve	OPEN	D. U. D.		OPEN	AZ
MOV-3125BG	P-3125B Drain Valve	OPEN	D. &D.	N/A	OPEN	1/2
MOV-3125BH	P-3125B Drain Valve	OPEN	9.91 D	- 1	OPEN	SE
MOV-3125BJ	P-3125B Drain Valve	OPEN	P. 7. 9.9	N/A	OPEN	SE
MOV-3125BK	P-3125B Vent Valve	OPEN	O. M.	N/A	OPEN	SE.

real Verifications by: M.c. Wing Fre ld Impelae MM 12/19/9.

PRINT NAME INITIALS DATE

MCS Verifications by:

Doug Gehen PRINT NAME D. J. INITIALS 12/18/9) DATE

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 124 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

	APPENDIX F-1 - Transfer Scheme 2A Valve Alignment						
VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	LOCAL POSITION	INITIALS		
CLOSED; Green,	valve position is given by color and designates OPEN, Red, designates Fa ndicator on SOV's.	d fill of valve ( AILED. Local ind	on computer sc dication (OPEN,	reen. White, de /CLOSED) is give	esignates en by valve		
	Solenoid Operate	d Valves in Dive	rsion Box		. 400		
SOV-3182A	SNL-3150	CLOSED	DH.	CLOSED	12/19		
SOV-3182B	SNL-3150	CLOSED	9.21.	CLOSED 🗸	DU 1		
SOV-3184	SNL-3150	CLOSED	19.91	OPEN 🗸	<i>AM</i> )		
SOV-3173A	Sump Line SNL-3151	CLOSED	D.S.	CLOSED 🗸	VID .		
SOV-3173B	Sump Line SNL-3151	CLOSED	D.W.	CLOSED 🗸	Vgp		
SOV-3183A	SLL-3160	OPEN	D.Y,	CLOSED ~	BUN		
SOV-3183B	SLL-3160	OPEN	n H.	CLOSED 🗸	$\mathcal{A}(\mathcal{C})$		
SOV-3163	Pump Bypass SLL-3160	CLOSED	9.9,	CLOSED 🗸			
SOV-3125E	P-3125A Intake SLL-3163	-CLOSED	D.H.	CLOSED VPEN	90		
SOV-3125C	P-3125A Discharge SLL-3163	-CL-OSED	D.H.	CLOSED OF A	gra l		
SOV-3125G	P-3125B Intake SLL-3164	-1888	9.9	ACCOSED V	all a		
SOV-3125D	P-3125B Discharge SLL-3164	CLOSED.	$\mathcal{D}\mathcal{Y}$ .	CLOSED 🗸	All +		
		CHANGED STE	P 7.14		V		
	Solenoid Operato	ed Valves in Vent	t Station				
SOV-3165A	SNL-3150	CLOSED	99	* OPEN	AD 12/4		
SOV-3166A	SNL-3150	CLOSED	D.J.	y CLOSED	KOO		
SOV-3185A	Vent Line SNL-3152	CLOSED	DD.	y CLOSED (	Sec !		
SOV-3185B	Vent Line SNL-3152	CLOSED	D.Y	∢ CLOSED			
SOV-3167A	Sump Line SNL-3153	CLOSED	dd	د CLOSED	Seo L		
SOV-3167B	Sump Line SNL-3153	CLOSED	AL	x CLOSED	10		
SOV-3165B	SLL-3160	OPEN	D. St.	× OPEN	A		
SOV-3166B	SLL-3160	OPEN	D.S.	x CLOSED	AD L		
SOV-3168A	Vent Line SLL-3160	CLOSED	B.Y	CLOSED	100		
SOV-3168B	Vent Line SLL-3160	CLOSED	9.4	CLOSED	10		

#### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 125 OF 132 HNF-1857

REVISION NO. \_0\_

ATTACHMENT A

	APPENDIX F-1 - Trans	fer Scheme 2A	Valve Alignm	ent	
VALVE NO.	DESCRIPTION	MCS INITIALS POSITION		LOCAL POSITION	INITIALS
	Pump P-3125A	Motor Operated '	Valves		4.0
MOV-3125AA	P-3125A Drain Valve	CLOSED	229	CLOSED /	12/19
MOV-3125AB	P-3125A Drain Valve	CLOSED	Đ.Ÿ.	CLOSED /	1
MOV-3125AC	P-3125A Drain Valve	CLOSED	D.H.	CLOSED	CHO
MOV-3125AD	P-3125A Drain Valve	CLOSED	D, <i>H</i> .	CLOSED 🗸	20
MOV-3125AE	P-3125A Drain Valve	CLOSED	D.G.	CLOSED 🗸	De
MOV-3125AF	P-3125A Drain Valve	CLOSED	D. H.	CLOSED 🗸	900
MOV-3125AG	P-3125A Drain Valve	CLOSED	9.9	CLOSED 🗸	8
MOV-3125AH	P-3125A Drain Valve	CLOSED	P.J.	CLOSED 🗸	Oka
MOV-3125AJ	P-3125A Drain Valve	CLOSED	19,5%.	CLOSED 🗸	Ste
MOV-3125AK	P-3125A Vent Valve	CLOSED	ŶŊ,	CLOSED /	
	P-3125B Mo	otor Operated Val	ves		¥
MOV-3125BA	P-3125B Drain Valve	CLOSED	D.J.	CLOSED 🗸	De 12/19
MOV-3125BB	P-3125B Drain Valve	CLOSED	24	CLOSED 🗸	app 1
MOV-3125BC	P-3125B Drain Valve	CLOSED	E). H.	CLOSED /	AR I
MOV-3125BD	P-3125B Drain Valve	CLOSED	D. W.	CLOSED 🗸	Sec
MOV-3125BE	P-3125B Drain Valve	CLOSED	2.9/	CLOSED ~	900
MOV-3125BF	P-3125B Drain Valve	CLOSED	D. D	CLOSED ~	SO
MOV-3125BG	P-3125B Drain Valve	CLOSED	D.H	CLOSED ✓	A l
MOV-3125BH	P-3125B Drain Valve	CLOSED.	0.9/	CLOSED 🗸	<i>QR</i>
MOV-3125BJ	P-3125B Drain Valve	CLOSED	D.J	CLOSED 🗸	A l
MOV-3125BK	P-3125B Vent Valve	CLOSED	DA	CLOSED 🗸	ya v

Local Verifications by: JEINUKS

Verifications by:

P.J. ELMENDORF PRINT NAME

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 126 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

	APPENDIX F-2 - Trans	fer Scheme 2B	Valve Alignr	ment	
VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	LOCAL POSITION	INITIALS
CLOSED; Green,	valve position is given by color and designates OPEN, Red, designates F ndicator on SOV's.	d fill of valve AILED. Local in	on computer sc dication (OPEN	reen. White, de /CLOSED) is give	signates n by valve
	Solemoid Operato	ed Valves in Div	ersion Box 7/_	1	
SOV-3182A	SNL-3150	CLOSED	D.S. 11/	CLOSED .	D.G 3/17/98
· SOV-3182B	SNL-3150	CLOSED	Dil	CLOSED	
SOV-3184	SNL-3150	CLOSED	Del	OPEN	
SOV-3173A	Sump Line SNL-3151	CLOSED	09.	CLOSED	
SOV-3173B	Sump Line SNL-3151	CLOSED	DJ.	CLOSED	
SOV-3183A	SLL-3160	OPEN	1 N. O	CLOSED	
SOV-3183B	SLL-3160	OPEN	D.H.	CLOSED	
SOV-3163	Pump Bypass SLL-3160	CLOSED	P.H.	CLOSED	
SOV-3125E	P-3125A Intake SLL-3163	CLOSED	D. 91,	CLOSED	
SOV-3125C	P-3125A Discharge SLL-3163	CLOSED.	D. H.	CLOSED	
SOV-3125G	P-3125B Intake SLL-3164	CLOSED	8.98.	CLOSED.	
SOV-3125D	P-3125B Discharge SLL-3164	CLOSED	D.H.	CLOSED	
		LCHAPA	80 Pensrop	8./6	<u> </u>
	Solenoid Operat	ed Valves in Ver	nt Station 🔏		
SOV-3165A	SNL-3150	CLOSED	D.J.J.	OPEN	D. H 2/17/2
SOV-3166A	SNL-3150	CLOSED	Def.	CLOSED	
SOV-3185A	Vent Line SNL-3152	CLOSED	D. Id.	CLOSED	:
SOV-3185B	Vent Line SNL-3152	CLOSED	Del.	CLOSED	
SOV-3167A	Sump Line SNL-3153	CLOSED	D. S.	CLOSED	
SOV-3167B	Sump Line SNL-3153	CLOSED	8.2	CLOSED	
SOV-3165B	SLL-3160	OPEN	8.D.	OPEN	
SOV-3166B	SLL-3160	OPEN	B.H.	CLOSED	
SOV-3168A	Vent Line SLL-3160	CLOSED	S.S.	CLOSED	
SOV-3168B	Vent Line SLL-3160	CLOSED	9.9/	CLOSED	1

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 127 OF 132

REVISION NO. 0

ATTACHMENT A

	APPENDIX F-2 - Trans	sfer Scheme 2B	Valve Alignr	nent	·	
VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	LOCAL POSITION	INITIALS	
	Pump P-3125	A Motor Operated	Valves			
MOV-3125AA	P-3125A Drain Valve	CLOSED	D. H. 47/9x	CLOSED	D.4	: 3/11/
MOV-3125AB	P-3125A Drain Valve	CLOSED		CLOSED	<u>-</u>	
MOV-3125AC	P-3125A Drain Valve	CLOSED		CLOSED		
MOV-3125AD	P-3125A Drain Valve	CLOSED		CLOSED		
MOV-3125AE	P-3125A Drain Valve	CLOSED		CLOSED		
MOV-3125AF	P-3125A Drain Valve	CLOSED		CLOSED		
MOV-3125AG	P-3125A Drain Valve	CLOSED		CLOSED		
MOV-3125AH	P-3125A Drain Valve	CLOSED		CLOSED		
MOV-3125AJ	P-3125A Drain Valve	CLOSED		CLOSED		
MOV-3125AK	P-3125A Vent Valve	CLOSED	V	CLOSED	,	4
	P-31258 I	Motor Operated Va	lves			
MOV-3125BA	P-3125B Drain Valve	CLOSED	D. H. 2/1/8	CLOSED	D.4.	2/11/9
MOV-3125BB	P-3125B Drain Valve	CLOSED	1	CLOSED		
MOV-3125BC	P-3125B Drain Valve	CLOSED		CLOSED		
MOV-3125BD	P-3125B Drain Valve	CLOSED		CLOSED		
MOV-3125BE	P-3125B Drain Valve	CLOSED		CLOSED		
MOV-3125BF	P-3125B Drain Valve	CLOSED		CLOSED		
MOV-3125BG	P-3125B Drain Valve	CLOSED		CLOSED		
MOV-3125BH	P-3125B Drain Valve	CLOSED		CLOSED		
MOV-3125BJ	P-3125B Drain Valve	CLOSED		CLOSED		
MOV-3125BK	P-3125B Vent Valve	CLOSED		CLOSED	1	/

Local Verifications by:  $\frac{Doub}{PRINT} \frac{Gence}{NAME} = \frac{D.G.}{INITIALS} = \frac{2/17/98}{DATE}$ Verifications by:  $\frac{Ken Willsoghbi}{Verifications} = \frac{Verifications}{Verifications} = \frac{Verifications}{Verificat$ 

HNF-2504, REV. 0 ATTACHMENT | PAG틱기

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 128 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

·	APPENDIX F-3 - Trans	fer Scheme 2A	Valve Alignm	ient.	
VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	LOCAL POSITION	INITIALS
CLOSED; Green,	valve position is given by color and designates OPEN, Red, designates Fundicator on SOV's.	d fill of valve AILED. Local in	on computer scr dication (OPEN/	reen. White, de CLOSED) is give	esignates en by valve
	Solenoid Operato	ed Valves in Div			
SOV-3182A	SNL-3150	CLOSED	D.4 2/2/98	CLOSED	D. y 2/26/18
\$0V-3182B	SNL-3150	CLOSED	Ì	CLOSED	
SOV-3184	SNL-3150	CLOSED .		OPEN	
S0V-3173A	Sump Line SNL-3151	CLOSED		CLOSED	
SOV-3173B	Sump Line SNL-3151	CLOSED		CLOSED	
SOV-3183A	SLL-3160	OPEN		CLOSED	
SOV-3183B	SLL-3160	OPEN		CLOSED	
SOV-3163	Pump Bypass SLL-3160	CLOSED		CLOSED	
S0V-3125E	P-3125A Intake SLL-3163	CLOSED		CLOSED	
SOV-3125C	P-3125A Discharge SLL-3163	CLOSED		CLOSED	
SOV-3125G	P-3125B Intake SLL-3164	CLOSED		CLOSED	
SOV-3125D	P-3125B Discharge SLL-3164	. CLOSED		CLOSED	1
	   Solenoid Operat	ed Valves in Ver	nt Station	L	]
SOV-3165A	SNL-3150	CLOSED	D9 44/48	OPEN	D. 912/26/98
SOV-3166A	SNL-3150	CLOSED		CLOSED	
SOV-3185A	Vent Line SNL-3152	CLOSED		CLOSED	
SOV-3185B	Vent Line SNL-3152	CLOSED		CLOSED	
SOV-3167A	Sump Line SNL-3153	CLOSED		CLOSED	
SOV-3167B	Sump Line SNL-3153	CLOSED		CLOSED	
SOV-3165B	SLL-3160	OPEN		OPEN	
SOV-3166B	SLL-3160	OPEN		CLOSED	
SOV-3168A	Vent Line SLL-3160	CLOSED		CLOSED	
SOV-3168B	Vent Line SLL-3160	CLOSED		CLOSED	<b>✓</b>

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 129 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

	APPENDIX F-3 - Trans	fer Scheme 2A	Valve Alignm	ent	
VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	LOCAL POSITION	INITIALS
	Pump P-3125	A Motor Operated	Valves		
MOV-3125AA	P-3125A Drain Valve	CLOSED	D. D. 2/26/9	CLOSED	D. Stz/z6/58
MOV-3125AB	P-3125A Drain Valve	CLOSED	Ì	CLOSED	]
MOV-3125AC	P-3125A Drain Valve	CLOSED		CLOSED	
MOV-3125AD	P-3125A Drain Valve	CLOSED		CLOSED	
MOV-3125AE	P-3125A Drain Valve	CLOSED		CLOSED	
MOV-3125AF	P-3125A Drain Valve	CLOSED ,		CLOSED	
MOV-3125AG	P-3125A Drain Valve	CLOSED		CLOSED	
MOV-3125AH	P-3125A Drain Valve	CLOSED		CLOSED	,
MOV-3125AJ	P-3125A Drain Valve	CLOSED		CLOSED	
40V-3125AK	P-3125A Vent Valve	CLOSED	<b>1</b>	CLOSED	1
	P-3125B N	Motor Operated Va	lves		
MOV-3125BA	P-3125B Drain Valve	CLOSED	D-2/26/58	CLOSED	D. H 2/26/98
MOV-3125BB	P-3125B Drain Valve	CLOSED		CLOSED	
MOV-3125BC	P-3125B Drain Valve	CLOSED		CLOSED	
MOV-3125BD	P-3125B Drain Valve	CLOSED		CLOSED	
MOV-3125BE	P-3125B Drain Valve	CLOSED		CLOSED	
MOV-3125BF	P-3125B Drain Valve	CLOSED		CLOSED	
MOV-3125BG	P-3125B Drain Valve	CLOSED		CLOSED	
MOV-3125BH	P-3125B Drain Valve	CLOSED		CLOSED	
MOV-3125BJ	P-3125B Drain Valve	CLOSED		CLOSED	
MOV-3125BK	P-3125B Vent Valve	CLOSED	V	CLOSED	V

Local Verifications by: Doub Genker 111 INITIALS DATE

Verifications by: Doub Genker Dy 2/16/98

PRINT NAME

HNF-2504, REV. 0 ATTACHMENT | PAGE 13

## PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 130 OF 132

REVISION NO. 0

ATTACHMENT A

	APPENDIX F-4 - Tran	sfer Scheme 2B	Valve Alignm	nent		
VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	LOCAL POSITION	INITIALS	
CLOSED; Green,	valve position is given by color a designates OPEN, Red, designates ndicator on SOV's.					
	Solenoid Opera	ted Valves in Dive	ersion Box			
SOV-3182A	SNL-3150	3/29/08 ED OPEN	D. H/3 214	CLOSED	SE YAK	
SOV-3182B	SNL-3150	GLOSED OPEN		CLOSED	1	
ŠOV-3184	SNL-3150	GLOSED-OPEN		OPEN		
SOV-3173A	Sump Line SNL-3151	CLOSED		CLOSED		
SOV-3173B	Sump Line SNL-3151	CLOSED		CLOSED		
SOV-3183A	SLL-3160	Forcep OPEN		CLOSED		
SOV-3183B	SLL-3160	95 FORCES 3/21/98 OPEN		CLOSED		
SOV-3163	Pump Bypass SLL-3160	CLOSED		CLOSED		
SOV-3125E	P-3125A Intake SLL-3163	CLOSED		CLOSED		
SOV-3125C	P-3125A Discharge SLL-3163	CLOSED		CLOSED		
SOV-3125G	P-3125B Intake SLL-3164	CLOSED		CLOSED		
SOV-3125D	P-3125B Discharge SLL-3164	CLOSED		CLOSED		
	Solenoid Opera	ted Valves in Ven	t Station			
SOV-3165A	SNL-3150	DO 3/29/98 OPEN GLOSED.	D. 4. 3/29/gs	OPEN	ME 429/8	
SOV-3166A	SNL-3150	GLOSED PONCED	)	CLOSED	OE (	
SOV-3185A	Vent Line SNL-3152	CLOSED		· CLOSED .	AE \	
SOV-3185B	· Vent Line SNL-3152	CLOSED		CLOSED	47	
SOV-3167A	Sump Line SNL-3153	CLOSED		CLOSED	AE	
SOV-3167B	Sump Line SNL-3153	CLOSED		CLOSED	St	
SOV-3165B	SLL-3160	OPEN		OPEN	# Z	
SÓV-3166B	SLL-3160	3/2478 OPEN		CLOSED	SE.	
SOV-3168A	Vent Line SLL-3160	CLOSED		CLOSED	HE.	
SOV-3168B	Vent Line SLL-3160	CLOSED	1	CLOSED	Ac.	

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 131 OF 132

REVISION NO. 0

ATTACHMENT A

APPENDIX F-4 - Transfer Scheme 2B Valve Alignment								
VALVE NO.	DESCRIPTION	MCS POSITION	INITIALS	LOCAL POSITION	INITIALS			
	Pump P-3125 <i>t</i>	A Motor Operated	Valves					
MOV-3125AA	P-3125A Drain Valve	CLOSED	D.G./3/2990	✓ CLOSED ✓	1 3/2478			
MOV-3125AB	P-3125A Drain Valve	CLOSED		CLOSED				
MOV-3125AC	P-3125A Drain Valve	CLOSED		CLOSED				
MOV-3125AD	P-3125A Drain Valve	CLOSED		CLOSED				
MOV-3125AE	P-3125A Drain Valve	CLOSED		CLOSED				
MOV-3125AF ·	P-3125A Drain Valve	CLOSED		CLOSED				
MOV-3125AG	P-3125A Drain Valve	CLOSED		CLOSED				
MOV-3125AH	P-3125A Drain Valve	CLOSED		CLOSED				
MOV-3125AJ	P-3125A Drain Valve	CLOSED		CLOSED				
MOV-3125AK	P-3125A Vent Valve	CLOSED	1	CLOSED	V			
	P-3125B M	otor Operated Va	lves					
MOV-3125BA	P-3125B Drain Valve	CLOSED	D.G./3/24/98	CLOSED	YE 34h			
MOV-3125BB	P-3125B Drain Valve .	CLOSED	1	CLOSED	953 JAPRE			
MOV-3125BC	P-3125B Drain Valve	CLOSED		CLOSED	8			
MOV-3125BD	P-3125B Drain Valve	CLOSED		CLOSED				
MOV-3125BE	P-3125B Drain Valve	CLOSED		CLOSED				
MOV-3125BF	P-3125B Drain Valve	CLOSED		CLOSED				
MOV-3125BG	P-3125B Drain Valve	CLOSED		CLOSED				
MOV-3125BH	P-3125B Drain Valve	CLOSED		CLOSED				
MOV-3125BJ	P-3125B Drain Valve	CLOSED		CLOSED				
MOV-3125BK	P-3125B Vent Valve	CLOSED	1	CLOSED				

Local Verifications by:

Seneriente e

INITIALS

7/24/98 DATE

Verifications by:

PRINT NAME

<u>8.9</u> INITIALS 3/24/98 DATE

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 132 OF 132

REVISION NO. 0

ATTACHMENT A

50% SPEER

	Appendix	G - System	Data Sheet		) 0/ 00	. /
Item	Description					
Pump ID	P-3125% or B	P-31250	P-3125A			
Proc. Step No.	Procedure Step Number	7,30	7.32			
Date	Date	2/13/98	43/98			· · · · · · · · · · · · · · · · · · ·
Time	Time, hr:min	19:05 Pax	19" 150	·		
Test Instrumentati	on					
FI-temp	System Flow, gpm	98.	105			
PI-temp-1	Supply Pressure, psig	, 55	35			
PI-temp-2	Press. upstream V-temp-2, psig	-69	654			
PI-temp-3	Return Pressure, psig	1-)5	3109			
Pump Statistics (o	perating booster pump, from PCU-2 s	creen on MCS)				
TI-3125A1 B1	Thrust End Bearing Temp, °F	64'	65			
3125A2, B2	Drive End Bearing Temp, °F	66	71			
SI-3125A. B	Motor Speed, rpm	1715	1726			
VI-3125A1, B1	Thrust End Vibration, mils	Ø0.01	0.01	•	·	
VI-3125A2/, B2	Drive End Vibration, mils	0.01	0:01			
FIC-3125 PV	Fluid Flow Present Value, gpm	101	99			
FIC-3125 SP	Fluid Flow Set Point, gpm	120	120			
TI-3125A	Fluid Temp, °F	62	62			
PI-3125A. B	Fluid Inlet Pressure, psig	58	59			
PI-3125C D	Fluid Outlet Pressure, psig	260	262			
Header Data (from	PCU-2 and PCU-3 screens on MCS)					,
PI-3126B	SLL-3160 Press, Vent Sta. psig	125	128			
TI-3126B	SLL-3160 Temp; Vent Sta. °F	64	52			
TI-3126A (*)	SNL-3150 Temp, Vent Sta, °F	·52	62			, à
TI-3125B	SNL-3150 Temp, Div Box, °F	59	68			.87

LOCAL TACK TEMP 62 F

(Make copies of this sheet as required)

(x) Note: TI-3126A located in dead leg of SNL; not representative of Eiravit temperature.

Data Recorder: Doub GERKEN

DY.

2/13/98

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST

HNF-1857 ATTACHMENT A

REVISION NO. 0

PAGE 132 OF 132

60% SPEED

				10 2	·	
	Appendix	G - System	Data Sheet	,		
Item	Description					
Pump ID	(P-3125A) or B	P-3125A	P-3125A			
Proc. Step No.	Procedure Step Number	7.40	7,41			
Date	Date	2/13/98	2/13/98			
Time	. Time, hr:min	19:45	19:55			
Test Instrumentati	on					
FI-temp .	System Flow, gpm	119	121			
PI-temp-1	Supply Pressure, psig	48	-48			
PI-temp-2	Press. upstream V-temp-2, psig	0	0			
PI-temp-3	Return Pressure. psig	0	, O			
Pump Statistics (c	perating booster pump, from PCU-2 s	screen on MCS)				
TI-3125A), B1	Thrust End Bearing Temp, °F	.67	68			
3125A2, B2	Drive End Bearing Temp, °F	75	76	·		
SI-3125A, B	Motor Speed, rpm	2094	2082			,
VI-3125A1 B1	Thrust End Vibration, mils	0,02	0.02	•		
VI-3125A2, B2	Drive End Vibration, mils	0.02	0.02			
FIC-3125 PV	Fluid Flow Present Value, gpm	125	124			
FIC-3125 SP	Fluid Flow Set Point, gpm	144	144			
TI-3125A	Fluid Temp, °F	64	65			
PI-3125A. B	Fluid Inlet Pressure, psig	50	49			
PI-3125C D	Fluid Outlet Pressure, psig	315	316			
Header Data (from	PCU+2 and PCU+3 screens on MCS)			,	·	
PI-3126B	SLL-3160 Press, Vent Sta, psig	128	128			
TI-3126B	SLL-3160 Temp, Vent Sta, °F	62	62			
TI-3126A	SNL-3150 Temp, Vent Sta, °F	52	52			
TI-3125B	SNL-3150 Temp, Div Box, °F	<b>52</b> 64	64			

(Make copies of this sheet as required)

9.97 4,5/48

Data Recorder:

### PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST

REVISION NO. <u>0</u>

HNF-1857

ATTACHMENT A

PAGE 132 OF 132

	Appendix	G - System	Data Sheet			
Item	Description					
Pump ID	P-3125A or B	P-3125A	P-3125A			
Proc. Step No.	Procedure Step Number	7.47	7.48			
Date	Date	2/13/98	2/13/98			
Time	Time, hr:min	20:10	20:20			<u> </u>
Test Instrumentat	ion					
FI-temp	System Flow, gpm	139	140			
PI-temp-1	Supply Pressure, psig	44	99			
PI-temp-2	Press. upstream V-temp-2. psig	<	<1			
PI-temp-3	Return Pressure, psig	.<1	<			
Pump Statistics (	operating booster pump, from PCU-2 s	creen on MCS)				
TI-312541, B1	Thrust End Bearing Temp, °F	68	69			
3125A2\ B2	Drive End Bearing Temp, °F	28	79			
SI-3125A. B	Motor Speed, rpm	2470	2460			
VI-3125A1 B1	Thrust End Vibration, mils	0.03	0.63	•	·	
VI-312942. B2	Drive End Vibration, mils	0.02	0.02			
FIC-3125 PV	Fluid Flow Present Value, gpm	145	145			
FIC-3125 SP	Fluid Flow Set Point, gpm	168	168			
TI-3125A	Fluid Temp. °F	65	65			
PI-3125A. B	Fluid Inlet Pressure, psig	43	43			
PI-3125C D	Fluid Outlet Pressure, psig	407	410	·		
Header Data (from	n: PCU42: and: PCU43: screens on: MCS)				· · · · · · · · · · · · · · · · · · ·	
PI-3126B	SLL-3160 Press, Vent Sta. psig	178	178			
TI-3126B	SLL-3160 Temp, Vent Sta, °F	52	63			
TI-3126A	SNL-3150 Temp, Vent Sta, °F	52	52			
TI-3125B	SNL-3150 Temp, Div Box, °F	64	62			

(Make copies of this sheet as required)

Data Recorder: DOUG GER

HNF-1857

REVISION NO. \_0\_

ATTACHMENT A

PAGE 132 OF 132

				0 ~	/	7 000
	Appendix	G - System	Data Sheet		.	- Fatotopiosoppiosoppiosoppios
Item	Description					
Pump ID	P-3125A or B	P-3125A	P-3115A			
Proc. Step No.	Procedure Step Number	7.54	7.55			
Date	Date	2/13/98	NA			
Time	Time, hr:min	20:25				
Test Instrumentati	or					
FI-temp	System Flow, gpm	158				
PI-temp-1	Supply Pressure, psig	38				
PI-temp-2	Press. upstream V-temp-2, psig	11				
PI-temp-3	Return Pressure, psig	3			<u> </u>	
1 A A	perating booster pump, from PCU-2's	creen on MCS)				
TI-3125AI BO	Thrust End Bearing Temp, °F	71			ļ	
3125A2 B2	Drive End Bearing Temp, °F	81				1
SI-3125A. B \ \	Motor Speed, rpm	2845				
VI-3125A1\.B1\	Thrust End Vibration, mils	0.0)				
VI-3125A2 82	Drive End Vibration, mils	0.05				
FIC-3125 PV	Fluid Flow Present Value, gpm	. 165				
FIC-3125 SP	Fluid Flow Set Point, gpm	192				
TI-3125A	Fluid Temp, °F	65				
PI-3125A B	Fluid Inlet Pressure, psig	<u> </u>				
PI-3125C (D)	Fluid Outlet Pressure, psig	5/4				
Header Data (from	PCU-2 and PCU-3 screens on MCS)				1	
PI-3126B	SLL-3160 Press, Vent Sta. psig	231				
TI-3126B	SLL-3160 Temp, Vent Sta. °F	64				· · · · · · · · · · · · · · · · · · ·
TI-3126A	SNL-3150 Temp, Vent Sta. °F	52				
TI-3125B	SNL-3150 Temp. Div Box. °F	62				

(Make copies of this sheet as required)

Data Recorder:

HNF-1857

PAGE 132 OF 132

REVISION NO. \_0\_

ATTACHMENT A

50% SPEED

				W//// 70 )	OGPM	Pen		101
	Appendix	G - System	Data Sheet	į.				
Item	Description							
Pump ID	P-3125A or B	i						
Proc. Step No.	Procedure Step Number	PER SBI REQUE	<b>3</b> T					
Date	Date	2/1)/98						
Time	Time, hr:min	0.925						
Test Instrumentat	ion							
FI-temp	System Flow, gpm	70						
PI-temp-1	Supply Pressure, psig	62						
PI-temp-2	Press. upstream V-temp-2, psig	155						,
PI-temp-3	Return Pressure. psig	0						
Pump Statistics (	operating booster pump, from PCU-2	screen on MCS)						
II-3125A1 / B1	Thrust End Bearing Temp. °F	61						
3125A2 B2	Drive End Bearing Temp. °F	61						
SI-3125A. 8	Motor Speed, rpm	1650						
VI-3125A1, B1	Thrust End Vibration, mils	0.01		-				
VI-3125A2. B2	Drive End Vibration, mils	0.0/		•				
FIC-3125 PV	Fluid Flow Present Value, gpm	76						
FIC-3125 SP	Fluid Flow Set Point, gpm	120						
TI-3125A	Fluid Temp, °F	50					ļ	
PI-3125A B	Fluid Inlet Pressure, psig	66			·			
PI-3125C D	Fluid Outlet Pressure, psig	287			·		20	and see a
Header Data (from	PCU-2 and PCU-3 screens on MCS)			T			T T	
PI-3126B	SLL-3160 Press, Vent Sta. psig	184					<u> </u>	
TI-3126B	SLL-3160 Temp, Vent Sta. °F	49		<u> </u>				
TI-3126A	SNL-3150 Temp, Vent Sta. °F	52						
TI-3125B	SNL-3150 Temp, Div Box. °F	50					<u> </u>	

(Make copies of this sheet as required)

Data Recorder: \_

HNF-1857

PAGE 132 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

75% SPEED WITH VALUE THROTTLED TO 1054PM PER PUMP CORVE

	Appendix	G - System	Data Sheet			
Item	Description					
Pump ID	P-3125A or B		(SBI)			
Proc. Step No.	Procedure Step Number	PER SULE	<b>e</b> s7			
Date	Date	Zhlge				
Time	Time, hr:min	09:35				
Test Instrumentation	nc					
FI-temp	System Flow, gpm	105				
PI-temp-1	Supply Pressure, psig	55				
PI-temp-2	Press. upstream V-temp-2, psig	310	,			
PI-temp-3	Return Pressure, psig	0				
Pump Statistics (o	perating booster pump. from PCU-2 s	screen on MCS)				
TI-3125A1 B1	Thrust End Bearing Temp. °F	6.5				
125A2 B2	Drive End Bearing Temp. °F	65				
SI-3125A.B	Motor Speed, rpm	2608				
VI-3125A1 B1	Thrust End Vibration, mils	0.07		•		
VI-312502 B2	Drive End Vibration, mils	0.04				
FIC-3125 PV	Fluid Flow Present Value, gpm	+4180				
FIC-3125 SP	Fluid Flow Set Point, gpm	51				
TI-3125A	Fluid Temp. °F	SI				
PI-3125A B	Fluid Inlet Pressure. psig	57				
PI-3125C D	Fluid Outlet Pressure. psig	570				<u></u>
Header Data (from	PCU-2 and PCU-3 screens on MCS)					
PI-3126B	SLL-3160 Press. Vent Sta. psig	404				
TI-3126B	SLL-3160 Temp. Vent Sta. °F	49				
TI-3126A	SNL-3150 Temp. Vent Sta. °F	52				
TI-3125B	SNL-3150 Temp. Div Box. °F	50			<u> </u>	

(Make copies of this sheet as required)

Data Recorder:

DOUG GERKGU PRINT NAME D. &

2/1)/98 DATE

F 2504 REV 0 ATTACHMENT | PAGE (8)

HNF-1857

PAGE 132 OF 132

REVISION NO. 0

ATTACHMENT A 100% SPEED WITH UALUE TANOTTIES TO 140 GPT

				THAOTT	ceo to	170GP~
	Appendix	G - System	Data Sheet			····
Item	Description					
Pump ID	P-3125A or B	4	200- (50)			
Proc. Step No.	Procedure Step Number	per 500	2 er (502)			,
Date	Date	2/17/98	2/17/98			
Time	Time. hr:min	0.9:45	09:55			
Test Instrumentatio	nd					
FI-temp	System Flow, gpm	<b>45</b> 132	37			
PI-temp-1	Supply Pressure. psig	45	161			
PI-temp-2	Press. upstream V-temp-2, psig	543	310			
PI-temp-3	Return Pressure, psig	0	9			
Pump Statistics (o	perating booster pump, from PCU-2 s	creen on MCS)				
TI-3125A1 B1	Thrust End Bearing Temp. °F	69	75			
125A2 B2	Drive End Bearing Temp. °F	68	72			
SI-3125A. B	Motor Speed. rpm	3529 JUNGED TOOS	3522			
VI-3129A1 B1	Thrust End Vibration, mils	JUNGED TOUS	@ 250 pp ~ (SD)			
VI-3129A.Z. B2	Drive End Vibration, mils	0.06	0.06			
FIC-3125 PV	Fluid Flow Present Value. gpm	148	123			
FIC-3125 SP	Fluid Flow Set Point, gpm	290	240			
TI-3125A	Fluid Temp. °F	53	<u>53</u> 33			
PI-3125A B	Fluid Inlet Pressure. psig	52	33			
PI-3125C. D	Fluid Outlet Pressure, psig	931	871			
Header Data (from )	PCU-2 and PCU-3 screens on MCS)					
PI -3126B	SLL-3160 Press. Vent Sta. psig	62,4	<i>S</i> 57			
ŢI -3126B	SLL-3160 Temp. Vent Sta. °F	49	50			
TI-3126A	SNL-3150 Temp, Vent Sta. °F	52	82	·		
TI-3125B	SNL-3150 Temp. Div Box. °F	5/	51			

(Make copies of this sheet as required)

Data Recorder: 2004 GENKEY
PRINT NAME

ATTACHMENT | PAGE 182-HNF-2504, REV. 0



REVISION NO. 0

ATTACHMENT A

AT

			Data Sheet			
Item	Description					
Pump ID	(P-3125A) or B					
Proc. Step No.	Procedure Step Number	pen source	7			
Date	Date	2/20/98				
Time	Time, hr:min	10:53	- " - " - " - " - " - " - " - " - " - "			
Test Instrumentati	on					
FI-temp	System Flow, gpm	102				
PI-temp-1	Supply Pressure, psig	58		· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·	
PI-temp-2	Press. upstream V-temp-2. psig	910				
PI-temp-3	Return Pressure, psig	11				
Pump Statistics (o	perating booster pump, from PCU-2:	screen on MCS)				
TI-3125A1. B1	Thrust End Bearing Temp. °F	62				
125A2. B2	Orive End Bearing Temp. °F	69				
SI-3123A. B	Motor Speed, rpm	270/				
VI-3125A1 B1	Thrust End Vibration, mils	0.0)		,		
VI-3125/2. B2	Drive End Vibration, mils	0.04				
FIC-3125 PV	Fluid Flow Present Value, gpm	107				
FIC-3125 SP	Fluid Flow Set Point, gpm	180				
TI-3125A	Fluid Temp, °F	52				
PI-312 <b>5</b> A 8	Fluid Inlet Pressure, psig	58				
PI-3125C D	Fluid Outlet Pressure, psig	647				
Header Data (from	PCU-2 and PCU-3 screens on MCS)					
PI-3126B	SLL-3160 Press, Vent Sta. psig	491		· · · · · · · · · · · · · · · · · · ·		
TI-3126B	SLL-3160 Temp. Vent Sta. °F	5/				
TI-3126A	SNL-3150 Temp. Vent Sta. °F	53		, 		
TI-3125B	SNL-3150 Temp. Div Box. °F	51				

(Make copies of this sheet as required)

Data Recorder: DOUL GERRES
PRINT NAME

HNF-2504, REV. 0 ATTACHMENT | PAGE 185

REVISION NO. 0

ATTACHMENT A

PAGE 132 OF 132

A pump Q 100 %

			FCOW SI	st 70 15	7 GP~	
	<u>Appendix</u>	G - System	Data Sheet		***************************************	
Item	Description					ja salah
Pump ID	P-3125A or B	. 6017	er )			
Proc. Step No.	Procedure Step Number	per solz person	(382)			
Date	Date	2/20/98	2/20/98	2/24/98		
Time	Time, hr:min	11.30	11:35	12:10		
Test İnstrumentat	ion					
FI-temp	System Flow, gpm	143	145	143		
PI-temp-1	Supply Pressure. psig	44	39	40		
PI-temp-2	Press. upstream V-temp-2. psig	550	490	592		
PI-temp-3	Return Pressure, psig	3		3		
Pump Statistics (	operating booster pump, from PCU-2:	screen on MCS)				
TI-3125A1 B1	Thrust End Bearing Temp, °F	74	78	79		
B125A2 B2	Drive End Bearing Temp, °F	)2	76	77		
SI-3125A, B	Motor Speed, rpm	3608	3611	3610		
VI-3125A1, B1	Thrust End Vibration, mils	0.08	0.08	0.08		
VI-3125A2 B2	Drive End Vibration, mils	0.06	0.06	0.05		
FIC-3125 PV	Fluid Flow Present Value. gpm	157	169	152		
FIC-3125 SP	Fluid Flow Set Point, gpm	240	240	240		
TI-3125A	Fluid Temp, °F	54	54	55		
PI-3125A. 8	Fluid Inlet Pressure, psig	41	36	43		
PI-3125C/D	Fluid Outlet Pressure, psig	1026	974	1039		
1 2 1 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	PCU-2 and PCU-3 screens on MCS)					Salar Sa
PI-3126B	SLL-3160 Press, Vent Sta. psig	758	678	781		
TI-3126B	SLL-3160 Temp, Vent Sta, °F	51	SZ	54		
TI-3126A	SNL-3150 Temp, Vent Sta. °F	54	54	54		
TI-3125B	SNL-3150 Temp, Div Box. °F	51	52	52		

(Make copies of this sheet as required)

Data Recorder: 0004 LEAKES PRINT NAME

REVISION NO. <u>0</u>

ATTACHMENT A

50% B-Pump

	Appendix	G - System	Data Sheet		<del></del>
Item	Description				5146
Pump ID	(P-3125)A or (B)	P-3125B	P-3125D		
Proc. Step No.	Procedure Step Number	8.32	8,33		
Date	Date	2/19/98	2/19/98		
Time	Time, hr:min	12:50	13:00		
Test Instrumentati	on				ngos as siy. An ana
FI-temp	System Flow, gpm	80	80		
PI-temp-1	Supply Pressure, psig	58	58		
PI-temp-2	Press. upstream V-temp-2, psig	130	120-130		
PI-temp-3	Return Pressure, psig	0	0		
Pump Statistics (o	perating booster pump, from PCU-2 s	screen on MCS)			
TI-3125A1, 81	Thrust End Bearing Temp. °F	64	64		
125A2 B2	Drive End Bearing Temp. °F	73	73		
SI-3125A, B	Motor Speed, rpm	1821	1826		
VI-3125A1. B1	Thrust End Vibration, mils	0,01	0.01		
VI-3125A2, B2	Drive End Vibration, mils	0.01	0.01		
FIC-3125 PV	Fluid Flow Present Value, gpm	84	83		
FIC-3125 SP	Fluid Flow Set Point, gpm	120	720		
TI-3125A	Fluid Temp. °F	5/	51		
PI-3125A. B	Fluid Inlet Pressure, psig	64	65		
PI-3125C. D	Fluid Outlet Pressure, psig	301	30	 <u> </u>	<u> </u>
Header Data (from	PCU-2 and PCU-3 screens on MCS)				
PI-3126B	SLL-3160 Press. Vent Sta. psig	181	186		
TI-3126B	SLL-3160 Temp, Vent Sta. °F	50	50		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	53	53		
TI-31258	SNL-3150 Temp. Div Box. °F	50	50		

(Make copies of this sheet as required)

Data Recorder: Doug GENKEY
PRINT NAME

HNF-2504, REV. 0 ATTACHMENT | PAGE 185

REVISION NO. 0

ATTACHMENT A

	Appendix (	G - System	Data Sheet			
Item	Description					
Pump ID	P-3125 or B	f-3125B	P-3125B			
Proc. Step No.	Procedure Step Number	8.42	8,43			
Date	Date	2/19/98	2/19/98			
Time	Time, hr:min	13:05	13:15			
Test Instrumentation	no					
FI-temp	System Flow, gpm	94	94			
PI-temp-1	Supply Pressure, psig	36	56			
PI-temp-2	Press. upstream V-temp-2, psig	180	180			
PI-temp-3	Return Pressure, psig	2	1	<u> </u>		
Pump Statistics (o	perating booster pump, from PCU-2 s	screen on MCS)				
TI-3125A1./B1	Thrust End Bearing Temp. °F	65	65			
125A2 B2	Drive End Bearing Temp. °F	74	25			
SI-3125A. B	Motor Speed, rpm	2200	2195			
VI-3125A1 B1	Thrust End Vibration, mils	0.03	0.03			
VI-3125A2. B2	Drive End Vibration, mils	0.02	0.02			
FIC-3125 PV	Fluid Flow Present Value, gpm	97	97			<u> </u>
FIC-3125 SP	Fluid Flow Set Point, gpm	@144	144			
TI-3125A	Fluid Temp, °F	51	51			ļ
PI-3125A. B	Fluid Inlet Pressure, psig	60	61			
PI-3125C. D	Fluid Outlet Pressure, psig	403	402		<u> </u>	<u></u>
Header Data (from	PCU-2 and PCU-3 screens on MCS)					
PI-3126B	SLL-3160 Press, Vent Sta. psig	260	257	ļ	ļ	
TI-3126B	SLL-3160 Temp, Vent Sta. °F	50	56	<u> </u>		
TI-3126A	SNL-3150 Temp, Vent Sta, °F	53	\$3		<u> </u>	
TI-3125B	SNL-3150 Temp, Div Box, °F	50	50			

(Make copies of this sheet as required)

Data Recorder: DOUL GERICER'
PRINT NAME

REVISION NO. 0

ATTACHMENT A B-Pump 70 %

	Appendix (	G - System	Data Sheet		
Item	Description				e in andere e
Pump ID	2-3125% or B	P-3125B	P-3125 B		
Proc. Step No.	Procedure Step Number	8.49	8.50	: :	
Date	Date	2/19/98	2/19/98		
Time .	Time, hr:min	13:20	13:30		
Test Instrumentati	on				
FI-temp	System Flow, gpm	110	110		
PI-temp-1	Supply Pressure, psig	<i>5</i> 3	53		
PI-temp-2	Press. upstream V-temp-2, psig	240	240		
PI-temp-3	Return Pressure, psig	9	@3		
Pump Statistics (o	perating booster pump, from PCU-2's	screen on MCS)			
TI-3125A1.B1	Thrust End Bearing Temp, °F	68	70		
125A2.B2	Orive End Bearing Temp, °F	75	77		
SI-3125A. (B)	Motor Speed, rpm	2560	2564		
VI-3125A1 B1	Thrust End Vibration, mils	0.03	0.03	•	
VI-3125A2. B2	Drive End Vibration, mils	0.03	0.03		
FIC-3125 PV	Fluid Flow Present Value, gpm	110	107		
FIC-3125 SP	Fluid Flow Set Point, gpm	168	168		
TI-3125A	Fluid Temp. °F	52	52		 
PI-3125A./B	Fluid Inlet Pressure. psig	56	53		
PI-3125C. D	Fluid Outlet Pressure, psig	522	300		
Header Data (from	PCU-2 and PCU-3 screens on MCS)				San
PI-3126B	SLL-3160 Press, Vent Sta. psig	398	352		
TI-3126B	SLL-3160 Temp. Vent Sta. °F	50	53		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	53	50		 
TI-3125B	SNL-3150 Temp. Div Box. °F	50	51		

(Make copies of this sheet as required)

Data Recorder: DOU 4 GENCEN
PRINT NAME

HNF-2504, REV. 0 ATTACHMENT | PAGE 18

REVISION NO. 0

ATTACHMENT A

B-PU~P 80%

<del></del>	Appendix	G - System	Data Sheet			
Item	Description			25, (3, 0, 4) (3) (1, 1, 1) (1)		
Pump ID	P-3125A or B	P-31250				
Proc. Step No.	Procedure Step Number	8.56	8.57			
Date	Date	2/19/98	2/19/98			
Time	Time, hr:min	14:05	14:15			
Test Instrumentati	on					
FI-temp	System Flow, gpm	120	123			
PI-temp-1	Supply Pressure, psig	49	49		<u> </u>	
PI-temp-2	Press. upstream V-temp-2, psig	310	3/0			
PI-temp-3	Return Pressure. psig	3	3			
Pump Statistics (o	perating booster pump, from PCU-2 s	screen on MCS)				
TI-3125A1. B1	Thrust End Bearing Temp. °F	70	72	-		
125A2. B2	Drive End Bearing Temp, °F	76	77			
SI-3125A. B	Motor Speed. rpm	2912	2916			
VI-3125A1 B1	Thrust End Vibration, mils	0.21	0,22			
VI-3125A2. B2	Drive End Vibration, mils	0.14	0,14	·		
FIC-3125 PV	Fluid Flow Present Value, gpm	123	123			
FIC-3125 SP	Fluid Flow Set Point, gpm	192	192			
TI-3125A	Fluid Temp. °F	534	<i>چ</i> ک			
PI-3125A, B	Fluid Inlet Pressure, psig	51	<i>31</i>			
PI-3125C. D	Fluid Outlet Pressure, psig	663	660			
Header Data (from	PCU-2 and PCU-3 screens on MCS)				Partale av i :	
PI-3126B	SLL-3160 Press. Vent Sta. psig	460	455			
TI-3126B	SLL-3160 Temp, Vent Sta. °F	51	51			
TI -3126A	SNL-3150 Temp, Vent Sta. °F	53	53			
TI-31258	SNL-3150 Temp. Div Box. °F	51	51			

(Make copies of this sheet as required)

Data Recorder: <u>0004 GENCE</u> PRINT NAME

HNF-1857

REVISION NO. 0

ATTACHMENT A

-pen succession

100% WITH VALVE THATTLED TO 140GP.

	Appendix	G - System	Data Sheet		
Item	Description				
Pump ID	P-3125% or (B)	P-31258	p-3125B		
Proc. Step No.	Procedure Step Number				
Date	Date	2/01/98	2/19/92		
Time	Time, hr:min	14-04-30	19:40		
Test Instrumentati	on				
FI-temp	System Flow, gpm	141	161)		
PI-temp-1	Supply Pressure, psig	143	38		
PI-temp-2	Press. upstream V-temp-2, psig	570	400		
PI-temp-3	Return Pressure, psig	3	4		
Pump Statistics (o	perating booster pump, from PCU-2 s	screen on MCS).			
TI-3125A1. B1	Thrust End Bearing Temp. °F	)6	78		
125A2 B2	Drive End Bearing Temp, °F	79	81		
SI-3125A B	Motor Speed. rpm	3650	3666		
VI-3125AI, B1	Thrust End Vibration, mils	0.06	0.06	,	
VI-3125A2. B2	Drive End Vibration, mils	0.03	0.04		 
FIC-3125 PV	Fluid Flow Present Value. gpm	/47	164		
FIC-3125 SP	Fluid Flow Set Point, gpm	240	240		
TI-3125A	Fluid Temp. °F	34	54		
PI-3125A. B	Fluid Inlet Pressure, psig	42	35		 
PI-3125C. D	Fluid Outlet Pressure, psig	1027	970		 
Header Data (from	PCU-2 and PCU-3 screens on MCS)				tanan da
PI-3126B	SLL-3160 Press. Vent Sta. psig	763	660		
TI-3126B	SLL-3160 Temp, Vent Sta. °F	51	52		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	83	53		 
TI-3125B	SNL-3150 Temp, Div Box. °F	51	51		

(Make copies of this sheet as required)

Data Recorder:

DOUG GENCEN
PRINT NAME

D.G.

2/19/98 DATE

HNF-2504. REV. 0 ATTACHMENT | PAGE 184

REVISION NO. 0

ATTACHMENT A

A-P

	Appendix	G - System	Data Sheet			
Item	Description					
Pump ID	P-3125A or B	P-3125A		7		
Proc. Step No.	Procedure Step Number	9.29	9.29	9.29		
Date	Date	2/26/98	2/26/98	2/26/98		
Time	Time, hr:min	14:30	14:40	14:50		
Test İnstrumentati		eri (f. Merce) 1800 - S				
FI-temp	System Flow, gpm	104	104	/03.8		
PI-temp-1	Supply Pressure, psig	36	56	56		
PI-temp-2	Press. upstream V-temp-2, psig	13	[3	13		
PI-temp-3	Return Pressure, psig	0	U	0		
Pump Statistics (c	perating booster pump, from PCU-2 s	screen on MCS)				38431 3461 - 15
TI-3125AN B1	Thrust End Bearing Temp. °F	67	67	67		
125A2. B2	Drive End Bearing Temp. °F	70	7/	71		·
SI-3126A, B	Motor Speed, rpm	1874	1873	187)		
VI-3125A1. B1	Thrust End Vibration, mils	0.01	0.0/	0.01		
VI-3125A2. B2	Drive End Vibration, mils	0.01	0.01	0.01		
FIC-3125 PV	Fluid Flow Present Value, gpm	110	1/0	1/0		
FIC-3125 SP	Fluid Flow Set Point. gpm	110	1/0	1/0		
TI-3125A	Fluid Temp, °F	51	52	52		
PI-3125A. B	Fluid Inlet Pressure, psig	59	58	58		
PI-3125C/D	Fluid Outlet Pressure, psig	272	273	274	L	
Header Data (from	PCU-2 and PCU-3 screens on MCS)					<u></u>
PI-3126B	SLL-3160 Press, Vent Sta. psig	108	109	109		
TI-31268	SLL-3160 Temp. Vent Sta. °F	51	51	51		
TI-3126A	SNL-3150 Temp, Vent Sta, °F	\$5	<u>55                                   </u>	<i>5</i> 5		
TI-31258	SNL-3150 Temp. Div Box, °F	50	<i>5</i> 0	50		

(Make copies of this sheet as required)

1

Data Recorder: <u>ρους</u>

PRINT NAME

D. H. INITIALS 2/<sub>26</sub>/98 DATE THIS PAGE INTENTIONALLY LEFT BLANK

REVISION NO. <u>0</u>

ATTACHMENT A

	Appendix	G - System	Data Sheet			
Item	Description				2 3 3 2 2 2 3 3 3 3 3 3 3 3 3 3 3 3 3 3	
Pump ID	(P-3125A)or B	P-3125A -		->		
Proc. Step No.	Procedure Step Number	9.35	9.35	9.35		
Date	Date	2/26/38	2/26/98	2/26/98	-	
Time	Time, hr:min	15:10	15.120	15:30		
Test Instrumentati	ón i de la companya de la companya de la companya de la companya de la companya de la companya de la companya d			26/98		
FI-temp	System Flow, gpm	104	107	108		
PI-temp-1	Supply Pressure, psig	56	56	56		
PI-temp-2	Press. upstream V-temp-2, psig	45	45	45		
PI-temp-3	Return Pressure, psig	3	4	4		
Pump Statistics (o	perating booster pump. from PCU-2's	creen on MCS)				
TI-3125A1 B1	Thrust End Bearing Temp, °F	67	67	68		
.125/\(\frac{1}{2}\) 82	Drive End Bearing Temp. °F	23	73	23		
ST-3125A. B	Motor Speed, rpm	1958	1965	1971		
VI-3125A1. B1	Thrust End Vibration, mils	0.0/	0.01	0.01		
VI-3125A2/ 82	Drive End Vibration, mils	0.0/	0.0/	0.00		
FIC-3125 PV	Fluid Flow Present Value, gpm	1/0	1/0	110		
FIC-3125 SP	Fluid Flow Set Point, gpm	110	116	110		
TI-3125A	Fluid Temp. °F	52	52	52		
PI-312\$A. B	Fluid Inlet Pressure, psig	58	58	58		
PI-3125C. D	Fluid Outlet Pressure, psig	30/	302	303		
Header Data (from	PCU-2 and PCU-3 screens on MCS)		<u> </u>		1	
PI-31268	SLL-3160 Press. Vent Sta. psig	139	136	137		
TI-31268	SLL-3160 Temp. Vent Sta. °F	51	51	51		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	55	<i>\$</i> 5	55		
TI-31258	SNL-3150 Temp, Div Box, °F	51	51	51		

(Make copies of this sheet as required)

Data Recorder:

DOUG GENKEN
PRINT NAME

D.D.

ZZ6/6/6 DATE

REVISION NO. 0

ATTACHMENT A

	Appendix	G - System	Data Sheet		
Item	Description				
Pump ID	P-3125A) or B	P-3125A		7	
Proc. Step No.	Procedure Step Number	9.40	9.40	9.46	
Date	Date	3/2/98	3/2/98	3/2/98	
Time	Time, hr:min	10:45	10:55	11:05	
Test Instrumentati	ón tradición de la constatión		1, 1, 2,		
FI-temp	System Flow, gpm	104	102	102	
PI-temp-1	Supply Pressure, psig	56	56	56	
PI-temp-2	Press. upstream V-temp-2, psig	120	125	115	
PI-temp-3	Return Pressure, psig	0	0	0	
Pump Statistics (d	perating booster pump, from PCU-2 s	screen on MCS)			
TI-3129A1\ B1	Thrust End Bearing Temp, °F	63	64	64	
,125A2. B2	Drive End Bearing Temp. °F	60	67	64	
ST-3125A, B	Motor Speed, rpm	2150	2150	2/05	
VI-3125A1. B1	Thrust End Vibration, mils	0.02	0.02	0,07	
VI-3125A2 B2	Drive End Vibration, mils	0.02	0.02	0.01	
FIC-3125 PV	Fluid Flow Present Value, gpm	110	[10	1/0	
FIC-3125 SP	Fluid Flow Set Point, gpm	110	110	110	
TI-3125A	Fluid Temp, °F	48	48	49	
PI-3125A. B	Fluid Inlet Pressure, psig	59	59	59	
P1-3125C D	Fluid Outlet Pressure, psig	373	378	364	
Header Data (from	PCU-2 and PCU-3 screens on MCS)				
PI-3126B	SLL-3160 Press. Vent Sta. psig	2/2	2/4	208	
TI-3126B	SLL-3160 Temp. Vent Sta. °F	47	48	51	
TI-3126A	SNL-3150 Temp. Vent Sta. °F	ςς	55	SS	
TI-3125B	SNL-3150 Temp. Div Box. °F	48	48	48	

(Make copies of this sheet as required)

Data Recorder: Doug Gence

REVISION NO. <u>0</u>

ATTACHMENT A

	Appendix	G - System	Data Sheet			
Item	Description			8		,
Pump ID	P-3125A) or B	PZISA		7		
Proc. Step No.	Procedure Step Number	9,46	9,46	9.46		
Date	Date	3/2/98	3/2/98	3/2/98		
Time	Time, hr:min	11:45	11:55	12:05		
Test Instrumentat	ion Black Strain	······				· · · · · · · · · · · · · · · · · · ·
FI-temp	System Flow. gpm	130	130	131		
PI-temp-1	Supply Pressure, psig	46	46	46		
PI-temp-2	Press. upstream V-temp-2. psig	15	25	18		
PI-temp-3	Return Pressure, psig	<b>Ø</b> 2	2	1		
Pump Statistics (	operating booster pump, from PCU-2 s	creen on MCS).		film filma.		
TI-3125A1. B1	Thrust End Bearing Temp, °F	68	68	68		
,125A2, B2	Drive End Bearing Temp, °F	68	69'	70		
51-3125A. B	Motor Speed. rpm	2430	2424	2429	·	
VI-3125A1. B1	Thrust End Vibration, mils	0,03	0.03	0.63		
VI-3125A2. B2	Drive End Vibration, mils	0.02	0.02	0.02		
FIC-3125 PV	Fluid Flow Present Value, gpm	140	140	140		
FIC-3125 SP	Fluid Flow Set Point, gpm	140	140	140		
TI-3125A	Fluid Temp, °F	50	50	50		
PI-3125A. 8	Fluid Inlet Pressure, psig	47	4)	4)		
PI-3125C. D	Fluid Outlet Pressure. psig	4/6	4/3	4/4	·	
Header Data (from	PCU-2 and PCU-3 screens on MCS)		. :	<u>,</u>		·
PI-3126B	SLL-3160 Press. Vent Sta. psig	182	[83	182		
TI-3126B	SLL-3160 Temp, Vent Sta, °F	49	49	50		· 
TI-3126A	SNL-3150 Temp, Vent Sta, °F	55	55	SS		
TI-3125B	SNL-3150 Temp, Div Box, °F	50	48	49		

(Make copies of this sheet as required)

Data Recorder: \_

DOUG GERKEY PRINT NAME O.J INITIALS 3/2/98 DATE

REVISION NO. 0

ATTACHMENT A

	Appendix	G - System	Data Sheet	-		
Item	Description					
Pump ID	(P-3125A) or B	P-3/15A-		<del></del>		
Proc. Step No.	Procedure Step Number	9.51	9,51	9.51		
Date	Date	3/2/98	3/2/98	3/2/98		
Time	Time, br:min	12:25	121.35	12:45		
Test İnstrumentati	on the second				A January 1	
FI-temp	System Flow, gpm	132	131	13/		
PI-temp-1	Supply Pressure, psig	48	48	48		
PI-temp-2	Press. upstream V-temp-2, psig	68	68	68		
PI-temp-3	Return Pressure, psig	1	1	1		
Pump Statistics (o	perating booster pump, from PCU-2 s	screen on MCS)				
TI-3125A1. B1	Thrust End Bearing Temp. °F	69	69	20		
.125A2. B2	Drive End Bearing Temp, °F	7/	21	72		
51-3125A, B	Motor Speed, rpm	2528	2530	2523		
VI-3125A1. B1	Thrust End Vibration, mils	0.64	0.04	0.09		
VI-3125A2. B2	Drive End Vibration, mils	0.03	0,03	0.03		
FIC-3125 PV	Fluid Flow Present Value, gpm	140	140	140		
FIC-3125 SP	Fluid Flow Set Point. gpm	140	140	140		
TI-3125A	Fluid Temp, °F	51	51	5/		
PI-3125A. B	Fluid Inlet Pressure, psig	47	4)	4)		
PI-3125C, D	Fluid Outlet Pressure. psig	459	463	460		
Header Data (from E	PCU-2 and PCU-3 screens on MCS)					
PI-3126B	SLL-3160 Press. Vent Sta. psig	227	227	(55		
TI-3126B	SLL-3160 Temp. Vent Sta. °F	_56	50	50		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	55	55	ۍ ک	-	
TI-31258	SNL-3150 Temp. Div Box. °F	49	49	5/		

(Make copies of this sheet as required)

Data Recorder:

DOUG GENCER

DY

3/2/18/ DATE

REVISION NO. <u>0</u>

ATTACHMENT A

	Appendix	G - System	Data Sheet		· · · · · · · · · · · · · · · · · · ·	
Item	Description					
Pump ID	P-3125A or B	P-3125A_		<del>)</del>		
Proc. Step No.	Procedure Step Number	9.56	9,56	9.56		
Date	Date	3/2/98	3/2/98			
Time	Time, hr:min	13:00	13:10	13:20		
Test İnstrumentati	on the second					
FI-temp	System Flow, gpm	116	117	118		
PI-temp-1	Supply Pressure, psig	48	48	46		· · · · · · · · · · · · · · · · · · ·
PI-temp-2	Press. upstream V-temp-2, psig	162	163	164		
PI-temp-3	Return Pressure. psig	1		2		<u> </u>
Pump Statistics (o	perating booster pump, from PCU-2 s	creen on MCS)				
TI-3125A1. B1	Thrust End Bearing Temp. °F	21	72	72		
,125A2. B2	Drive End Bearing Temp. °F	73	73	74	·	
51-3125A, B	Motor Speed, rpm	2719	2736	2721		
VI-3125A1, B1	Thrust End Vibration, mils	0.05	0.05	0.05		
VI-3125A2. 82	Drive End Vibration. mils	0.04	0.04	0,04		
FIC-3125 PV	Fluid Flow Present Value. gpm	140	140	140		
FIC-3125 SP	Fluid Flow Set Point, gpm	140	140	140		
TI-3125A	Fluid Temp. °F	52	52	52		
PI-3125A. B	Fluid Inlet Pressure. psig	42	4)	47		
PI-3125C, D	Fluid Outlet Pressure, psig	554	5 <i>55</i>	·555		
Header Data (from	PCU-2 and PCU-3 screens on MCS)					<u> </u>
PI-3126B	SLL-3160 Press. Vent Sta. psig	321	324	325		
TI-3126B	SLL-3160 Temp. Vent Sta. °F	50	50`	51		
TI-3126A	SNL-3150 Temp, Vent Sta. °F	55	5.5	<b>\$</b> \$		
T-I-31258	SNL-3150 Temp. Div Box. °F	51	51	51		

(Make copies of this sheet as required)

Data Recorder: DOUG GERKEY DD 3/2/98
PRINT NAME INITIALS DATE

REVISION NO. 0

ATTACHMENT A

	Appendix	G - System	Data Sheet			
Item	Description				, , , , , , , , , , , , , , , , , , ,	,
Pump ID	P-3125A) or B	P-3125#.		<b>&gt;</b>		
Proc. Step No.	Procedure Step Number	9,62	9.62	9.62		,
Date	Date	3/2/98	3/2/98	3/2/98		
Time	Time, hr:min	13:30	13:40	13:50		
Test İnstrumentati		94 - E. A. P				· .
FI-temp	System Flow, gpm	145	144	145		
PI-temp-1	Supply Pressure, psig	44	' '	44		
PI-temp-2	Press. upstream V-temp-2. psig	30	<i>44</i> 30	25		
PI-temp-3	Return Pressure, psig	5	5	3		
Pump Statistics (d	perating booster pump, from PCU-2:	screen on MCS)				
TI-3125A1 B1	Thrust End Bearing Temp. °F	72	72	72		
.125A2 B2	Orive End Bearing Temp, °F	74	24	75		
SI-3125A, B	Motor Speed, rpm	2708	2680	2693		
VI-3125A1 B1	Thrust End Vibration, mils	0.07	0.09	0.09		
VI-3129AZ. B2	Drive End Vibration, mils	0.05	0.06	0.05		
FIC-3125 PV	Fluid Flow Present Value, gpm	155	155	155		
FIC-3125 SP	Fluid Flow Set Point, gpm	155	155	155		
TI-3125A	Fluid Temp, °F	52	53	<i>5</i> 3		
PI-3125A. B	Fluid Inlet Pressure, psig	42	42	42		
PI-3125C/D	Fluid Outlet Pressure, psig	499	489	489		
Header Data (from	PCU-2 and PCU-3 screens on MCS)					· -
PI-3126B	SLL-3160 Press. Vent Sta. psig	227	224	223		
TI-3126B	SLL-3160 Temp, Vent Sta, °F	51	52	52		
TI-3126A	SNL-3150 Temp, Vent Sta. °F	55	55	SS		
TI-31258	SNL-3150 Temp, Div Box. °F	5/	51	5/		

(Make copies of this sheet as required)

Data Recorder: DOUG GERICEN

REVISION NO. 0

ATTACHMENT A

	Appendix	G - System	Data Sheet		_	
Item	Description					:
Pump ID	(P-3125A) or 8	P-3125A-		<del>)</del>		
Proc. Step No.	Procedure Step Number	9.67	9.67	9.67		٠.
Date	Date	3/2/98	3/2/98	3/2/98		
Time	Time, hr;min	14:40	14:50	15:00	·	
Test Instrumentati	on Park Case Case					
FI-temp	System Flow, gpm	148	144	146		
PI-temp-1	Supply Pressure, psig	60	42	42		
PI-temp-2	Press. upstream V-temp-2. psig	42	60	60		
PI-temp-3	Return Pressure, psig	7	3	3		
Pump Statistics (o	perating booster pump. from PCU-2 s	creen on MCS)				
TI-3125A1 B1	Thrust End Bearing Temp, °F	23	73	23		
.12\$A2\ B2	Orive End Bearing Temp. °F	76	)(	76		
51-3125A. B	Motor Speed. rpm	2736	2747	2743		
VI-3125A1 B1	Thrust End Vibration. mils	0.06	0.07	0,08		
VI-312502, B2	Drive End Vibration, mils	0.04	0.05	0.05		
FIC-3125 PV	Fluid Flow Present Value, gpm	155	155	155		
FIC-3125 SP	Fluid Flow Set Point, gpm	155	155	155		
TI-3125A	Fluid Temp, °F	54	54	54		
PI-3125/.) B	Fluid Inlet Pressure, psig	42	42	42		
PI-3125C D	Fluid Outlet Pressure, psig	519	520	524		
Header Data (from	PCU-2 and PCU-3 screens on MCS)	,				1.5
PI-31268	SLL-3160 Press. Vent Sta. psig	255	254	254		
TI-31268	SLL-3160 Temp. Vent Sta. °F	53	53	53		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	55	55	55		
T.I - 3125B	SNL-3150 Temp. Div Box. °F	53	53	53		

(Make copies of this sheet as required)

Data Recorder:

DODY GENCE!

D.J. INITIALS 3/2/98 DATE

REVISION NO. 0

ATTACHMENT A

	Appendix	G - System	Data Sheet	<u> </u>	 
Item	Description				
Pump ID	P-3125A or B	P-3125A		<del></del>	
Proc. Step No.	Procedure Step Number	9,23	9:23	9.33	
Date	Date	3/2/98	3/2/98	3/2/98	
Time	Time, hrimin	14:05	14:15	14:25	
Test Instrumentati	ónia Migrafia				
FI-temp	System Flow, gpm	143	143	145	
PI-temp-1	Supply Pressure, psig	44	43	44	
PI-temp-2	Press. upstream V-temp-2. psig	1/0	110	110	
PI-temp-3	Return Pressure, psig	3	3	3	
Pump Statistics (o	perating booster pump, from PCU-2 s	creen on MCS)			
TI-3125A1 81	Thrust End Bearing Temp. °F	73	74	74	
,125A2, B2	Orive End Bearing Temp. °F	75	75	76	
S1-3125A, B	Motor Speed, rpm	2840	2831	28.56	
VI-3125A1 B1	Thrust End Vibration. mils	0.16	0.16	0.21	
VI-3125AZ. B2	Drive End Vibration, mils	0.09	610	0./3	
FIC-3125 PV	Fluid Flow Present Value, gpm	155	155	/55	,
FIC-3125 SP	Fluid Flow Set Point, gpm	155	155	155	
TI-3125A	Fluid Temp. °F	<i>5</i> 3	53	53	
PI-3125A B	Fluid Inlet Pressure. psig	42	42	42	
PI-3125C D	Fluid Outlet Pressure, psig	57/	576	524	 
Header Data (from	PCU-2 and PCU-3 screens on MCS)		4 4		 <u>-</u>
PI-3126B	SLL-3160 Press. Vent Sta. psig	307	305	305	
TI-3126B	SLL-3160 Temp, Vent Sta. °F	52'	SZ	53	
TI-3126A	SNL-3150 Temp. Vent Sta. °F	55	55	55	 
TI-31258	SNL-3150 Temp. Div Box. °F	52	52	<i>5</i> 3	

(Make copies of this sheet as required)

Data Recorder:

DOOG GERKER

DY.
INITIALS

3/2/98 DATE

REVISION NO. 0

ATTACHMENT A

Brump AUTO AT 110 GPM THE POINT 1

	Appendix	G - System	Data Sheet		
Item	Description				
Pump ID	P-3125A or B	P-3125B	P-3125B	P-3125B	
Proc. Step No.	Procedure Step Number	10.30	10,30	10.30	
Date	Date	3/24/98	3/24/98	3/29/98	
Time	Time, hr:min	10:10	10:20	10:30	
Test Instrumentati	ón Chipaga				
FI-temp	System Flow, gpm	107	108	/07	
PI-temp-1	Supply Pressure. psig	54	ς 6	56	
PI-temp-2	Press. upstream V-temp-2, psig	15	15	15	
PI-temp-3	Return Pressure, psig	0	0	0	
Pump Statistics (c	perating booster pump, from PCU-2 s	screen on MCS)			
TI-3125A1. 81	Thrust End Bearing Temp. °F	6.2	64	65	
.125A2 B2	Drive End Bearing Temp, °F	62	64	65	
ST-3125A. B	Motor Speed. rpm	1994	1995	2005	
VI-3125A1 81	Thrust End Vibration, mils	0.01	0.01	0.01	
VI-3125A2 82	Drive End Vibration, mils	0.01	0.01	0.01	
FIC-3125 PV	Fluid Flow Present Value, gpm	110	110	110	
FIC-3125 SP	Fluid Flow Set Point, gpm	110	110	1/0	
TI-3125A	Fluid Temp. °F	54	54	54	
PI-3125A. B	Fluid Inlet Pressure, psig	57	57	57	
P1-3125C. D	Fluid Outlet Pressure, psig	292	291	295	
Header Data (from	PCU-2 and PCU-3 screens on MCS)		1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1		· ·
PI-3126B	SLL-3160 Press. Vent Sta. psig	118	119	121	
TI-3126B	SLL-3160 Temp. Vent Sta. °F	50	49	51	
TI-3126A	SNL-3150 Temp. Vent Sta. °F	56	56	56	
TI-31258	SNL-3150 Temp. Div Box. °F	51	49	50	

(Make copies of this sheet as required)

Data Recorder: <u>Dou</u>

DOUG GERKED

B. 9.

3/24/98 DATE

REVISION NO. 0

ATTACHMENT A

AUTO AT 1006PM THROTTLED FOR POINT Z

	Appendix	G - System	Data Sheet		<del></del>	
Item	Description					
Pump ID	P-3125A or B	P-3125B	P-3125B	P-3125B		
Proc. Step No.	Procedure Step Number	/0:35	10.35	10,35		
Date	Date	3/24/98	3/24/98	3/24/98		
Time .	Time, hr:min	10:40	10.50	11:00		
Test Instrumentati	on.					
FI-temp	System Flow, gpm	109	108	109		
PI-temp-1	Supply Pressure, psig	56	56	56		
PI-temp-2	Press. upstream V-temp-2. psig	55	55	55		
PI-temp-3	Return Pressure, psig	, Q.	0	0		
Pump Statistics (c	perating booster pump, from PCU-2 s	screen on MCS)				
TI-3125A1, B1	Thrust End Bearing Temp. °F	67	68	68		
125A2. B2	Drive End Bearing Temp, °F	69	71	73		
SI-3125A, B	Motor Speed, rpm	2105	2100	2/00		
VI-3125A1. B1	Thrust End Vibration, mils	0.01	0.01	0,01		
VI-3125A2, 82	Drive End Vibration, mils	0.01	0.01	0.01		
FIC-3125 PV	Fluid Flow Present Value, gpm	110	110	110		
FIC-3125 SP	Fluid Flow Set Point, gpm	110	110	110		
TI-3125A	Fluid Temp. °F	53	53	53		
PI-3125A. B	Fluid Inlet Pressure, psig	57	57	57		
PI-3125C. b	Fluid Outlet Pressure, psig	332	329	331		
Header Data (from	PCU-2 and PCU-3 screens on MCS)					
PI-3126B	SLL-3160 Press, Vent Sta. psig	159	155	156		
TI-3126B	SLL-3160 Temp, Vent Sta. °F	53459	53	53		
TI-3126A	SNL-3150 Temp, Vent Sta, °F	56466	56	56		
TI-31258	SNL-3150 Temp, Div Box, °F	50	50	50		

(Make copies of this sheet as required)

Data Recorder: Doug Genker PRINT NAME

B-PUMP DUTO- AT +456 PM THROTTLED FOR POINT 3

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 132 OF 132

REVISION NO. <u>0</u>

ATTACHMENT A

	Appendix	G - System	Data Sheet			
Item	Description					
Pump ID	P-3125A or B	P-3125B	P-3/25B	P-3125B		
Proc. Step No.	Procedure Step Number	10.40	10.40	10.46		
Date	Date	3/24/98	3/24/98	3/24/98		
Time	Time, hr:min	11:05	11:15	11:25		
Test Instrumentat	ion:					
FI-temp	System Flow, gpm	105	1035	105		
PI-temp-1	Supply Pressure. psig	56	56	56		·
PI-temp-2	Press. upstream V-temp-2, psig	130	130	130		
PI-temp-3	Return Pressure, psig	.0	0	0		
Pump Statistics (	operating booster pump, from PCU-2:s	screen on MCS)				
II-3125A1, B1	Thrust End Bearing Temp, °F	69	70	70		
3125A2 B2	Drive End Bearing Temp, °F	74	75	22		
SI-3125A. B	Motor Speed. rpm	2300	2300	2300		
VI-3125A1, B1	Thrust End Vibration, mils	0.02	0.02	0.02		
VI-3125A2 B2	Drive End Vibration, mils	0.01	0.01	0.01	<u> </u>	
FIC-3125 PV	Fluid Flow Present Value, gpm	110	110.	110		·
FIC-3125 SP	Fluid Flow Set Point, gpm	110	1/0	1/0		
TI-3125A	Fluid Temp, °F	53	53	53		
PI-3125A./8	Fluid Inlet Pressure. psig	37	56	57		
PI-3125C. D	Fluid Outlet Pressure. psig	410	410	411		
Header Data (from	PCU-2 and PCU-3 screens on MCS)					
PI-3126B	SLL-3160 Press, Vent Sta. psig	235	235	235		
TI-3126B	SLL-3160 Temp, Vent Sta, °F	53	53	<i>_</i> \$3		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	56	56	56		
TI-3125B	SNL-3150 Temp, Div Box, °F	50	51	51		

(Make copies of this sheet as required)

Data Recorder: Doug Genker PRINT NAME

REVISION NO. 0

ATTACHMENT A

B-Pump guto AT 1404Pm POINT

	Appendix	G - System	Data Sheet		
Item	Description				
Pump ID	P-3125A or B	P-3125B	P-3125 B	P-3125B	
Proc. Step No.	Procedure Step Number	10.96	10.46	10.46	
Date	Date	3/24/98	3/29/98	3/24/98	
Time	Time. hr:min	11:35	11:45	11:55	
Test Instrumentat	ion	ii neddd odii Medd Nan o			
FI-temp	System Flow, gpm	140	140	140	
PI-temp-1	Supply Pressure, psig	44	44	44	
PI-temp-2	Press. upstream V-temp-2, psig	20	20	-20	
PI-temp-3	Return Pressure, psig	0	0	0	
Pump Statistics (	operating booster pump, from PCU-2:	screen on MCS)			
TI-3125A1. B1	Thrust End Bearing Temp. °F	72	23	23	
.3125A2 B2	Drive End Bearing Temp, °F	79	81	82	
125A. B	Motor Speed. rpm	26/6	2616	2610.	
VI-3125A1 B1	Thrust End Vibration, mils	0.08	0,05	0.05	
VI-3125A2. B2	Orive End Vibration, mils	0.06	0.09	0.04	
FIC-3125 PV	Fluid Flow Present Value, gpm	140	140	140	
FIC-3125 SP	Fluid Flow Set Point, gpm	140	140	140	
T1-3125A	Fluid Temp, °F	53	59	54	
PI-3125A. B	Fluid Inlet Pressure, psig	46	46	46	
PI-3125C. D	Fluid Outlet Pressure, psig	455	45 6	449	
Header Data (from	PCU-2 and PCU-3 screens on MCS)				,
PI-31268	SLL-3160 Press, Vent Sta. psig	204	207	202	
TI-3126B	SLL-3160 Temp. Vent Sta. °F	53	53	53	
TI-3126A	SNL-3150 Temp. Vent Sta. °F	56	56	56	
TI-3125B	SNL-3150 Temp, Div Box. °F	53	54	54	

(Make copies of this sheet as required)

Data Recorder: Dovi 4E NL

D.C. 3/29/S
INITIALS DATE

REVISION NO. 0

ATTACHMENT A

B-PUMP AUTO POINT 2 @ 1406PM

	Appendix	G · System	Data Sheet			
Item	Description	984(10)0			40年度12年4年	
Pump 10	P-3125A or B	P-3/15B	P-3125B	P-3125B		
Proc. Step No.	Procedure Step Number	10.51	10.51	10.51		
Date	Date	3/29/95	3/2 9/98	3/24/98		
Time ,	Time, hr:min	12:05Pm	_	12:25		
Test Instrumentati	on			Simbolitudes suddi i i i i i i		
FI-temp	System Flow, gpm	138	13.8	138		
PI-temp-1	Supply Pressure, psig	49	44	44		
PI-temp-2	Press. upstream V-temp-2, psig	/35	135	19 85 19 85		
PI-temp-3	Return Pressure, psig		1	0		
Pump Statistics (o	perating booster pump. from PCU-2 s	screen on MCS)				1.12 d. 14 J. L. L.
T1-3125A1./B)\	Thrust End Bearing Temp, °F	74	74	75		
-3125A2. B2	Drive End Bearing Temp. °F	83	84	85		
3125A. B	Motor Speed, rpm	2710	27/0	2716		
VI-3125A1. B1	Thrust End Vibration. mils	0.05	0.05	0.05		
VI-3125A2, B2	Drive End Vibration, mils	0.03	0.03	0.03		
F1C-3125 PV	Fluid Flow Present Value, gpm	140	140	140		
FIC-3125 SP	Fluid Flow Set Point, gpm	140	140.	140		
T1-3125A	Fluid Temp, °F	3.5	55	<i>\$5</i>		
PI-3125A. B	Fluid Inlet Pressure, psig	46	46	46		
PI-3125C. D	Fluid Outlet Pressure, psig	507	567	507		
Header Data (from	PCU-2 and PCU-3 screens on MCS)					
PI-3126B	SLL-3160 Press. Vent Sta. psig	262	262	262		
TI-31268	SLL-3160 Temp. Vent Sta. °F	53	<i>5</i> 3	54	·	
TI-3126A	SNL-3150 Temp. Vent Sta. °F	56	56	56		
T1-3125B	SNL-3150 Temp. Div Box. °F	53	<b>68</b> 53	<i>5</i> 3		

(Make copies of this sheet as required)

3/29/98

Data Recorder: DOUG GEAKEN

1).6. 3/24/90
INITIALS DATE

REVISION NO. 0

ATTACHMENT A

PAGE 132 OF 132

B-pump	Buto	1406.0m	P.01~ 7	2
	17010	_ / / V W / · · · · · ·	/ 1/1/2 /	3

	Appendix	G - System	Data Sheet			
Item	Description	4000000				1. 1. 1. 1
Pump ID	P-3125A or B	P-3125B	P-3125B	P-3128B		
Proc. Step No.	Procedure Step Number	10.56	10.56	10.56		
Date	Date	3/29/98	3/24/98	3/24/98		
Time	Time. hr:min	12:45	12:55	13:05		
Test Instrumentat	ion					
FI-temp	System Flow, gpm	127	125	127		
PI-temp-1	Supply Pressure, psig	44	44	44		
PI-temp-2	Press. upstream V-temp-2, psig	195	195	195		
PI-temp-3	Return Pressure, psig	.0	1	1.		:
Pump Statistics (	operating booster pump, from PCU-2 s	screen on MCS)			Talayaya Miller (1900) Talaya Talaya (1900)	·
TI-3125A1./81	Thrust End Bearing Temp, °F	725	77	77		
·3125A2 / B2	Drive End Bearing Temp. °F	87	87	88		
5125A. B	Motor Speed, rpm	29/0	2910	2910		
VI-3125A1 B1	Thrust End Vibration, mils	0.13	0,16	0.12		
VI-3125A2.B2	Drive End Vibration, mils	0,11	0.10	0.11	,	
FIC-3125 PV	Fluid Flow Present Value, gpm	140	140	190		
FIC-3125 SP	Fluid Flow Set Point, gpm	140	140	140		
T1-3125A	Fluid Temp, °F	5.L	56	26		
PI-3125A. B	Fluid Inlet Pressure, psig	46	46	46		
PI-3125C. D	Fluid Outlet Pressure, psig	614	612	610		
Header Data (from	PCU-2 and PCU-3 screens on MCS)			3 1 N 3 1 N	: 	
PI-31268	SLL-3160 Press, Vent Sta. psig	367	366	366		
TI-31268	SLL-3160 Temp. Vent Sta. °F	55	55	SS.		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	56	56	56		
TI-3125B	SNL-3150 Temp, Div Box, °F	54	59	54		

(Make copies of this sheet as required)

Data Recorder:

HNF-2504, REV. 0 ATTACHMENT | PAGE205

155 GPM

REVISION NO. 0

ATTACHMENT A

AUTO

B- pomp

· · · · · · · · · · · · · · · · · · ·	Appendix	G - System	Data Sheet			
Item	Description					er i ga e te i e est
Pump ID	P-3125A or B	P-3125A	P-3125B	P-3/25B		
Proc. Step No.	Procedure Step Number	10.62	10.62	10,62		
Date	Date	3/29/98	3/24/98	3/24/98		
Time	Time. hr:min	13:10	13:20	13:30		
Test Instrumentat	ion					
FI-temp	System Flow. gpm	153	153	152		
PI-temp-1	Supply Pressure, psig	40	42	42	·	
PI-temp-2	Press. upstream V-temp-2, psig	25	25	25		
PI-temp-3	Return Pressure, psig	3	. 3	3		
Pump Statistics (	operating booster pump, from PCU-2 s	creen on MCS)				
TI-3125A1./B1	Thrust End Bearing Temp, °F	72	77	72		
·3125A2 B2	Drive End Bearing Temp. °F	88	88	89		
3125A.B	Motor Speed, rpm	2850	28 <b>5</b> 0	2840		
VI-3125A1 81	Thrust End Vibration. mils	0.09	0,08	0,08		
VI-3125A2. B2	Drive End Vibration. mils	0.05	0.05	0.05		
FIC-3125 PV	Fluid Flow Present Value, gpm	155	155	155		
FIC-3125 SP	Fluid Flow Set Point, gpm	155	155	155		
T1-3125A	Fluid Temp. °F	56	56	57		
PI-3125A. B	Fluid Inlet Pressure. psig	46	40	4/		,
PI-3125C. D	Fluid Outlet Pressure. psig	526	525	522		
Header Data (from	PCU-2 and PCU-3 screens on MCS)				·	, <u></u>
PI-31268	SLL-3160 Press. Vent Sta. psig	242	242	242		ļ
TI-31268	SLL-3160 Temp. Vent Sta. °F	56	. 56	56		
TI-3126A	SNL-3150 Temp. Vent Sta. °F	56	56	56		
TI-31258	SNL-3150 Temp. Div Box. °F	55	5.5	55		

(Make copies of this sheet as required)

Data Recorder: Doul Lenger D.G. 3/2/8
PRINT NAME INITIALS DATE

HNF-2504, REV. 0 ATTACHMENT I PAGE 204

REVISION NO. \_0\_

ATTACHMENT A

155 GPM POINT 2

	Appendix	G - System	Data Sheet			
Item	Description		240 (may 200)			31 - X - 13 3 - 245
Pump ID	P-3125A or B	P-3/25B	P-3125B	P-3/25B		- 0.
Proc. Step No.	Procedure Step Number	10.63	10.103	10.63	10.67	3/20/00
)ate	Date	3/24/98	3/24/98	3/24/98		101110
ime	Time, hr:min	13:40	13:50	14:00		
Test Instrumental	ion					
1-temp	System Flow. gpm	151	152	152		
Pi-temp-1	Supply Pressure, psig	42	40	40		
Pl-temp-2	Press. upstream V-temp-2, psig	75	75	75		
PI-temp-3	Return Pressure, psig	3	3	3		
Pump Statistics (	operating booster pump. from PCU-2 s	screen on MCS)			Ange Nage in	
TI-3125A1./BI	Thrust End Bearing Temp, °F	78	78	78	X	
-3125A2 B2	Drive End Bearing Temp. °F	89	90	90		
3125A. B	Motor Speed, rpm	2930	2950	2930	,	
/I-3125A1, B1	Thrust End Vibration, mils	0.16	0.10	0,15		
VI-3125A2. B2	Drive End Vibration, mils	0.10	6.07	0,10		
FIC-3125 PV	Fluid Flow Present Value. gpm	155	155	155		
IC-3125 SP	Fluid Flow Set Point, gpm	155	155	155		
Γ1-3125Λ	Fluid Temp, °F	57	57	58		
PI-3125A./B	Fluid Inlet Pressure, psig	40	40	40		
PI-3125C.D	Fluid Outlet Pressure, psig	565	- 5 23	568		
Header Data (from	PCU-2 and PCU-3 screens on MCS)				:	
PI-31268	SLL-3160 Press, Vent Sta. psig	292	285	285		
TI-31268	SLL-3160 Temp. Vent Sta. °F	56	56	56		
[I-3126Λ	SWL-3150 Temp, Vent Sta, °F	56	56	56		
TI-3125B	SNL-3150 Temp. Div Box. °F	56	56	56		

(Make copies of this sheet as required)

Data Recorder: <u>Dov4 GERICEN</u> <u>D.G.</u> 3/2 4/1

REVISION NO. \_0

ATTACHMENT A

B-Pump AUTO 155 GPM POINT 3

	Appendix	G - System	Data Sheet			
Item	Description	\$2.000 Sept. (1980)			en trighten at	1. 1. 1. 1. 1. 1. 1. 1. 1. 1. 1. 1. 1. 1
Pump ID	P-3125A or B	P-3123B	P-312512	P-3125B		
Proc. Step No.	Procedure Step Number	10.73	10.73	10.73		
Date	Date	3/24/98	3/29/98	3/24/48		
Time	Time, hr:min	19:10	14:20	14:30	,	
Test Instrumentat	ion					
FI-temp	System Flow, gpm	145	145	145		
PI-temp-1	Supply Pressure, psig	40	42	42		
PI-temp-2	Press. upstream V-temp-2. psig	195	195	195		
PI-temp-3	Return Pressure. psig	3	3	3		
Pump Statistics (	operating booster pump, from PCU-2 s	screen on MCS)			A Comprehension	
TI-3125A1.	Thrust End Bearing Temp, °F	79	80	80		
3125A2./B2	Drive End Bearing Temp. °F	90	90	91		
8125A. B	Motor Speed. rpm	3/50	3150	3/40		
VI-3125A1 B1	Thrust End Vibration. mils	0.11	0.12	0.13		
VI-3125A2. B2	Drive End Vibration. mils	0.09	0.09	0.10		
FIC-3125 PV	Fluid Flow Present Value, gpm	155	155	155		
FIC-3125 SP	Fluid Flow Set Point, gpm	155	155	155		
TI-3125A	Fluid Temp, °F	59	59	59		
PI-3125A. (B)	Fluid Inlet Pressure, psig	40	39	40	,	
PI-3125C. D	Fluid Outlet Pressure, psig	692	692	682		
Header Data (from	PCU-2 and PCU-3 screens on MCS)				:	
PI-3126B	SLL-3160 Press. Vent Sta. psig	406	404	402		
TI-31268	SLL-3160 Temp, Vent Sta. °F	57	57	58		
TI-3126A	SML-3150 Temp. Vent Sta. °F	56	56	56		
TI-3125B	SNL-3150 Temp. Div Box. °F	57	57	57		

(Make copies of this sheet as required)

Data Recorder: DOUL CENICEN D.G. 3/24/9

#### SIGNATURE/INITIAL VERIFICATION

All persons involved in procedure performance, data recording, and verification or evaluation of test steps shall provide their name, job title, signature, and initials in the following table.

NAME (PRINT)	TITLE	SIGNATURE	INITIAL
St Leshikar	Test Engineer	Ma Lishikar	Las
M.D. GERKEN	TEST ENGINEER	Day Lyhn	<i>9.01</i>
Phylo YosthusTA	RIFETRZEZIAN	Into the fortune	FLP
R.L. THOMPSON	Neo	Gl. L. Shorps	As.
GCOOper	Labor	A Cooper	M16.
Fidel Rivera	Electrician	Fall Milesa	R
20NNIEJ STEADWAN	FITTER	Jonnie & trech	211
William A Johnson	<u>Electrician</u>	Ollon Allman	WAJ
Smith SL	Litter	Joseph Joseph	20
Renz Enloz	BITTER	Den Enles	SE
Carl van Katnijk	Project Engr	he in thing	le
11 2 PARSONS	PROS. MOR	MI Parsons	MR
J.M. Newle	Supen	Jahr M. Veulle	FDWW
RONALD A. APNOT	i	Frank G Clando	DON RAINING
DAVID A. GIZEENAWAY	TEST DIR.	190	All
LOURY B. ATKING	FONW CE	your to the	HA
PJ ELLENDORF	LMHC QC	P) Elmendon	NE
J.E.DUNKS	TEST ENGINEER	Manh	920
K. WILLOUGHBY	LMHC QC "	Kost illing.	KW
L.R. HALL	PROJECTS QE	Lan R. Hall	埋
( R GCHMUTH	Tout Die	Tr. Mille.	· OL

CRECHMUTH E.PACQUET

Test Dik. Test Manager attent when the second

£.P.

REVISION NO. 0

ATTACHMENT C

	TEST LOG	TEST NUMBER: HNF-1857	TEST LOG PAGE NUMBER:
TEST TITLE: Preoper	rational Test POTP-007, Cross Site Transfer	System Integr	ated Test
TIME/DATE	EVENT DESCRIPTION/S	SIGNATURE	
9'00	(both pumps) using decade box	on Al, AZ, B	1; and B2.
1000	Performed motor winding temp test a waiting on street elbows to replumb be	1 1	
	•		

REVISION NO. 0

FEST LOG PAGE NUMBER: TEST NUMBER: TEST LOG HNF-1857 1\_ of <u>/8</u>\_ TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test TIME/DATE EVENT DESCRIPTION/SIGNATURE POTP-007 "Kickoff" Prejob Meeting 12/12 7:00 Am IA-V-1115A +hrs 111BA incorrect valve 4's in procedure procedure (Appendix c) with correct valve #'s, IA-V-3115A thru 3118A Breaken #'s listed in Appendix D incorrect per field verification. redlined procedure with correct breaker #'s per ECN-058-098 Redline Step 1.12.1, valve # corrected to 1A-V-3105B Ball valves on SOV's for flushing /cleanout (1 pcp SOV) 10:00 Am FE-3125, Utrasonic flowmeter, calibration certificate from vendor 10:30am does not list cal, due date. Will check with vendor - Never needs recal P-162-SY-OZA 012 - Panel label where lock ! tag blace Leads A.B. C Removed VSD-1 and VSD-2 LED screens show "MASTER INHIBIT" and FAULT indicator RESET button USD keypad does not take USD out of fault. Shutting off power to each VSD and then reclosing disconnect resulted in

DRIVE READY indication, correcting problem and allowing Section Steps 2.1-2,10

and 3,1-3.10 to commence.

# PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 1 OF 1 REVISION NO. 0 ATTACHMENT C

	TEST LOG	TEST NUMBER: HNF-1857	TEST LOG PAGE NUMBER: 2 Of 18			
TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test						
TIME/DATE EVENT DESCRIPTION/SIGNATURE						
12/13 7:00	Pre-job meeting					
8:10	Booster pump low oil level switch, LSL-3125BZ, sightglass is empty					
	Alarm table on MCS shows LAL-3125AZ	• •				
8'15	Jumpered low oil level switches LSL-3125	AZ and LSL-3	125BZ closed			
	so that booster pumps can be started.	for testing of	other pump			
	interlocks					
8:30	APPEARS LSL-3125Bl and LSL-3125BZ AR	ce wired backu	mrds (vice-versa)			
9:30	Per-field troubleshooting, LSL-3125B1 wires u					
	wires at 24V junction box at booster pump.					
	W-058 drawings don't show each wire termination					
	Fixed problem by swapping wires to correct configuration. Alarms were					
8111	cleared from MCS alarm table					
7.45	PLC logic being modified for LDA-3150 and LDA-3151 sumpleak detection					
iD:30	Steps 1.32,5 and 1.32,7,  Step Z.Z3, Diversion BOX ICON IN transfer path (Scheme ZA)					
10	PCU-Z is RED and Z44A Lift Station	,	~ 1			
	Does not affect performance of Interlock to					
	Indicated in GREEN on MCS overview scre	en, per tester	ng thee r			

REVISION NO. 0

ATTACHMENT C

	TEST LOG	TEST NUMBER: HNF-1857	TEST LOG PAGE NUMBER: _3Of/_			
TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test						
TIME/DATE _	EVENT DESCRIPTION/SIGNATURE					
10:40	with Step 2.24, Boxes PLV-Z and PLV	-4 on MCS or	serview screen			
10:45	Add step After 2.25.4, bypass hi-loglarum on 102-54-transfer pump					
11(00	So that it won't shot down pump after 5 minutes  Step 2.25.3, VSD-1 tripped on "overfrequency" according to VSD-1  LED display; after booster pump START scleeted at MCS. Turned off  Power to VSD-1 (per vendor manual instructions for troubleshooting) and then					
11:05	restarted approx. a minite later, to reset VSD-1.  5 Step 2.25.3, booster pump start selected, RUN LED illuminated for approx  2 seconds then returned to DRIVE READY (VED illuminated). FAULT LED NOT  illuminated. Booster pump stopped on McS for unknown reason.					
	1:20 Reason why USD-1 and booster pump shutting down was due to PLC logic error, 10 psig minimum required at PT-3125A and 50 psig required at					
	PT-3125C (to get "booster pump is running" on Mcs). Were programmed  vice-versa. Switched to proper logic and transfer scheme 2A executed  and booster pump started successfully, no shutdown at VSD-1					

ATTACHMENT C

TEST NUMBER: TEST LOG TEST LOG PAGE NUMBER: HNF-1857 4 of <u>18</u> |TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test TIME/DATE EVENT DESCRIPTION/SIGNATURE To allow boosky pump to stop, must remove pressure provided to PT-31252 2:05 2:20 booster pump when STOP button pressed (transfer pump still running mp actually Starts but then stops after 5 seconds, second delay programmed in the logic. Modify Her say booster pump stops after 5 seconds." After troubleshooting, Step 2.25,9 thru. 11 successfully comp PLC logic (removed force" left in Computer terminal on right would not accept transfer scheme ZB value lineup (Roeset, initiate, type 2B), no path in GREEN Step. 3,23,1, Diversion Box Icon in transfer path (Scheme 28) on Mes overview screen is illuminated in RED. Does not affect performance

of interlock fests as PATH CLEAR is illuminated

(would stop on low inlet pressure when transfer pump stopped)

Step 3.37.6, add step to RESET P-102-SV-02A Hr-low limit alarm.

Remove step 3.37.11, booster pump does not stop on high in let pressure, direct

REVISION NO. <u>0</u>

ATTACHMENT C

	TEST LOG	TEST NUMBER: HNF-1857	TEST LOG PAGE NUMBER:  5 Of 18		
TEST TITLE: Preoper	ational Test POTP-007, Cross Site Transfer	System Integra	ated Test		
TIME/DATE	EVENT DESCRIPTION/S	IGNATURE			
	Select booster pump START		a verify pump stopped.		
3:55					
3:56	After step 3.38.4, Reset SY pump hi-low.				
4:15	Testing Interlock 7,10,14 on both pumps 8-312	SA: B using V	TPS.		
<u> </u>	Other interlocks will test having pressures (20) "Forced" which has same effect. Will not cha				
4:20	Changing from Transfer Scheme 2B to 21				
	and get correct value lineup, however Tra	nsfee Path or	rilluminates (GREEN)		
	\$ 010 ZB path not ZA path like it sho	wrona.	sturny line onth 15 LI		
	(GRAPHIC IS COMPECT AS 15)	confusion	with SY-A and SY-B		
12/15 7:00	Pre-job meeting at Diversion Box	like their	is a path for 2A and ZF		
	PCS forced bits (20 psig) to inlet passure		lischarge pressure		
	on booster pumps, allowing VTPs's to be removed for Interlock 6 tests.				
10:00	Interlock 15 test, booster pump DOES NOT physically start.				
	when bypass valve, drain valves, or vent valve opened, "STATUS UNKNOWN"				
	Appears on Missireen for Pul-Z and pur				
	the STARET by Hon depressed.				
11:60	on MCS screen, when drain valve (MOV) actuated the value icon stays RED				
	for approx 10 seconds until limit switch finally -	trips, turns icon	WHITE OR GREEN		

PREOPERATIONAL TEST POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST
HNF-1857
PAGE 1 OF 1

TEST LOG
PAGE NUMBER:
HNF-1857
Of 18

TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test TIME/DATE EVENT DESCRIPTION/SIGNATURE MOV-3125BE will not open from MCS, physically did not open-local vertication MOV-3125BF when opened from MCS, also opens MOV-3125BE Construction changing wire labels in 244-A, LDA-841 tripped on mov-3125BE problem appears to have been caused by RSVIEW (MCS) and the 9600 band data highway. PCS thinks that stringing the new, temporary cable aboveground (in progress) will prevent such problems in future MOV-3125BE BF now operating properly. L. Atkins, FDNW construction, added all (topped off) oil reservoirs on pump bearing housings Al, AZ, A3, A4 to manf. recommended levels LAL-3125AZ in AlARM after oil fill 2:00 Nipple, 14" x 4", to AZ or krobent downwards after inspection, Perhaps a heavy object feel on it during shipment? Replaced nipple.

Adjusted oiler to max height and tightened oil Float cosing down

Sulzer Bingham field rep. to resolve.

but LAL-3125AZ still in alarm on MCS. Will contact

REVISION NO. 0

ATTACHMENT C

	TEST LOG	TEST NUMBER: HNF-1857	TEST LOG PAGE NUMBER:
TEST TITLE: Preoper	rational Test POTP-007, Cross Site Transfer	System Integr	ated Test
TIME/DATE	EVENT DESCRIPTION/S	IGNATURE	
	, 0	.61 m/s	
4110	Vibration interlock activates at 13.7 ma, step		ration velocity
	tolerance + 0.05 in/s corresponds to +. 8 mo	1	<i>j</i> 11
	interlock within tolerance		
		•	
· · · · · · · · · · · · · · · · · · ·			
		•	
12/16 7:00	Pre-job at Diversion Box		·
11:00	All morning, communications problems he	tween OIT (n	1CS) computer
	terminals and PCU-1. Installation of		
	prevent these problems. (INSTAUED DA	TA HILHWAY F	RON OIT TO PCUI
11:30	LAL-3125AZ switch supposed to be fixed.	11-08 2042	<b>2</b> -24.
12:30	successfully completed pump seal high flow or	nd low pressur	e ksts
	for pump P-3125B.		
	Temperature simulator instrument has dead		
1:15	Attempted to perform Interlock Z test.		
	PT-3/68 pressure transmitter 0-1000 psi ra	inge has not	tyet been
	replaced with a -15 psi to 30 psi range - (vacuum)	transmi Hea	( REPLAGO TANK
	(VACWIN)		DE CONNECT D

REVISION NO. 0

ATTACHMENT C

	TEST LOG	TEST NUMBER: HNF-1857	TEST LOG PAGE NUMBER: 8 OF 18	
TEST TITLE: Preoper	rational Test POTP-007, Cross Site Transfe	System Integra	ated Test	
TIME/DATE	EVENT DESCRIPTION/	SIGNATURE		
2 100	Have new batteries for temperative sim	vlator, but no	w have no.	
2:15	Step 3.31, drained entire bearing oil reservoir Bl and got no alarm, LAL-3125B1.			
2:20	Volume of oil = 1020mL including oil in globe  Volume of oil in globe = 200 mL			
2:30	Discovered that LAL-3125BI was jumpered out! Checked the other  3 to verify theyother were not also jumpered.			
3:00	Nobody can figure out temp. simulater manual. Will postpone and have  Belhaven bring out a calibrated decade box tomorrow.			
3130 3145	Performed pump seal high flow tests for pu Problem with software, STOP bit for	np P-3125A. 2-102-54-02A tra	insfer pmp	
4:30	not dropping out (0:7/3 and 0:7/4) to Problem solved by Friedrich and PCS Software change on SOV-3125D.	guy. Was cau	sed by	
	OPOSED TO STEPS 2.50 2 2.61 AS	the state of the s	Į!	

REVISION NO. 0

ATTACHMENT C

TEST NUMBER: TEST LOG PAGE NUMBER: TEST LOG HNF-1857 9 of 18 TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test TIME/DATE EVENT DESCRIPTION/SIGNATURE 7:00 Pre-job meeting 12/17 UHrasonic Flowmeter DF868 Electronics Console Parameters Step 4.12 of Pre-Regulaites Value Transducen No. - will be changed. Current transducer Pipe Material Proc O.D. 3.5 mohes 0.216 inches NO Tracking Windows No water Normal water Water Temperature Standard 1,0

Transducer Spacing 3,279 in, 83.3 mm

REVISION NO. <u>0</u>

ATTACHMENT C

		HNF - 1857	PAGE NUMBER:			
TEST TITLE: Preopera	TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test					
TIME/DATE	EVENT DESCRIPTION/S	IGNATURE				
12/18/07	FERRMED VALUE LINEUPS, REU	oork alls	NET SENSOUS			
	ON BP'S (UNDERDIRECTION) FRO					
	FIELD REP, GENERAL PROP TO TILL	PIPG				
12/19/97	0836 BEGAN FILLING PIPE					
·	20945 BWATT TRUCK - REFILL -C	ENTINUE 7	acing.			
	2 1245 BECAN RECIRC WITH SUPPLY PUMP					
	SYSTEM CLEDRED OF AIR					
	= 1600 VENTED BD - LARGE AIR BUBBLE IN PUMP					
	(BULL THEU US PAT CEMEN)					
	~ 1000 BUMPED PUMP - ROTA					
	\$1645 22 BUMP- ROTATION	correct	[			
	ALGEO RUN PUMP	7 15-01-				
10/01/07	# 1750 FOCKED DOMM FOR ENFING					
	0900 BEGAN CIRC. OF WATER	udo Alar	277 400 0			
	E-1 - not when all 312 TO 15					
	F-1 - note values SOU 31250 €E • PEBET EXCEL TIME ON USD TO 10 See					

REVISION NO. <u>0</u> ATTACHMENT C

	TEST LOG		TEST LOG PAGE NUMBER:  // Of _/8
TEST TITLE: Preopei	rational Test POTP-007, Cross Site Transfer	System Integra	ated Test
TIME/DATE	EVENT DESCRIPTION/S	IGNATURE	
12/2067	% 1030HRS ATTEMPTED TO STATE T	BPA - FA	LED
	CHECKED PORMETERS - FOILED	DGAN	
	LOCKED OUT USD - BEGSN TR	ourte sy	COTING.
	BLOKE COUPLING - MOTOR SP	INS-PUM	P IS LOCKED
-	DECISION MADE TO OPEN A	) MP BEFOR	E TESTING
	13 CONTINUED	,	
1500 Ans	DECONFIGURED TOMP & SUS.		suny
	\ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \	S. WILL III	106-10
		row do	
		DISASTEM	
	THE STAND VALLE TO ALLOW	J DISASTI	14
*	-ME PUMP	***************************************	KN 12/20
<u> </u>			
		•	

REVISION NO. 0

ATTACHMENT C

TEST LOG PAGE NUMBER: TEST NUMBER: TEST LOG HNF-1857 12 of 18 TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test TIME/DATE EVENT DESCRIPTION/SIGNATURE RESUMED TESTING ON POTR-DOT AFTER PUMP FAILUR 2/11/28 REVERIFIED ECETACEALLWOUR PER STEP 1,3 AND ADPENBIX D. REVENEUR STEPSIELL 9 THRU 1,13 COMPLETED STEPS 1.19 THRU 129 2/12/98 RESUMED TESTING AN POTP-DOD STEP 1.30 - DIVERSION BOX COMPRESS - STEP 2.24 e3,24 BOXES ARE RED DUE TO MISSING VUMPERS & Pressure. SIGNALS. - MOU-3125AK CYLLES ON AND OFF TURNED OFF -POWER TO TROUBLESHOOT VALUES. WITH 29 PATH CLEAR INSTED 2/13/98 - VENT STATION SUMP WAS IN ALARM - ADJUSTED ALANN AND RETESTED ALANN NOW CLEGA - RESUMING TESTING ON B-PUMP INTERLOCKS - TO FACILITATE TESTING THE B-PUMP HILTAP WILL BE USED TO TEST BOTH PUMPS WHICH REQUIRES UNIVESOU-31254 OPEN

REVISION NO. 0

.ATTACHMENT C

	TEST LOG	TEST NUMBER: HNF-1857	TEST LOG PAGE NUMBER:  13 of 18
TEST TITLE: Preoper	ational Test POTP-007, Cross Site Trans	fer System Integ	rated Test
TIME/DATE	EVENT DESCRIPTIO	N/SIGNATURE	
2/3/98	- TROUBLESHOOTING. B. pump VEN	T UPLUE A	10U-3125 AK
	- PUMP 15 BEING STANTED	IN STER	7.6 47 20%
,	Speed pen suczen Reou	EST FOR IN	171AC STANTUA
	AND REDUCED TO 50%	IN STEP	7.25.1 AFTES
· .	Pump STANTS. ALSO SULZI		
(2/19/98)	RAMD BE SET TO S SECTION 7 - SETUP SYSTEM TO OPEN	LATE B-1	SD 1 & 2 .
	PER SECTION 8:0		
	- STANTED B-PUMP TES	T NOTIC	60 A-Pump
	WAS RECENTED A SAME	DO CHARG	E PRESSURE
	BS B- PUMP. STOPPED	PUMP TO	TROVBLE SMOOT.
· ,	FOUND VENT VALUE T	O A- PUMP	mOU-3125AL
	WAS NOT CLOSING.		
2/18/58	- REPLACING M- PUMP. VE	NT VALUE	mo U-3125At
	WIGH DRAIN VALVE From	_ pr pum	po 10 ACCON
	B-Pump TESTING TO		· II
	IS NOT WORKING PROPERLY	Y FOUND LOOS	E WIRE, THEHEO
	-STEPS 7.33.1 THAN 7.33.5 AND AL	026 WITH 8134	1 THEO 8.34.4 C 8.36
	WENE DELETED AS THESE STEPS WHICH HAS ALLNEADY BEEN I	ANE TO ASSIST	12 TONANG PIL

WHICH HAS ALLREADY BEEN DONE. TTACHMENT & PAGE 23

REVISION NO. 0

ATTACHMENT C

TEST LOG TEST NUMBER: HNF-1857 TEST LOG PAGE NUMBER: 14 of 18						
TEST TITLE: Preope	TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test					
TIME/DATE	EVENT DESCRIPTION/SIGNATURE					
2/19/98	- RESUMED TESTING OF B-PUMP AFTER FOR					
	TROUBLE SHOOTING B-PUMP SPEED PRIVEMOTED HIGH 7.0.30 IPS VIDERATION AT CENTAIN SPEEDSENCASE MENT LEAR DETECTON LOB-3/80					
·	ALARMOD AT 15:06, 15:12.					
	- CONCASEMENT LEAK DECECTON LD4-3/6/					
	- COMPLETED B-PUMPTESTING ATTEMPTED TO RUN					
	A-PUMP BUT THE USD EXIBITS THE SAME					
	PROBLEMS THAT THE B-DRIVE HAD. CORNERPM					
	STOPPED FROM MCS MOTON RPM SURGES BEFORE					
	STOPPING) ALSO MOTER PUMP RESTANTS BUTO MATICALLY AFTER USD POL					
	THE A-PUMP AFTER NAVES SOU-3125 At 2 SOU-355A)					
	MARTIN QC, KW2-20-98					
	- NOTED HIGH VIBRATION > . O. 601PS ON A PUMP					
	AT APPROX 3000 RPM.					

<sup>-</sup> NOTE USD VENDOR SET NINIMUM RUN FREQUENCY, TO 30 HZ THEREFORE PUMPS WILL NOT RUN BELOW 1800 RPM AS CURRENTY SETUP.

REVISION NO. 0

ATTACHMENT C

TEST LOG PAGE NUMBER: TEST NUMBER: TEST LOG HNF-1857 15 of 18 TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test TIME/DATE EVENT DESCRIPTION/SIGNATURE 2/20/98 - EPP COMPLETED : RUN IN OF A-PUMP IP MANUAL - ATTEMPTED TO RUN A PUMP IN PID-AUXO WITH SETPOINT OF 240 GPM AND PROPORTIONAL BALA SET TO . 8 ONLY GOT 90 4PM DE FLOW ALSO AFTER APPROX 10 M. FLOW DIA NOT INCREASE, ATTEMPTED DIFFEREN SET POINTS BUT WITH LIMITED SUCCESS STOP TESTING DUE TO TIME CONSTRAINTS. 2/23/98 - DIO NOT RUN PUMPS DUE TO FONW SAFETY CONCERNS. - RERANGED FLUSH PUMP FLOWMETER AND SLURRY PUMPS FLOW TRANSMATER. 2/24/98 - PERROMALERT ON SITE 70 INSTALL NEW SOFTWARE IN ENRASEMENT LEAK DETECTOR PANELS. ATTEMPTED TO OPERATE B- FUMP BUT USD PRIBLEMS CONTINUES TO SHUT DOUD

TO PREVENT PUMP FROM OPERATION OUTSIDE PUMP CURVE HNF-2504, REV. O PER JIM COLLINS (FONW LEAD PESILO ENLINEER)

REVISION NO. 0

ATTACHMENT C

TEST LOG PAGE NUMBER: TEST NUMBER: TEST LOG HNF-1857 16 of 18 TEST TITLE: Preoperational Test POTP-007, Cross Site Transfer System Integrated Test EVENT DESCRIPTION/SIGNATURE TIME/DATE 2/25/98 - ATTEMPTED TO RUN B- PUMP PUMP WILL NOT RUN PROPERLY ISOLATED PROBLEM TU VSD. (CONTACTED VSD VENDOR FOR ON-SITE SERVICE) - PERMAGERT ON SITE LOADING NEW SOFTWARE SO PUMP TESTING 15 \$TOPPED 2/16/98 - RAN A-PUMP GOT PUND TO OPENATE WITH INITIAL PID SETTINGS - HIGH VIBRATION CONTINUES ON A-PUMP AT BAPROX 3000 Rpm PIPEFITTENS WILL BITTEMPT TO BNCHOR PIPING DOWN DUD THEN WE WILL RETEST PUMP. - RAN B-DUMP IN PID BUTO AT 110 GPM PER SECTION 9 OF PROCEDURE. CONTINUED TESTING ON A PUMP IN PID BUTO MODE. COMPLETED A PUND AUTO TESTING.

REVISION NO. 0

	TEST LOG	TEST NUMBER: HNF-1857	TEST LOG PAGE NUMBER:
TEST TITLE: Preoper	rational Test POTP-007, Cross Site Transfer	System Integra	ated Test .
. TIME/DATE	EVENT DESCRIPTION/S	IGNATURE	
3/24/98	RESUMED TESTING STARTE - STEP 10.14, 1 PCU-2 15 RES 15 > 70 PSIG AND PCU-5 1 MPS 15 IN ALBRA	O BECAUSE S REA BE	IN LET PRESS
3/27/98 3/28/98 *\ 3/31/98	CONTINUED TESTING SECTION  COMPLETED TESTING SECTION  DURING INTERLOCK TESTING  NOT BEEN LABELED PER  DOCUMENTS. CORRECT W	WIRES A	\$ 12. VOTEO HAO OESIGN
	PS DETERINED BY TEST  PELACLED TO MATCH DESIGN  TO COMPLETION OF POTE  - NOTE 57Ep 7.5,36,8,27 & 9.38	ENGINEEN UN DOCUM -OOD. THE USD B	AND WERE ENT PRIOR  S DESIGNED
	DOES NOT PERFORM THESE	FUNCTIONS	

REVISION NO. 0

ATTACHMENT E

	TEST EXCEPTION LOG					
TE #	DATE	DESCRIPTION	DISPOSITIONED	DATE CLOSED		
-001	12/20/97	Pump P-3125A is locked up, however motor turns freely when decoupled from pump.	Disassemble both pumps P-3125A & P-3125B under vendor supervision and determine cause of lock up.  Vendor determined that the pump locked up because it was provided with a non protected (non overlaid) surface on the hub side of the impellers. Both pumps were modified to include a hub side wear ring and all wear rings were overlaid with the same type of material as the eye side wear rings for abrasive service, per SBPI NCR 155599, 155766 and 155767.  Resume testing upon completion of corrective work and close-out of referenced NCR's.	02/11/98		
-002	02/02/98	Observed leakage from pump air seals.	Replaced flowserve model #982 seals with new "wavy face" technolgy seals. Rechecked pump air seal flowrates per steps 1.8 and 1.9.	02/11/98		

REVISION NO. 0

ATTACHMENT E

-003	02/17/98	When B pump was started, pressure sensors (located between the A pump closed inlet and discharge valves) on the A pump loop also indicated a pressure rise. This indicates a leakage path from the B pump discharge to the A pump loop. The problem was identified as a leak through the A pump vent valve (MOV-3125AK).	<ol> <li>Replace MOV-3125AK valve body with valve body from first stage drain valve (MOV-3125AJ) and resume testing (concurrence by Jim Collins FDNW Lead Engineer).</li> <li>Procure a direct replacement valve body and install it in the MOV-3125AJ position.</li> <li>Verify that this rework meets original pressure testing requirements by performing a in service leak test.</li> </ol>	02/19/98
-004	02/18/98	The B-pump VSD goes into either overcurrent or overvoltage fault which causes the speed drive to shut down. This happens intermittently when the VSD is given a remote speed change from PCU-2.	VSD vendor to troubleshoot and repair. Retest to verify remote speed changes do not cause the drive to go into fault and shutdown.	2/20/98

REVISION NO. <u>0</u>

ATTACHMENT E

117			r · · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·	
	-005	02/19/98	Both the A and B-pumps exibit high vibration at certain RPM. The vibration on the A-pump exceeds the high vibration setpoint which causes the pump to automatically shutdown. Typically A pump exceeds .60 IPS at approximately 3,000 RPM and B pump exceeds .30 IPS at approximately 2,950 RPM.	Pump vendor to troubleshoot and repair. Retest to verify vibration is within acceptable tolerance.  MOUED TO OAC PUNCHLIST	3/3/98
	-006	02/19/98	Both A and B pumps restart automatically after a VSD fault because the start signal from PCU-2 is latched in and a VSD fault does not unlatch the start signal. Also the VSD's are reversed.	Write ECN to correct logic (unlatch start signal)and wiring (start/stop inputs reversed) at PCU-2 and retest that pump does not restart after a VSD fault.	3/27/98
			·		
		· ·			

REVISION NO. <u>0</u>

ATTACHMENT D

TEST EXCEPTION REPORT					
TEST PROCEDURE NO. & SECTION:	TEST NAME:		T.E. NUMBER:		
HNF-1857, 7.23	POTP-007 INTE	GRATED TEST	TE-001		
DESCRIPTION OF PROBLEM: Pump P-3125A is locked up, however motor turns freely when decoupled from pump.					
ORIGINATOR:		IMPACT ON TESTING: X HOL	D FOR RESOLUTION 🗆 CONTINUE		
M. D. Gerken		M. D. Gerken	12/20/97		
ORG: DATE:		TEST ENGINEER	DATE		
Disassemble both pumps P-3125A & Vendor determined that the pump los surface on the hub side of the impell wear rings were overlaid with the sat SBPI NCR 155599, 155766 and 155 Resume testing upon completion of SEE ATTACHED VENDO	cked up because ers. Both pumps me type of materi 767. corrective work ar	it was provided with were modified to incl al as the eye side we	a non protected (non overlaid) lude a hub side wear ring and all ear rings for abrasive service, per		
DISPOSITION AND RETEST REQUIREMENTS BY: M. D. Gerken  DATE  DISPOSITION ACTIONS COMPLETE:  Verified Av Sulu 2-10-98  DATE					
QAE CONCURRENCE WITH DISPOSITION OF	(if required): /10/98		/A		
DATE		TEST ENGINEER	DATE		

	•
NONCONFORMANCE REPORT	Page 121-12-990
ject No. W.O. No. Location (Bldg./Area) Safety Class W-058 C12300 B1dg. 6241-A/200W 3	NCR No. W-058-27 (FDNW-18)
Job Title Replacement Cross Site Transfer System	
	Sistribution B 12-29-97 FDH FDAW J O Knight 1,3
	NHC J L Gilbert 1,3 E A Pacquet 23 47 1,3
Section 3.3.4 States: The pump, motor, and antitiary equipment	G L Parsons 1,3 C Van Katwijk 1,3
	FDNW A I Files 1,3 Q C Files 1,3 Records Management 3 Const Doc Control 1,2 Compliance Assessment
Description of Nonconformance:	Quality Engrg 1,3 PM/J L Henderson 1,2,3 FCE/T E Nemzek 1,2,3 J R Collins 1,2,3
the slurry transfer pump P-3125-A failed to function properly.	J E Thomas 1,2,3 QA/L R Hall 1,3 J A Peltier 1,3
HNF-2504, REV. 0 ATTACHMENT 1 PAGE <sub>231</sub>	
HINT-2001)	
Originator JEFF MiddleTons Date Manager	Date 1/2/0

-6002-220 (02/97)

NONCONFORMANCE REPORT (continued)	Page <u>\$\frac{1}{2} \cdot 2</u>
Sposition  Use-as-is* Reject Repair* Rework  ASME Code Related No Yes  (ASME Code Section )  MOS9	<u> </u>
Disposition Instructions (generally not required for use-as-is and reject dispositions):  Sulzer Bingham Pumps to rework impellers per  NCR No. 155766, see attached.	their
ECN (generally required for repair and use-as-is dispositions):  Yes No If yes, ECN No  If no, provide explanation:	
Disposition Justification (if applicable):  Pump impellers rework will enhance the wear, the hub side and does not affect the pumps capa to meet the original specification requirements.	parts on bility
7	
HNF-2504, REV. 0 ATTACHMENT 1 PAGE 232	
Approval/Concurrence:  Construction Approval Customer Projects Ap	proval
CF/CM Engineer NA Date NA Engineer At Particul	Date
Field Quality Engineer NA Date NA QA SEE DESIGN APPROVAL  Design Approval Other Concurrence	Date <u>NA</u>
Design Engineer Date 1/12/98 FDH NA	Date
Quality Engineer (FONW)  Quality Engineer (FONW)  Quality Engineer (FONW)	Date
Safety Engineer NA Date NA Environmental	Date
Closure  Disposition Completed as Directed  Other (Explain) PER DIS POSTION SEE AFFICIENT Supervisor (  We # 1552 Class For Roy W. Clares Form)	Date 12 1660

1/

4-6002-220B

PAGE 1/2

SULZER PUMPS A

NCR #W-058-27 (FONW-18)

Between Bearings Business Unit

Kevin M. Harold

Product Group Manager 2800 N.W. Front Avenue

Portland, OR 97210-1502

U.S.A.

Tel. (503) 226-5354 Fax (503) 226-5242

Your reference: MZ4-APX-80708
Our reference: 1E776/777

Date: January 9, 1998

Sulzer Bingham Pumps Inc., 2800 N.W. Front Avenue, Portland, OR, U.S.A. 97210-1502

Fluor Daniel Northwest Inc. 2355 Stevens Drive Richland, Washington 99352-1100

Attn: Mr. Jack Henderson

Subject: NCR Report No. 155766 & Efficiency Update

Dear Mr. Henderson:

Please find attached the NCR generated in our factory for the rework described in our previous letter.

Please also note that an error was made in the hub ring efficiency calculation. When the correct values are used, the calculated losses due to this upgrade are less than 0.2% which is negligible.

If you have any questions or require additional information, please feel free to call me.

Best regards,

Best regards,

Kevin M. Harold

Zein W. Harold

HNF-2504, REV. 0 ATTACHMENT | PAGE 233

				FROM: SU	LZER BÎ	NGHAM		11	D:226	5242	<b>4</b> _	PAGE	2/2
				JMPS INC.	Ŋ			PA	SE '	4 OF	7	4	700
	NON-CC	MEORM.	ance kep	ORT (NCR)			NUR	# wo			NCR No.	1557	66
,	FORM !	561A-10							- WW		Sheet_	1 of	
		edure H3				ote: All notatio	nsvotcume	entation to					
4	PART DE				,	EMBLY) NO.	SEFIAL N		SALES OR		WORK O	RDER NO.	
-			->-1		7	20	IE	ط7		76		MA	
		S NUMBER		MATERIAL NI/A		PATTERN NO.	<b>A</b>	LOCATION	5	SUPPLIER N	AME	P.O. NO.	1/4
	OTY ON		6-08	OTY REJECTED		PART STATU			ASSY	,	ORDER X NO		•
	GIT ON	JABER	<u> </u>	GIT NESECTED	<b>'</b> {	PARI SIAIO	3; WMPL	- XX INCO	1		ONDER & IN		``
	COMPON	ENT NO.	N	<b>/</b> A	LAST OF	PER. COMPL	N/A	MA	TERIAL TRA	CE CODE NO.	PER (	:4	
				FOR REJEC	TABLE C	ONDITIONS	85508	THE BE	OUIBED		GRIC	MAP LOCA	TION
	LINE	QTY		TION AND TI							ALPHA N	A NO.	<b>시</b> 요
	1	4	N					L 13N	N			A	
			<b>U</b> (54	SCHAL	54-1		<del></del>			SKIS VOT		- neop	<del></del>
	2		THE	#0B	DIAL	CATEL	-5 A-	NP 3	TAC	G PIE	7 CE- ( \$	4055	700
	3		<b>D</b>				<del></del>						_
	4				^ -	- 3				- 0	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	<u> </u>	- 77. 2
			5-1	ECY_	0127	<u> </u>	<del></del>	<del>/// (/)</del>	1109	<u>&gt; 0</u>	110	<u>D-//</u>	5+16-C
	5		<del>-</del>	B-IE	776	-27		1/1/2	98			<u> </u>	
	6							1	1				
				<u> </u>									
	7		DE	MENT	pick	60 U	P	) Yu	ce He	2B 51	DE D	<u>い Sy</u>	198
	8		2 TT 2	5 120	The	Free	D	URLA	۶ ود	START	Up.		1
	9								/				
		<u> </u>		<del></del>		<del> </del>	<del></del>			···	<u></u>		<del></del>
	10				<del></del>					$\alpha \alpha$			
		ED 8Y: 🗻 Print Name	1.1	ec <del>us ice</del>	ا حبر	DATE: 1/S.	198	APPROVED Quality Dep		tu	zelen.	DATE: 1/8	198
i		SIBILITY		4 Com	E	RROR CODE!	10	PART	FAMILY:		WORK CENTE	RALIA	
•	UNE	ACTION	TO CORRE	CT: USE A	sis Ts	CRAP D	<b>TREWORK</b>	<del></del> -	·Use	as is Disposition	requires Engineer	ing justification.	
	Please check a box TREPAIR TOTHER RETURN TO SUPPLIER Requires Engineering Approval for non pre-approved repairs												
	and Engineering Justification for ASME items only.												
	REWORK EXISTING IMPERIERS TO DRAWINGS												
		B-	-1E-	176-2	25	lev A	A	42	<u>B-1E</u>	<u> - 276 -</u>	<u> 27 /2</u>	av A	
	ł										•	•	
		120.	· mand 1	EX	· · · · ·	0 0+	56 1	. 1 6-1	<u> </u>	2,,,98	>~		
	-							004	<u> </u>	Crass 2			
		E	SKARR	2209		<u>4978</u>	<u>3</u>			····			
	Ľ.	_م_ ا											
			Per	ECE	01-	0144	マラ )	)	-				
					ma R	V. Pa	<u>سرء د ده ۲</u>	in D	27200	Ome	SEMB	1- []	m in the
	-	120,	STALL	NEW W	ENK	M2108	COLVE	110/105	· vvous	1/5/0	0751410	G	siviety/>
	DISPO	SITION	8V:			1			Ď.	ATE: //o	. / -		· · · · · · · · · · · · · · · · · · ·
	(Please I	Print Name	$\mathbb{R}^{n}$	GER (	Kisch					'/8	198		
					AF	PROVAL	and/or	CONC	URREN	ICE			
	ļ	<del></del> -					d signsture o	oxes below to	or reduited a	oprovals and/or c			
			•	SIGNATUR	(E	DATE	1	O+	<b>0</b> #1/-3		ATURE		UE.
	1		ngineer_		4)	1 . [	7	-	•		··- <u></u>		
	120	ésign E	ngineer_	Form	feed)	1/8/	128	☐ Othe	er			<u> </u>	
	P	urchasi	ng					☐ Othe	er				·
	-		•	Ml	-S	9. Jan	98	☐ Othe	er .				
				<del></del>					<del></del>				
	1			R Part 21 is ective Action	•		r Barre	on Cardin		reported by:  upproved by:		<u></u>	<del>_</del>
								- N CARABIO		Phioreg by.			
	INCH	Action	compi.	(Bv Quality (	Jept. Univ	n crosede	>1:				DATE:		
	LINIE	-04 DE		ATTACUNT	Nitt 1 1 10 40	SEart					÷		

**Telefax** 

Division of Sulzer Rotea

Sulzer Bingham Pumps Inc. Between Bearing Pump **Bob Fowler** Contracts Administrator 2800 N.W. Front Avenue Portland, OR 97210-1502

Date:

February 26,1998

To:

Fluor Daniel Northwest

Lanny Hall

Fax 509-373-6303 Phone 509-372-0583

Tel. (503) 226-5280

U.S.A.

Fax (503) 226-5583

Pages: 4

(including this one)

Subject: Transfer Pump Contract # DE-AC06-87RL10930

Purchase Order MZ4-APX-80708

SBPI S/O # 1E776/777

QA signed NCR Reports # 155599, 155766 & 155767

Dear Lanny,

Following up on your phone call this afternoon morning, attached is the information you requested with regards to the closed NCR reports:

Should you have any questions or need additional clarification, please call.

Best Regards


**Bob Fowler** 

cc: Kevin Harold Tom Richfield

> HNF-2504, REV. 0 ATTACHMENT | PAGE 335

HNF-2504 REV. 0

NON-CONFORMANCE REPORT (NCR) NCR No. 155766 FORM 561A-10 Sheet \_\_\_\_ of \_2 Note: All notations/documentation to be in black ink. Ref Procedure H31.2 ITEM (ASSEMBLY) NO. SERIAL NO. SALES ORDER NO. WORK ORDER NO. ESCRIPTION N/A 1E776 200 1872b CLEMENT MATERIAL PATTERN NO DRAWING NUMBER REV. LOCATION SUPPLIER NAME P.O. NO M/V NA N/V B-1E-776-08 PUMP ASSY QTY REJECTED PART STATUS: COMPLIX INCOMPL. O.C. ORDER NON-O.C. ORDER - QTY ON ORDER LAST OPER. COMPL MATERIAL TRACE CODE NO. COMPONENT NO. 7/17 P = 2 GRID MAP LOCATION NOTE: FOR REJECTABLE CONDITIONS, REPORT THE REQUIRED QTY LINE ALPHA NO NO NO CONDITION AND THE ACTUAL CONDITION. 1 2 3 4 5 8 7 8 9 10 REPORTED BY: . DATE: APPROVED BY: (Quality Dept. Only) Print Name) FREOR CODE PART FAMILY: WORK CENTER ONSIBILITY CODE: 10 900 ACTION TO CORRECT: REWORK " USE AS IS SCRAP Use as is Disposition requires Engineering justification. \*\* Requires Engineering Approval for non pre-approved repairs REPAIR OTHER RETURN TO SUPPLIER Please check a box and Engineering Justification for ASME items only. GX1577NG CASE WEAR DRAWWS -0144 AVETMPEL DISPOSITION BY: -(Please Print Name) APPROVAL and/or CONCURRENCE (Quality Department shall check the required signature boxes below for required approvals and/or concurrence) SIGNATURE DATE DATE Manuf, Engineer. Specify Other(s) Design Engineer. Other ] Purchasing . ☐ Other 11/1/1 √Z¹ Quality Dept. \_ Other Check box if 10CFR Part 21 is reportable Reported by: Check box if Corrective Action is required (Significant or Reccurring Conditions) Approved by: NCR Action Compl. (By Quality Dept. Only) CLOSED BY: DATE: ATTACHMENT | PAGE 136

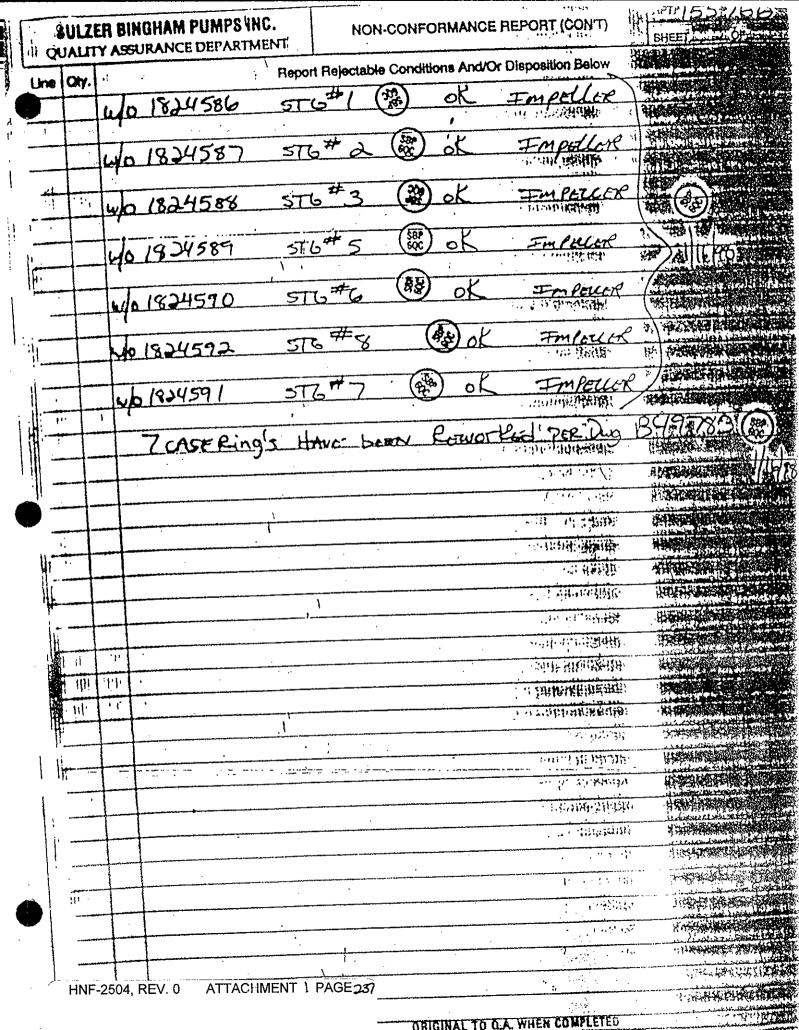

FORM 561A-10

ID:5032265583

PAGE

2/4

NON-CONFORMANCE REPORT (NCR)


155767 NCR No. Sheet \_\_\_\_\_\_ of \_\_\_\_2

Ref Procedure H					
DESCRIPTION	ENT 200 15777 15777 MA				
B-1E7	76-08 N/A N/A PUMP ASSY N/A N/A				
OTY ON ORDER	OTY REJECTED   PART STATUS: COMPLIZE INCOMPL. Q.C. ORDER NON-Q.C. ORDER				
COMPONENT NO.	N/A N/A N/A N/A				
LINE QTY	NOTE: FOR REJECTABLE CONDITIONS, REPORT THE REQUIRED  CONDITION AND THE ACTUAL CONDITION.  GRID MAP LOCATION  ALPHA NO. WIA				
1	DISASSEMBLE SLEMENT AND DUMENSION ALLY INSPECT				
2	THE HUB DIAMETERS AND STRUE PIECE (HUB STOCK)				
3	DIMMERS - AND RECORD DIMENSIONS				
4.	CHECK PARTS TO DRAWINGS \$ 17675, B-15-776-25				
5	-3 B-16776-27 TR 1/8/97				
6					
7	SEE NCR 155766 - THIS ELEMENT DID NOT				
8	START-UP, BUT WAS RETURNED FOR MODIFICATION				
9	PER 1E-776 PURAP.				
10					
REPORTED BY:	E) T. PICHFIELD DATE: 1/5/98 APPROVED BY: Stolen DATE: 1/8/98				
PONSIBILITY					
1 1	N TO CORRECT: USE AS IS SCRAP REWORK Use as is Disposition requires Engineering justification.  check a box "REPAIR OTHER RETURN TO SUPPLIER "Requires Engineering Approval for non pre-approved repairs and Engineering Justification for ASME items only.				
7 25	WOLK EXISTING IMPHLEES TO DRAWINGS				
1	B-18776-25 Rev A AND B-18776-27 Rev A				
	OCITI 18 - C3 160 A AND CITE 18 - CT				
7/20	WORK BXISTING CASE WEAR RINGS TO				
N	RAWING 849783				
7 (7	Dowoty DER ECR 01-014437)				
IN.	STAL NEW WEAPS, BALANCE IMPRIESS & REASSEMBLE ELEMENT.				
	DAYE: ///				
DISPOSITION (Please Print Nam	nei Koger Kisch /8/98				
	APPROVAL and/or CONCURRENCE (Quality Department shall check the required signature boxes below for required approvals and/or concurrence)				
	SIGNATURE DATE SIGNATURE DATE				
☐ Manuf. I	Engineer Specify Other(s)				
☐ Design	Engineer 474 18/18 Other				
Purchas					
Quality	Dept. 75 9 Jan. 98 Other				
	pox if 10CFR Part 21 is reportable Reported by:				
	xx if Corrective Action is required (Significant or Recouring Conditions)  Approved by:  Approved by:				
NCR Action Compl. (By Quality Dept. Only) CLOSED BY: ( ) any Leader DATE: ( - 23-98					

Note: All notations/documentation to be in black ink.

TYZER BI	NGHAM PUMPS INC	NON-CO	IFORMANCE REP	ORT (CONT) A	SHEET LOF MANEE
EA YTUAUL	SURANCE DEPARTME	Report Rejectable Con	ditions And/Or Disp	position Below $\hat{\vec{J}}^i$	and and same
Uno City.			(12) of I	Where the	
W	01824586	_,_5.1.6		क्तात्रात्रममस्याद्योषः	Anna Control of the C
-	111 .	. 576 #2	(88) 6K	FMPOUR	Ford Sylvey and House Street
w	01824587	, STG "2	1 11/11/2	animanianianis)	11, 20, 20, 20, 20, 20, 20, 20, 20, 20, 20
		# 2	( a ) 1	- m PETICK	sale seize and desire and desire and desired
	1824288	516#3	- Park	SIR THE PROPERTY.	
		516#5	Control of the second	Impace R.	
	0182 4589	516 2	1111 : 111	किया इत्या प्रस्ता	N. Licko
1 1		et p	( oK	Imperior	17)
-	0 1814590	516 \$ 5	- (39) OK	1 中国新铁路路	
		576#8	(88)01	TMPEZLER	
14	0 1824592	516.0			770
1	•	5T6#7	ok	Impacex	
	0 1824591			der street betreet betreet betreet	and the second s
		Have Boon R	P-d nex	Dua B497	83. (88)
11.	7 CAST RINGS	HAVE BEEN E	worker per	ं जारा निर्माण हो।	FAC 74/6/82
				, arms	
				4.1365种	
		· · · · · · · · · · · · · · · · · · ·	<u></u>	141011111111111111	A STATE OF THE STATE OF
***				१ - १ वर अस्तिम	
		1	<u> </u>	ः सन्पर्धाः	And Andrews
- 1				14:14:14:134148	
A				ः । स्राम्धाना	
	`			• ाः न्याञ्चलम् <u>य</u> ाः	
				राम इति सम्राम्भित	
				ांगुः वाग्यं मेलेसि	
1 1				ं लेगानारस्यान्त्रमानिवा	
# 1	,			THE CHEST SHIP	
		· 4-	-	11 1115 ATOM	
. 12.		<u> </u>		The second of th	
		· ·	· · · · · · · · · · · · · · · · · · ·	1040 11 - \$40 <b>1</b> 84	
-				. 19 - 19 1 - 19	Charles and the Control of the Contr
				्य १०५० व्यक्ति स्टब्स्	1 Property of the Parket of th
		1		0-3-58 31 CM	A CONTRACTOR OF THE PROPERTY O
				1 : skr.312a:3;	
				التورموق بموقي مدار	The state of the s
1		1		Hip-Market.	Charles of the last of the las
	504 0514 0 47740	HMENT   PAGE239		. १ र मुक्तिक	
HNF-2	504, REV. 0 ATTAC	HIVIENT I FAGE 337		्रस्था क्षा क्षेत्र । इस्त्राच्या क्षा क्षेत्र ।	And the second s
			DRIGINAL TO O	WHEN COMPLETED	

FEE	25,-26,-9	38 13:05 FROM:SI	BPI PDX CONTRACT	s ID	:5032265583	NCR No.	155599
FORM	' 561A-10				•		1 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7
Ref Prox	edure H	31.2	Note: All notations/	occumentation to be in	rblack ink,	Sheet/_	or <u></u>
	SCRIPTIC				ES ORDER NO.	WORK ORDE	
	丹宁丁 G NUMBER		1910839   PATTERNO.	LACATION	5145 (WARZ		4593
PER		PORT	NA	Rung As	· '		P.O. NO.
QTY ON ?	ORDER	OTY REJECTED	/ PART STATUS:	COMPL. INCOMPL.		ORDER LION-O	.C, ORDER
СОМРОН	ENT NO.	1910835	LAST OPER. COMPL.	(D) MATERIA	AL TRACE CODE NO.		
UNE	QTY	NOTE: FOR REJECT	ABLE CONDITIONS, RE E ACTUAL CONDITION	PORT THE REQUI	IRED .	GRID M	AP LOCATION 2 NO. NA
1	,	when TR	YING TO R	E Assemble	e ROTOR	Par 1	wlo-Assy
. 2		NOTED THAT	- (1) Shaft	NUT WO	. •	TIGHTEN	,
3	-	EMPELLER LI	KE DESIGNE	D: (# 19	10835 -	- DRAW)	NG #
4		A 39477)	ROTOR DIST	ASSEMBLED	- PARTS	THSPECT	ED 70
5		DRAWINGS -	They WERE	- TO PRIN	)T-		
6					• .		
7		Attention	1 EHG: K	DOED RIS	- h		
8							
9							
10		-			1 0		
REPORT	ED BY: rint Name)	Tan Crea	DATE: 1/21/0	APPROVED BY:	1 -tra	DAT.	22/80
	SIBILATY	ODE:	ERROR CODE:	(Quality Dept. One PART FAMIL		WORK CENTER	1000,00
FINE		TO CORRECT: USE AS I			Use as is Disposition n	equires Engineering j	ustification,
	0	- Marilan C		7	and Engineering Justi	fication for ASME iter	ns only.
	~~	MACHINE	DHAFT WILL	(A39477)	. INCRE	ASE DE	30114
	$\frac{U_{j}}{U_{j}}$	KEUER	00 10 -	11/25	·	wing U	IN BE
	_P\$t	NEC.		-			
<del></del>		· · · · · · · · · · · · · · · · · · ·	~ ~ .			•	
	For	- 5/N	E 777		,	<del></del>	
		<u> </u>	- · · · · · · · · · · · · · · · · · · ·				
		· · · · · · · · · · · · · · · · · · ·	•		<u></u>	·	
,				· .		<u> </u>	
מפות	SITION I	N. O	<del></del>	<del> </del>	DATE: 1		
	rint Name	$V \wedge V = V$	KISCH-	· · · · · · · · · · · · · · · · · · ·	1 /	22/98	•
•		Words Dage	APPROVAL an				
		SIGNATURE	ment shall check the required sign DATE	ratrus poxez pejow tot tedn		rcurrence) YURE	DATE
□Ма	anuf. Er	ngineer	1)	Specify Othe	er(s)		
<b>⊡</b> ₽€	sign Er	ngineer /	Kist 1221	<b>98</b> □ Other _			•
	ırchasin		/ - /	Other			
	ality De		22h;	Other _			
		x if 10CFR Part 21 is re	eportable		Reported by:		
	☐ Check box if Corrective Action is required (Significant or Reccurring Conditions) Approved by:						
NCR /	Action	Compl. (By Quality De	pt. Only) CLOSED BY:	Gar Ho	do.	DATE: /_	22-98
( H	INF-250	04, REV. 0 ATTACH	IMENT   PAGEDYO' A.S.	NT I WHEN COURS	c'en		<del>o klan</del>

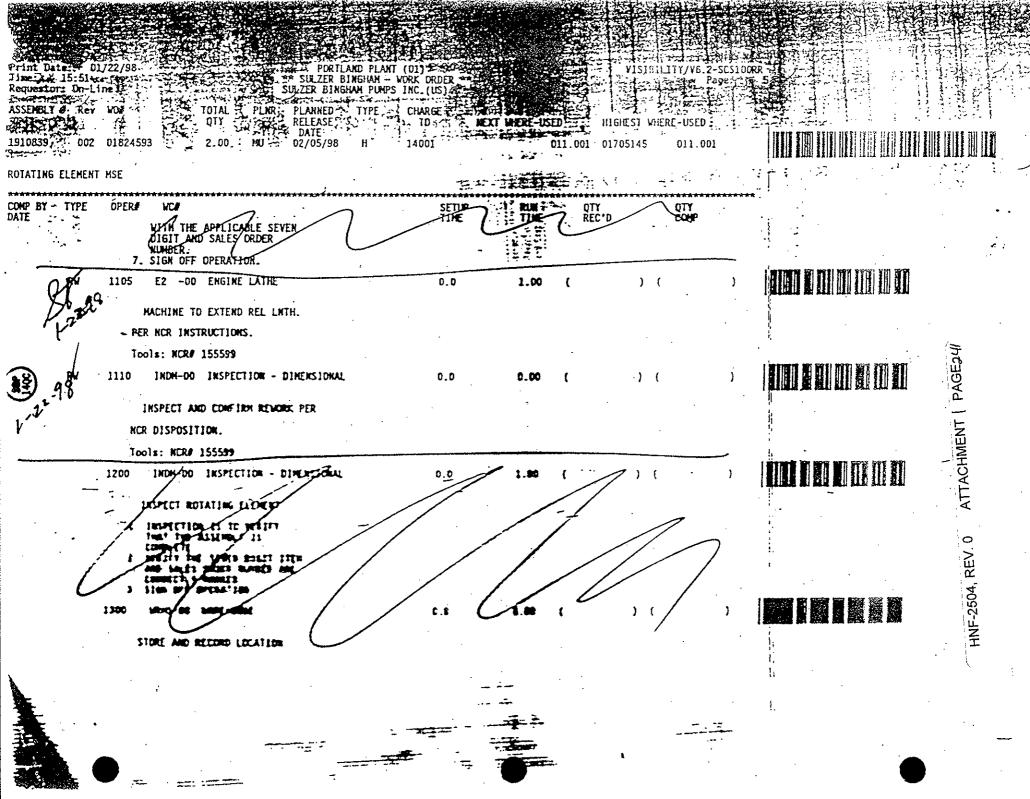



Sulzer Bingham Pumps Inc., 2800 N:W. Front Avenue, Portland, OR, U.S.A. 97210-1502

Between Bearings Business Unit Kevin Harold , Product Cell Manager 2800 N.W. Front Avenue Portland, OR 97210-1502 U.S.A. Tel. (503) 226-5354

Fluor Daniel Northwest Inc. 1100 Jadwin Ave Richland, Washington 99352 Fax (503) 226-5583

Attn.: Jack Henderson - Project Manager

Your reference: MZ4-APX-80708 Our reference: 1E776/777

Bob Kitchen - Purchasing

Date: February 18,1998

Subject: Transfer Pump Contract # DE-AC06-87RL10930 Purchase Order # MZ4-APX-80708 SBPI S/O # 1E776/777 Reply to Telephone Conference Call, February 6,1998

Dear Jack.

In response to the conference call meeting minutes dated February 6,1998, below is SBPI's responses to the questions asked.

1) Have SBPI explain the events of pump failure and their understanding of the mode failure.

Action Item: SBPI to provide a written failure report including closed out Non Conformance Reports and corrective action.

Anticipated Completion Date: See explanation below

The element picked up because the pump was provided with a non protected (not overlaid) surfaces on the hub side of the impellers. This design was not suitable for the abrasive nature of the product. A hub side wear ring was added and the wear rings overlaid with the same type of material as the eye side wear rings for abrasive service.

Copy of closed out NCR's 155766, 155767 & 15599 enclosed (mailed to Jack Henderson on January 28,1998)

2) Have SBPI explain the corrective action taken in detail.

Action Item: Explanation provided in topic 1

3) Have SBPI assure us that they have designed this pump to meet our specified requirements, specifically stating some of the design features and design verification methods use to assure that these requirement were met.

> HNF-2504, REV. 0 ATTACHMENT ! PAGEOUS



Date: February 18,1998

Action Item: SBPI to provide additional information on SBPI pump applications. In addition, they will certify that they designed and manufactured these pumps for the specified life and service.

Anticipated Completion Date: See explanation below

Sulzer Bingham Pumps certifies that we have designed the slurry transport pumps to meet the operability, performance and life requirements set forth in the pump specifications.

The pump selection due to the head and flow rate required a multistage pump (although the optimum pump for slurry services is a slow running single stage pump; this pump will not provide the necessary dynamic head required). A single volute pump design was selected to provide two advantages:

- 1) The volute passageway is larger than a double volute design for the same flow (thisprovides improved flow of particulates and reduces erosion by reducing turbulent flow at the side walls)
- 2) The volute cavities are more easily drained due to improved accessibility caused by not having a long cross under passage.

The metallurgy selection of duplex stainless is because this material provides the best combination of corrosion and erosion protection of common cast materials. This material is used almost entirely in the sea water injection pump services where the erosion / corrosion problems are severe due to high fluid velocities inside these high speed machines combined with corrosiveness of the saline water. Wear parts are overlayed with a cobalt hardfacing for increased erosion protection. [The hardness of the overlayed surfaces > HRC 58 (543 HB). Sophisticated materials which are sometimes utilized in the classic "slurry" services were not utilized due to the added complexity of the design and the increased risk of brittle materials. Sometimes the overall reliability of the pump is jeopardized by this added complexity.

4) Have SBPI explain that the discussion this past week regarding possible monthly rotation had to do with achieving the optimum pump life in light of the long storage period predicted and in no way indicated that the specified requirements can not be met without any maintenance.

This should be followed by a discussion of the possible periodic pump "bumping" with the pump full of water and both suction and discharge valves closed. This would achieve the optimum pump life while minimizing the ALARA concerns.

Action Item: SBPI to provide written procedure for both of these options including appropriate cautionary notes and advice.

Anticipated Completion Date: See attached instruction manual supplement

- 5) No action required of SBPI
- 6) Have SBPI describe how this pump would physically deal with a slurry as specified. For example, describe the pressure difference across the bushings and wear rings and the direction and volume of flow. Also discuss the wear characteristic of the different materials used in areas of the pump subject to either high velocity flow and the related erosion or high wear areas.

HNF-2504, REV. 0 ATTACHMENT | PAGE 243



Date: February 18,1998

**Action Item:** SBPI agreed to provide a summary of this discussion, correlating the technical requirements and the pump features.

Anticipated Completion Date See explanation below

Pump surfaces running in close proximity to one another are located at each side of the pump impellers, the center bushing and throttle bushing. It is at these surfaces where abrasion resistance is a design consideration. The other areas of the pump where the pumpage can cause wear to occur are described as high velocity areas.

SBPI has overlaid the wear surfaces, described above, with two hardness grades of Stellite. This provides a material combination that is resistant to abrasion due to particles in the pumpage, as well as the ability to tolerate contacting motion between the stationary and rotating components.

The other areas of concern for wear related mechanism resistance are "high velocity" areas of the pump. These are areas where the fluid velocity is greater than about 40 feet per second. The pump case and impeliers are cast from duplex stainless steel. This material provides excellent protection from both corrosion and erosion wear mechanisms.

See WP-681 (attached, 9 stages) with regards to the flow paths through the pump during operation and the principles relating to axial pump thrust and product lubricated bearing stiffness. The higher viscosity fluids provide for a higher bearing stiffness which is a benefit to the design.

The design life is based on a minimum of 10,000 hours as specified by the contract.

7) Have SBPI clearly identify their general inspection procedure for the MSE pump line and how it is designed to ensure that the equipment meets the design requirements.

Action Item: SBPI to check on the data package question raised by John Verderber.

Anticipated Completion Date: See explanation below

Item 4 Question Mark (?) Element Assembly Checklist for S/N 1E777

Impeller stack-up is O.K. for element assembly?

This check is to insure the impellers are assembled on the shaft to eliminate the vanes being in alignment with one another. This check is done to insure there is not a vane passing frequency problem (usually shows as a vibration problem on test). The mechanic who marked the paperwork with a "?" had a question with regards to the stack up. The test engineer inspected the element and determined there was not a problem. The unit was assembled and performance tested. The vibration readings were well within acceptable levels. The element assembly check list was not corrected to remove the "?" mark. On the warranty re-build element assembly check list item was checked off as acceptable.

HNF-2504, REV. 0 ATTACHMENT | PAGE 44)



Date: February 18,1998

8) Have SBPI explain the reason for the difference in the minimum speed stated in the SBPI instruction manual and the more recent response to VFD start up procedure that recommends 2500 rpm. Ultimately, whatever is decided should be in the instruction manual for future operators.

Action Item: SBPI will provide a written addenda to their instruction manual adding specific

information on starting the pump with a VFD.

Anticipated Completion Date: : See explanation below

The pump on startup should be brought up to 2500 rpm as quick as possible. After reaching 2500 rpm, the pump can be operated anywhere on the curve from 1200 rpm to 3600 rpm. Ramping up to 2500 rpm and reducing back to speeds below 2500 rpm is not required once the pump is running. SBPI will provide a supplement to the instruction manual noting this change in operations procedure.

9) Have SBPI discuss the reason why Flowserve (BW/IP Seals) decided to replace the mechanical seals.

Action Item: SBPI will provide revised mechanical seal drawing and a letter from the seal vendor explaining the reasons for the change, acknowledging that the new design is interchangeable with the old design and can operate with the same parameter.

Anticipated Completion Date: See attached letter from Flowserve dated 21 January 1998

Should you have any questions, please give me a call.

Best Regards,

Kévin Harold

Product Cell Manager


cc: Don Spencer

Tom Richfield - Field Service Bob McCain - L.A. Sales

> HNF-2504, REV. 0 ATTACHMENT | PAGE 24

Page Series 5.03 TECHNICAL DATA B12 14 February 1994

# SULZER BINGHAM TECHNICAL DATA - TYPE MSE FLOW DIAGRAM - SINGLE SUCTION

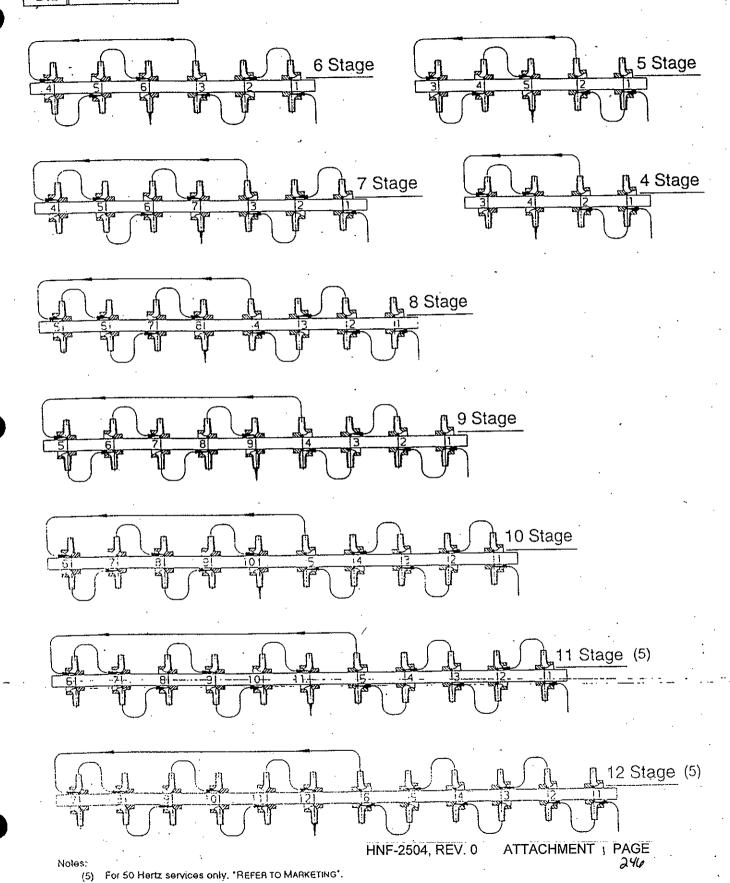



#### 1E776/1E777 INSTRUCTION MANUAL SUPPLEMENT

### RECOMMENDED PROCEDURE FOR 1E776/1E777 HANFORD TRANSFER HORIZONTAL MSE PUMPS

#### LONG TERM MAINTENANCE FOR INSTALLED PUMPS

### WARNING: Seals must have gas purge maintained at all times when pump is flooded.

This procedure outlines three (3) methods that can be used for pumps which may have long terms of inactivity between in operation:

<u>OPTION 1 FULL OPERATION</u> - (Frequency: 15-30 minute runs every month)

The purpose of this monthly run is to circulate the oil around the bearing housing to prevent corrosion of metal parts:

- 1) PARTIALLY CLOSE DISCHARGE VALVE
- 2) START NITROGEN PURGE TO SEAL
- 3) OPEN PUMP SUCTION VALVE
- 4) OPEN VENT VALVES, ENSURE PUMP IS COMPLETELY PRIMED
- 5) CLOSE VENT VALVES
- 6) START PUMP, BRING UP TO 2500 RPM (WITHIN 5 SECONDS)
- FULLY OPEN DISCHARGE VALVE AND ENSURE PUMP REACHES BEST EFFICIENCY FLOW AND DESIGN PRESSURE
- 8) OPERATE PUMP FOR 15-30 MINUTES

#### <u>OPTION 2 'BUMP' OPERATION</u> - (Frequency: Once every three (3) months or less)

Due to discharge system pipe work not being available/operational, an alternative is to 'bump' start pump (i.e. pump operates for approximately 15 seconds against fully closed discharge valve):

- 1) FULLY CLOSE DISCHARGE VALVE
- 2) START NITROGEN PURGE TO SEAL
- 3) OPEN PUMP SUCTION VALVE
- 4) OPEN VENT VALVES, ENSURE PUMP IS COMPLETELY PRIMED
- 5) CLOSE VENT VALVES
- 6) START PUMP, BRING UP TO 2500 RPM WITHIN 5 SECONDS
- 7) OPERATION AT 2500 RPM IS NOT TO EXCEED 10 SECONDS, (DUE TO TEMPERATURE INCREASE IN PUMPAGE) THEN STOP PUMP (COAST DOWN TIME IS ACCEPTABLE AND DESIRABLE)

TECHNICAL NOTE: The main concerns with infrequent operation is moisture in the bearing housing, which could cause corrosion. For this reason, SBPI selected a synthetic oil due to:

HNF-2504, REV. 0 ATTACHMENT ( PAGE 247)



#### 1E776/1E777 INSTRUCTION MANUAL SUPPLEMENT

### RECOMMENDED PROCEDURE FOR 1E776/1E777 HANFORD TRANSFER HORIZONTAL MSE PUMPS

#### LONG TERM MAINTENANCE FOR INSTALLED PUMPS

- Does not emulsify with water
- Synthetic corrosion inhibitors ironically bond to metal surfaces displacing water and other contamination's

Synthetic oil reduces operation time to every three (3) months, although every month would be even more desirable. Bump starting for 15 seconds (plus coast down time) will allow the oil rings to disperse synthetic oil throughout the bearing housing internals.

#### OPTION 3 REMOVE BEARINGS AND SEALS -

If the time between installation and pumping contaminants is long (>1 year) and pump is dry, bearing and seal removal from shaft should be considered:

Advantages:

- No maintenance (i.e., pump operation/turning not required)
- No risk of corrosion in bearing housing

#### The procedure is:

- 1) REMOVE COUPLING, BEARING HOUSINGS, COMPONENTS AND SEALS
- 2) COAT BEARING AND HOUSING SURFACES WITH RUST PREVENTATIVE (SHELL ENSIS FLUID NO. 210 OR EQUAL). ENCLOSE DESICCANT (BAGGED, NON-HALOGENATED, NON-DELIQUESCENT, CHEMICALLY INSERT SILICA GEL TO COMPLY WITH MIL-D-3464-D, TYPE 11). SEAL OFF WITH PROTECTIVE TARPAULIN
- 3) REMOVE SEALS. STORE SEALS IN ACCORDANCE WITH SEAL MANUFACTURERS INSTRUCTIONS.
- 4) PUMP ROTATING ELEMENT RESTS ON STATIONARY WEAR RINGS (NOTE DO NOT TURN SHAFT!)
- 5) BLANK OFF STUFFING BOX WITH WOODEN COVER AND WRAP WITH TARPAULIN TO PREVENT ENTRY OF FOREIGN MATERIAL
- 6) SEAL OFF EXPOSED SHAFTS WITH TARPAULIN

TECHNICAL NOTE: During rebuild/start-up a SBPI Field Services representative is recommended. It is also recommended, that if the storage period is excessive (>1 year), all elastomers (in seals) and bearings should be replaced prior to 'contaminated' start up.

REVISION NO. <u>0</u>

ATTACHMENT D

TEST EXCEPTION REPORT						
TEST PROCEDURE NO. & SECTION: HNF-1857	TEST NAME: POTP-007 INTE	GRATED TEST	T.E. NUMBER: TE-002			
DESCRIPTION OF PROBLEM:  Observed leakage from pump air seals.						
ORIGINATOR:		IMPACT ON TESTING: 🗆 HOL	LD FOR RESOLUTION X CONTINUE			
M. D. Gerken 02/02/98		M. D. Gerken	02/02/98			
ORG: DATE:		TEST ENGINEER	DATE			
Replaced flowserve model #982 sea flowrates per steps 1.8 and 1.9.  See Attached Uerdon			ıls. Rechecked pump air seal			
`						
DISPOSITION AND RETEST REQUIREMENT M. D. Gerken 02/03/98 DATE	'S BY:	DISPOSITION ACTION	S COMPLETE: 02/11/98 DATE			
QAE CONCURRENCE WITH DISPOSITION (	if required):	RETEST COMPLETE:  M. D. GERKEN  D. J.	02/11/98			



BW/IP International, Inc. Seal Division

BW Seets\*
Pacific Wietz\*
Flye Star

1305 Fraser Street Suite D8 Beilingham Washington 98226 Telephona 360 676 0702 Fax 360 676 1004

21 January, 1998

Sulzer Bingham Pumps - Portland, OR Plant

Attention:

Kevin Harold

CC:

Tim Wegener

Subject:

SULZER P.O.# 630234 / JOB# 96SEZ123726

Dear Mr. Harold:

The letter is to give notice of several issues regarding the Hanford Plant, Flowserve model 982 seals that are being retrofitted to incorporate the upgraded "Wavy Face" technology. Hanford discovered leakage problems with the job seals and contacted Flowserve (Tim Wegener) for input. Flowserve has agreed to, at Flowserve's expense, incorporate the newer "Wavy Face" technology to solve these performance issues. Flowserve will extend the warranty, upon receipt at the job-site, of the new retrofitted seals. The "Wavy Face" refers to the special "inverted wave" characteristic to the surface of the stationary seal faces. This technology has been utilized in the high performance compressor applications for eight years, and Flowserve is implementing this design into it's dry gas seal models (such as the 982 seal supplied). The seals faces are larger and require additional radial space. For this job we have engineered both inner / outer flanges, and sleeves (all to be made from the Hastalloy C). The only parts that could be reused are the springs. The status of this retrofit, that we are aggressively expediting, is for the heavy Hastalloy C components to arrive in Benicia, CA shop for complete assembly and testing on 1-31-98. The seals would, upon assembly and testing, immediately be air-freighted to Hanford,

The existing control panel settings and the seal installation procedures will remain to original specifications. Flowserve will provide complete seal assembly prints for distribution.


Should you have any questions or require additional information, please do not hesitate to contact us.


Sincerely,

Danny Trice - District Manager

Tim Wegener - Sales Engineer

Marc Hagn - Applications Engineer



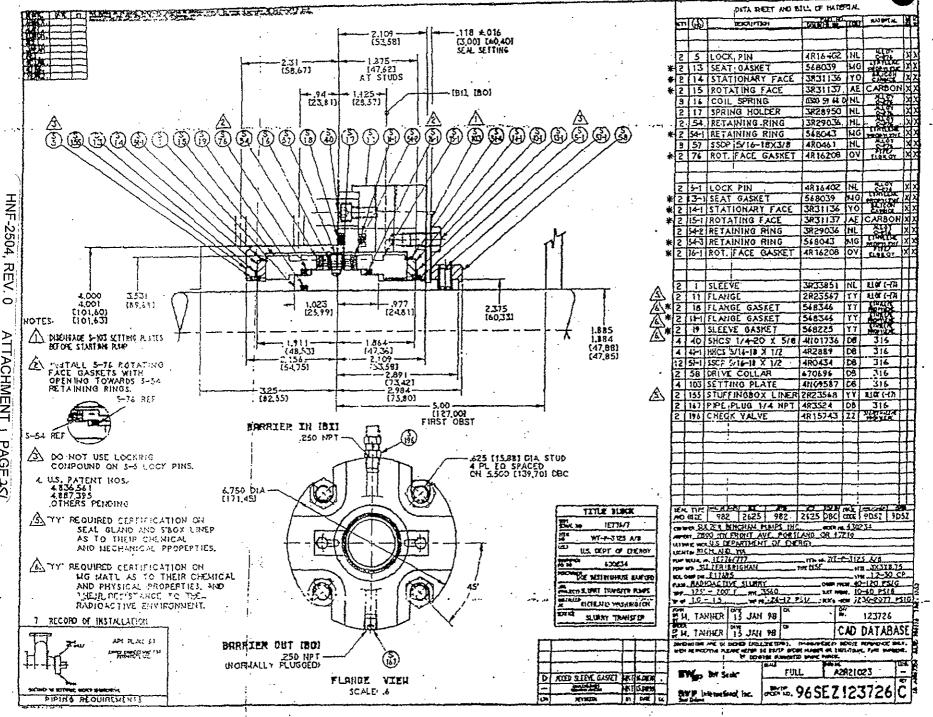

REV.

0

ATTACHMENT

PAGE

3

#### PREOPERATIONAL TESTING POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST PAGE 1 OF 1 HNF-1857

REVISION NO. 0 ATTACHMENT D

TEST EXCEPTION REPORT						
TEST PROCEDURE NO. & SECTION:	TEST NAME:		T.E. NUMBER:			
HNF-1857, 8.27	POTP-007 INTE	GRATED TEST	TE-003			
,						
DESCRIPTION OF PROBLEM: When B pump was and discharge valves) on the A pum	as started, pressu	ire sensors (located	between the A pump closed inlet			
from the B pump discharge to the A vent valve (MOV-3125AK).	pump loop. The p	roblem was identified	d as a leak through the A pump			
ORIGINATOR:		IMPACT ON TESTING: X HOLI	FOR RESOLUTION  CONTINUE			
J. E. Dunks 02/17/98		J. E. Dunks	02/18/98			
ORG: DATE:		TEST ENGINEER	DATE			
DISPOSITION:						
Replace MOV-3125AK valve resume testing (concurrence)	body with valve b by Jim Collins FD	ody from first stage NW Lead Engineer)	drain valve (MOV-3125AJ) and			
2. Procure a direct replacement	valve body and i	nstall it in the MOV-3	125AJ position.			
Verify that this rework meets test.	original pressure	testing requirements	by performing a in service leak			
		,				
			,			
			·			
		•				
DISPOSITION AND RETEST REQUIREMENT J. E. Dunks 02/18/98	rs by:	DISPOSITION ACTION	s complete:			
DATE		1	DATE			
QAE CONCURRENCE WITH DISPOSITION (	(if required):	RETEST COMPLETE:	0			
Day R. Hall 2/1	8/98	Doug Such TEST ENGINEER	2/19/98 DATE			
) DAIL		1591 ENGINEER	DAIE			

# PREOPERATIONAL TESTING POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 1 OF 1

REVISION NO. 0

ATTACHMENT D

TEST EXCEPTION REPORT						
TEST PROCEDURE NO. & SECTION:	TEST NAME:		T.E. NUMBER:			
HNF-1857,	POTP-007 INTE	GRATED TEST	TE-004			
DESCRIPTION OF PROBLEM: The B-pump VSD goes into either overcurrent or overvoltage fault which causes the speed drive to shut down. This happens intermittently when the VSD is given a remote speed change from PCU-2.						
ORIGINATOR:		IMPACT ON TESTING: 🗖 HOLI	D FOR RESOLUTION X CONTINUE			
M. D. Gerken 02/18/98		M. D. Gerken	02/18/98			
ORG: DATE:		TEST ENGINEER	DATE			
DISPOSITION: VSD vendor to troubleshood drive to go into fault and shutdown.	t and repair. Rete	est to verify remote s	peed changes do not cause the			
Vendor found drive in no motor test r	mode which cause	ed the overcurrent/ov	vervoltage problems.			
See attached Vendor report.						
, •						
	,					
DISPOSITION AND RETEST REQUIREMENT M. D. Gerken 02/19/98 DATE	S BY:	DISPOSITION ACTIONS  Verified As J	S COMPLETE:  02/20/98  DATE			
QAE CONCURRENCE WITH DISPOSITION (I	if required): 2/30/98	RETEST COMPLETE:  M. D. Gerken  D. TEST ENGINEER	02/20/98 DATE			

E:T.N

Cutier-Hammer & Westinghouse Products
5000 Meadows Road, Suite 300
Lake Orwego, Or. 97035

PHONEN 503-616-636-8333 FAX 8 503-624-604 636-8545 ADMET 8 AS67-4016

## Fax Cover Sheet

DATE: 3 26 98

TIME:

TO: JACK HENDERSON

PHONE: 509-376-9871

FAX:

509-373-0122

FROM: Scott MacLean

RE: ALL JOO

Number of pages including cover sheet: 5

Message

Fax#

HERE IS A COPY OF A ROUGH REPORT

THAT COUERS PROGRESS TO DATE. I EXPERT TO

RETURN NEXT WEEK TO CONTINUE ON UNIT "A".

Post-It Fax Note 7671 Date pages. 5

To E. PACIQUET From J. Lutt.

Co./Dept. Co.

Phone # Phone #

Fax #


	t No.	Qty.	Chrg.	War.	Price		1
						•	
						··· <del>·········</del>	1
							†
<del></del>				<del> </del>			4
						<del> </del>	4
		,					4
							_
<del></del>						•	
			1				7
	· · · · · · · · · · · · · · · · · · ·				<del></del>		
							-
		•		Total	L		4 .
ed Problem:	UNIT S	URGING	AND 7	RIPPIN	6 av 0	UERLOAI	ANS
	OUER YOU	TAGE A	FAULTS		,		
•			<del></del>				
						. ما در بران زناک در در در در در	
• •							
					4 -0 10		
tive Action: ,	APRIVET	AT SIGH	T AND	RAN	- B VK	COCH	STATE
1	THAT UN	T APPE	3120 7	O HUR	T FOR	0000	261 000 TT
•	POJNT P	and wo	alv F	- PAN	DO WEY	FOR	" MOTO
·	FOUND 7	HAT UND	CHOWA.	Not 6	BE RUM	1 TN	MATON
	7757	UKIT -	>1700,CL	COUL	VENTO	DRTU	5. RAW
	TEST V	UZIA A	17010/2	1000	<u> </u>		OFFE
	1105,95.	ETTO OF	ロロットロム	MEAL	FOR KING	emal i	יו דעייעט דעני
,	DETUE A	RETER RE	PROGRA	MING	FOR NO	UT EX	TENDEN
	AND OF	BSERVED	OUE	2 VOLTA	FOR Alon GE FIGU	UT EX	TENDEL
	DECEL ,	BSERVED RAHP TI	OUTH ME F	ROM S	FOR Alo. UE FIGU UO TO E	UT EX SO SECU	TENDEL
	DECEL OF	BSERVED RAHP TI WP REG VOLTAG	OVEL ME FI ENERA E P	EVOLTA DOM S TION F 730YU	FOR NO. GE FIGURE  DO TO E  DOM M	UT EX 50 SECU 510R WE VU	TENDEN XDS MEASU XTAGE
	AND OF DECEL TO ST DC BUS TS AT	BSERVED RAMP TI TOP REY VOLTAG 493 OF	OVER ME FI EVERA E P U AB 1	EVOLTA DOM & TION F 730YU FAC A	FOR Allow UP TO E ROM M C. LI WD 489	UT EX GO SECU GIOR WE YU I ON BU	TENDEN XDS MEASUN XTAGE LHTY
	AND DECEL OF TO ST DC BUS FS AT BUS VOL	BSERVED RAMP TI WP REG VOLTAG 493 OF TAGE IS	OVER ME F ENERA LE P U AB I	EVOLTA  DOM S  TION A  730 Y L  AC A  ODUCT C	FOR NO.  GE FIGURE  POM M  C LI  WD 489	UT EX 50 SECU OTOR WE VU TUH O	TENDEN XDS. MEASUN XTAGE L. HTG AC LTI
	AND DECEL OF TO ST DC BUS FS AT BUS VOL	BSERVED RAHP TI WP REG VOLTAG	OVER ME F ENERA LE P U AB I	EVOLTA  DOM S  TION A  730 Y L  AC A  ODUCT C	FOR NO.  GE FIGURE  POM M  C LI  WD 489	UT EX 50 SECU OTOR WE VU TUH O	TENDEN XDS. MEASUN XTAGE L. HTG AC LTI
	AND DECEL OF TO ST DC BUS FS AT BUS VOL	BSERVED RAMP TI WP REG VOLTAG 493 OF TAGE IS	OVER ME F ENERA LE P U AB I	EVOLTA  DOM S  TION A  730 Y L  AC A  ODUCT C	FOR NO.  GE FIGURE  POM M  C LI  WD 489	UT EX 50 SECU OTOR WE VU TUH O	TENDEN XDS. MEASUN XTAGE L. HTG AC LTI
	AND OF DECEL OF TO ST DC BUS TS AT BUS YOU AND TH	BSERVED RAMP TI WP REG VOLTAG 493 OF TAGE IS	OVER ME F ENERA LE P U AB I	EVOLTA  DOM S  TION A  730 Y L  AC A  ODUCT C	FOR NO.  GE FIGURE  POM M  C LI  WD 489	ICT EX SO SECU SOTOR VO WE VO WE VO DN BO TIGH OF	TENDEN XDS. MEASUN XTAGE L. HTG AC LTI
	AND DECEL OF TO ST DC BUS FS AT BUS VOL	BSERVED RAMP TI WP REG VOLTAG 493 OF TAGE IS	OVER ME F ENERA LE P U AB I	EVOLTA  DOM S  TION A  730 Y L  AC A  ODUCT C	FOR Allow  GE FIGURE  FORM M  C LI  WAS 489  FRONT E	ICT EX SO SECU SOTOR VO WE VO WE VO DN BO TIGH OF	TENDEN XDS. MEASUN XTAGE L. HTG AC LTI

Page	SERVICE REPORT CONTINUATION
Customer: PRO / G.O. #	Date: 3/23  Generic Name: ALC 700
Corrective Action Contin	ETAPPENS OF ISOLATION/STEP DOWN TRANSPORTED ETO 480 VAC OR AS CLOSES AS POSSIBLE.
·	FOUND THAT DC BUS VOLTAGE IS AT
605 VDC. 7	POUBLESHOOTING, SHOWS THAT ALL SCR'S ARE CTEST) INPUT TRANSFORMER YOUTHGES ARE GLOD
FOUND THAT REDDINGS.	3 SER'S HAD LOWER GATE/CATHODE RESIGN
SURGES P EXPLAINS I BELTEUE CHANGE OF THAT CH PARAMETER TO IMPLE	WHY VPD "B" WOULD HAVE CUPRENT LEASE SEE ATTACHED SHEET WHICH MOTOR TEST PROGRAMMONG AND OPERATED THAT OPERATORS / ELECTRICIANS WOULD GRAMETER DISPLAY AND BELIEVE ANGE WAS IMPLEMENTED. AFTER CHANGEN OR "MOTOR TEST" YOU NEED TO CYCLE POWER HENT CHANGE. THIS IS TO ENABLE OR DIS PARAMETER.

### D. TEST PROCEDURE

10. Lift the bus end of the 400A fuse away from the bus and insulate it momentarily from the bus with a thin piece of insulation or paper. If it is a multiple inverter system, insulate the fuse bypass diode assembly from the bus as well.

Close the main breaker and allow the drive to start up into its "drive ready" condition. Don't forget, this will put full do on the main do bus, so normal caution must still be observed. There should not be any red LEDs illuminated on the daughter boards. Check with a co voltmeter that each gate lead has approximately -5V between the top two pins of each gate plug. Check that the plugs are firmly seated and that no wires have come adrift.

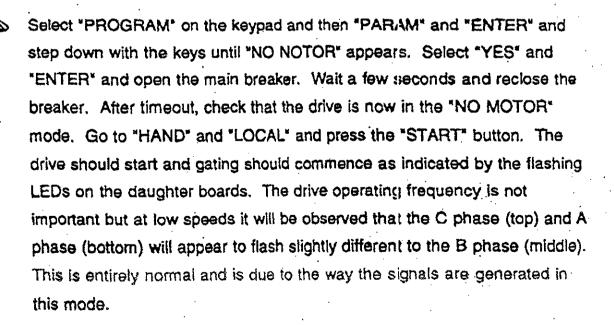

11. If all appears correct, proceed as follows. Press the "STOP" button and open the breaker. Allow enough time to discharge the dc link. If the motor can be disconnected easily, do so; if it cannot, disconnect the three leads connecting the inverter to the reactor in the bottom of the unit. Spread the

output connections and isolate them from ground. If there are multiple inverters disconnect them all from their associated reactors, ensuring that they cannot touch each other. Reconnect the 400A fuse for the inverter, together with its bypass diode, if a multiple system. Close the breaker, watch the dc come up, and start the drive. With an ac voltmeter check that the voltages across the three output terminals are balanced.

Switch off the drive and reconnect the next inverter (if fitted). Restart and check the ac voltages between similar output terminals of the two inverters. There should be very little difference (typically less than 1V ac).

Repeat with each inverter in turn until all are running.

Open the breaker and reconnect the output leads of the inverters to their respective reactors. Reconnect the motor if it was disconnected. Select bottom frequency, close the breaker and restart, observing the motor current. If all is OK, stop the drive select "NO MOTOR" and "OFF," reset the breaker and restart the drive.

# PREOPERATIONAL TESTING POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 1 OF 1

REVISION NO. \_0\_

ATTACHMENT D

TEST EXCEPTION REPORT						
TEST PROCEDURE NO. & SECTION: TEST N	NAME:		T.E. NUMBER:			
HNF-1857, POT	P-007 INTE	GRATED TEST	TE-005			
DESCRIPTION OF PROBLEM: Both the A and B-pumps exibit high vibration at certain RPM. The vibration on the A-pump exceeds the high vibration setpoint which causes the pump to automatically shutdown. Typically A pump exceeds .60 IPS at approximately 3,000 RPM and B pump exceeds .30 IPS at approximately 2,950 RPM.						
ORIGINATOR:		IMPACT ON TESTING:   HOLI	D FOR RESOLUTION X CONTINUE			
M. D. Gerken 02/19/98		M. D. Gerken	02/19/98			
ORG: DATE:		TEST ENGINEER	DATE			
DISPOSITION: Pump vendor to troubleshoot and repair. Retest to verify vibration is within acceptable tolerance.  THIS TEST EXCEPTION WILL BE: CLOSED AND THIS ITEM WILL  BE CARRIED AS AN EXCEPTION TO THE W-058 OAC PART II  ( REFERENCE S-FACILITY TESTING-EXCEPTION I) AND CONSIDERED  A PUMP WARRANTY ITEM.  SEE ATTRCHED UCHPOR REPORT						
DISPOSITION AND RETEST REQUIREMENTS BY: M. D. Gerken 02/20/98 DATE		DISPOSITION ACTIONS  Verified A. Raw	DATE			
QAE CONCURRENCE WITH DISPOSITION (if required to the property of the property	red): <u>3</u>	RETEST COMPLETE:	IL D.S. 4/1/98			
		1231 ENGINEER	DATE			

MAR 10 '98 11:29 FROM: SULZER BINGHAM T-002 P.01 F-847 SULZER BINGHAM PUMPS INC. 503 ASME CODE SULZER BINGHAM PUMPS INC. DOCUMENT SECTION " N/A E12.5.546 CLASS NO. CODE EDITION 12776 / 777: VIBRATION DIAGNOSIS (YEAR) ADDENDA 7671 SEASON ACK-Herderson YEAR 376. CUSTOMER FLUOR DANIEL HANFORD / D.O.E. PROJECT Slurry transfer pump OMER P.O. NO. CHANGE ORDER NO. Specification no. PEVINON NO. 0 CUSTOMER APPROVAL REQUIREMENT CUSTOMER APPROVAL NUMBER ☐ YES □ NO **E** INFORMATION ONLY CERTIFIED AS A VALID SULZER BINGHAM FUMPS INC. DOCUMENT SPACE FOR CUSTOMER APPROVAL STAMP (when applicable/available) For Outside Vendor ☐ Rick Ralesse Inspection Report # ☐ For Manufacture at Other (specify) Suber Bingham Pumps Inc. INITIAL APPROVAL'S (SIGNATURE) Date \$110198 Engry Assurance HNF-2504, REV. 0 ATTACHMENT | PAGE 2000 Quality Assurance Originating HEADQUARTERS CERTIFICATION (when applicable) ENGINEERING This Document is certified to be in compliance Dept. Marino Chiza with the applicable purchase order. Thomas F. Kaiser SPECIFICATIONS, PROCEDURES, AND ADDITIONAL REQUIREMENTS LISTED IN **DESIGN ANALYST** THE APPENDICES Title: Initial 03/69/1998 Date: N/A Professional Engineer APPLICABLE S.O. NUMBERS 12776/777 WP-98001 Registration No. State

Control

Order Number

Rev.

T-002 P.02 F-847

#### CONTENTS

- 1. Introduction
- 2. Vibration readings taken on A-pump (1E776)
- 3. Vibration readings taken on B-pump (1E777)
- 4. Modal testing
- 5. Lateral critical speed analysis
- 6. Other potential excitation sources
- 7. Conclusions

### ENCLOSURES

A-PUMP (1E776)

Enclosure 1: Horizontal 1x vibrations (POH, PIH, MIH 1.) at various operating speeds Horizontal overall vibrations (POH, PIH, MIH 1.) at various op. Speeds Enclosure 2: Enclosure 3: Vertical 1x vibrations (POV, PIV, MIV 1.) at various operating speeds Vertical overall vibrations (POV, PIV, MIV 1.) at various op. Speeds Enclosure 4: Enclosure 5: Vibration amplitude spectra taken at pump bearing housings (2910 RPM)

Enclosure 6: Vibration amplitude spectra and time waveform readings taken at

motor inboard bearing housings (2910 RPM)

Impact test results (pump inboard bearing housing) Enclosure 7: Impact test results (pump outboard bearing housing) Enclosure 8:

#### B-PUMP (1E777)

Enclosure 9: Impact test results (pump inboard bearing housing) Enclosure 10: Impact test results (pump outboard bearing housing)

#### **BOTH PUMPS**

Enclosure 11: Mechanical finite element model of pump rotor Enclosure 12: Results of non-linear static analysis (3560 RPM)

Enclosure 13: Lateral damped critical speed analysis: Campbell diagram Enclosure 14: Lateral damped critical speed analysis: 1st bending mode

1.) POH:	Pump Outboard Horizonta	ì
POV:	Pump Outboard Vertical	
mu.	Thims Inhand Marisantil	

PIV: Pump Inboard Vertical MIH: Motor Inboard Horizontal MIV: Motor Inboard Vertical

ATTACHMENT | PAGE 261 HNF-2504, REV. 0

T-002 P.03 F-647.

#### 1. INTRODUCTION:

A root cause analysis was done for the 1E776 / 777 pumps in order to determine the source of the high vibration levels experienced when testing these units at DOE's HANFORD site. SBPI's analysis work included taking vibration readings a various locations and operating speeds, modal testing (impact tests) of the bearing housings and some up front analysis.

### 2. VIBRATION READINGS TAKEN AT A-PUMP (1E776)

Vibration readings were taken at various locations within an operating speed range of 2600 RPM to 3600 RPM. With each new operating point investigated, the system was given enough time to stabilize before taking readings. All operating conditions were close to or at Best Efficiency Point (BEP).

Throughout the vibration spectra obtained, synchronous speed (1x) is the only frequency were significant vibration levels occur. In the horizontal plane vibrations peak at 2950 RPM, in the vertical plane they peak at maximum speed (see Enclosures 1 to 6).

## Synchronous vibration readings taken on the motor inboard bearing housing in horizontal and vertical direction indicate a motor airgap problem.

In case of high 1x vibrations caused by mechanical and / or hydraulic unbalance, simultaneous readings in two directions perpendicular to each other will show a 90° phase difference due to the fact that the force is rotating (with 1x). In case of an airgap problem, simultaneous vibration readings will be in phase, because the airgap excitation force is stationary.

The readings taken on the motor inboard bearing housing are perfectly in phase, as typical for an airgap problem (see Enclosure 6).

The vibration levels measured on the motor are very high for this type of equipment (WESTINGHOUSE TECO, frame 5009A, 300 HP). At 2950 RPM the horizontal 1x vibration levels at the motor inboard bearing housing is 0.31 ips. The motor pedestal 1x displacement is approximately 1 mil peak-peak at this operating point.

Modal testing of the pump bearing housings indicate resonance situations at 49 Hz in the horizontal plane (PIH, POH) and at 61 Hz in the vertical plane (see section 4). These resonance situations are likely to increase vibration amplitudes. However, the root cause seems to be the high excitation induced by the motor.

Recent finite element analyses on a similar design indicate that natural frequencies in the 1x cannot be excited by normal pump operation. But it is likely that high excitation forces acting on the casing / pedestals are capable of exciting those modes.

## 3. VIBRATION READINGS TAKEN AT B-PUMP (1E777)

The B-pump experienced lower vibration levels than the A-pump. Only one set of vibration readings was obtained. The horizontal 1x vibrations at the outboard bearing housing at 2900 RPM were 0.20 ips (0.47 ips at the A-pump and same operating conditions).

HNF-2504 REV 0 ATTACHMENT | PAGE 202

T-002 P.04/19 F-647

#### 4. MODAL TESTING

The bearing housings of both pumps were impact tested in order to determine structural natural frequencies. The tables below as well as Enclosures 7 to 10 show the results of these tests.

Natural Sequency	A-PUMP, PIH	A-PUMP, PIV	A-PUMP, POH	APUMP, POV	B-PUMP, PIH	B-PUMP, PIV	B-PUMP, POH	B-PUMP, POV
12	48.88	-	48.95	61.24	48.88	61.37	48.88	61.3
284	106.68	96.21	108.69	96.29	108.66	96,33	106.34	98.6
3rd	451.23	286,26	433.78	288,76	441.33	286,26	438.77	278.7
4 4	628.77	453.73	511.30	451.27	633,77	438.80	568.72	443.7
58	688.69	516.23	651.28	508.77	706.22	528.77	668.78	
- <del>The state of th</del>	Eccionure 7	Baciosure 7	Eccionire 2	Enclosure 8	Racionere 9	Encions v 9	Enclosure 10	NA

The impact tests indicate that both units are almost identical with respect to bearing housing structural natural frequencies.

Impact test on the pump pedestals show natural frequencies in the 600 Hz range only.

### 5. LATERAL CRITICAL SPEED ANALYSIS

Prior to doing vibration analysis in the field, a damped lateral roton synamic analysis has been performed. The analysis indicates that no critical speeds occur within the investigated operating speed range. The first bending mode is well separated from synchronous speed and sufficiently damped.

The analysis indicates that the pump has design integrity with respect to lateral rotordynamic behaviour.

#### 6. OTHER POTENTIAL EXCITATION SOURCES

The 'problem' frequency do not coincide with any of the know bearing frequencies;

EXCITATION FREQUENCY	SKF 7309 thrust bearing	SKF 6309 radial bearing
BPFO (ball pass freq. of the outer race)	80.3*RPM/1000	50.6*RPM/1000
BPFI (ball pass freq. of the inner race)	120.0*RPM/1000	82.7*RPM/1000
FIF (fundamental train frequency)	6,69*RPM/1000	6.32*RPM/1000
BSF (ball spin frequency)	33,3*RFM/1000	32.6*RPM/1000

 Long cross-over acoustic resonance takes place at vane passing frequency and not at lx.

T-002 P.05/19 F-847

#### 7. CONCLUSIONS

The data collected indicates a motor sirgap problem. It is recommended to have the motor supplier inspect its equipment (both units) and correct the problem. The sirgap problem may originate from misalignment between the motor rotor and stator.

Summary:

1. Both units (A-pump and B-pump) are identical in design but show different bearing housing vibrations levels. This indicates that different levels of excitation forces are acting on the pumps.

2. The motor inboard bearing housing vibration levels as well us the motor pedestal

vibration levels are high.

3. Simultaneous vibration readings on the motor inboard bearing housing in vertical and horizontal direction are *in phase*, which points to a stationary excitation force (such as motor airgap excitation) to cause the high structural vibrations.


4. Pump induced vibrations at 1x synchronous speed (with no considerable 0.5x or 2x frequency components) are caused by unbalance (hydraulic and / or mechanical) or rotor bow. Both phenomenon represent rotating excitation forces which will result in a 90° phase difference between simultaneous readings in two directions perpendicular to each other.

5. It is unlikely that a 3x3x8.75 MSE pump will force a motor to vibrate at 0.3 ips

levels.


T-002 P.06/19 F-647

Enclosure 1

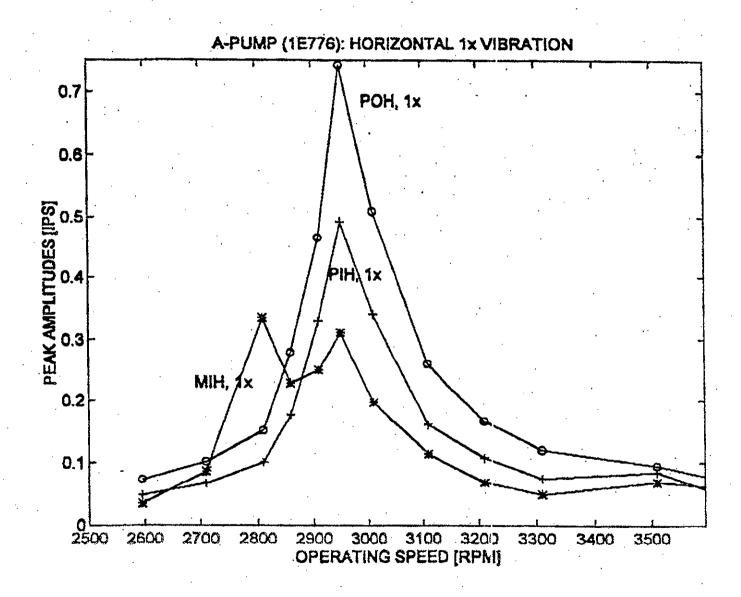

T-002 P.07/19 F-647


## Enclosure 2

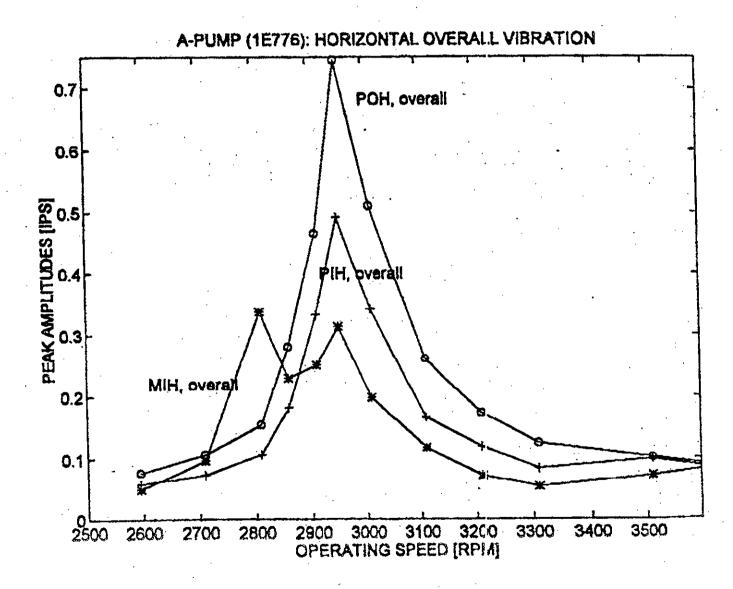

HNF-2504, REV. 0 ATTACHMENT | PAGE 200


T-002 P.08/19 F-647

Enciosure 3

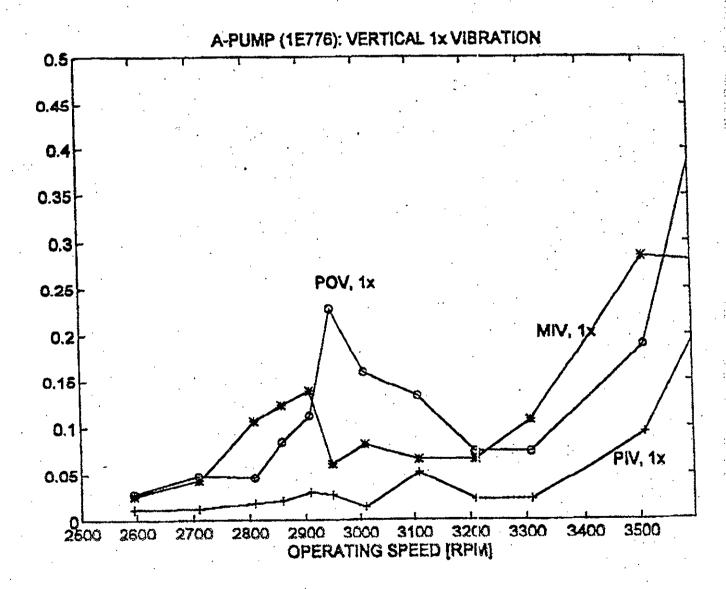

T-002 P.09/19 F-847

## Enclosure 4

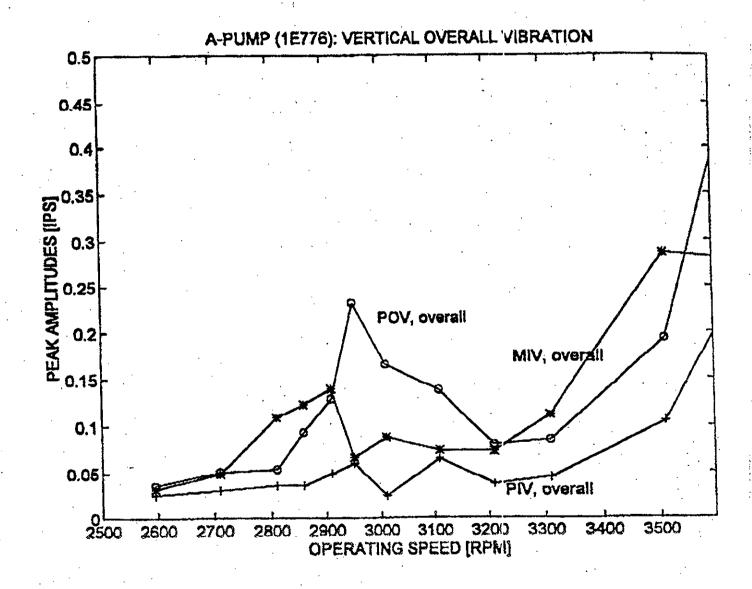


T-002 P.10/19 F-647

## A-PUMP (1E776): VIBRATION AMPLITUDE SPECTRA TAKEN AT PUMP BEARING HOUSINGS UNIT OPERATING AT 2910 RPM

Enclosure 5

#### from top to bottom:

- Pump inboard bearing housing, vertical direction (PIV)
- · Pump inboard bearing housing, horizontal direction (PIH)
- Pump outboard bearing housing, vertical direction (POV)
- Pump outboard bearing housing, horizontal direction (POH)

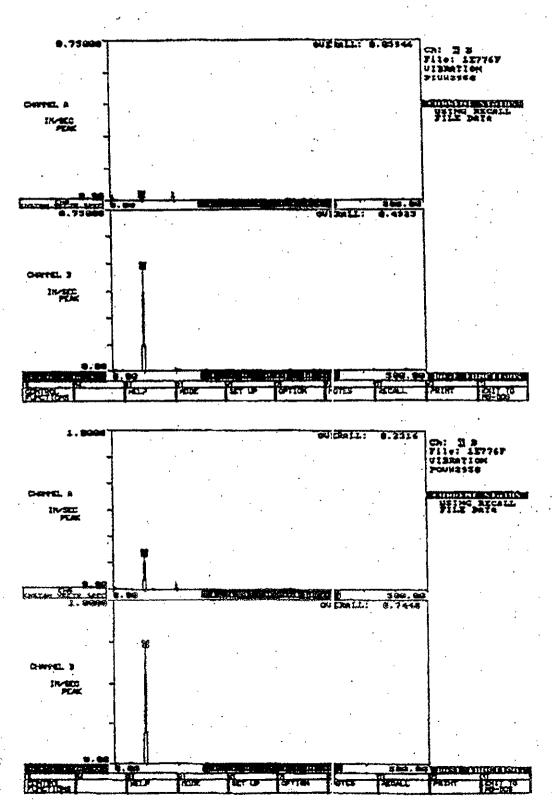

HNF-2504, REV. 0

ATTACHMENT | PAGERA


T-002 P.11/19 F-647


A-PUMP (1E776): VIBRATION AMPLITUDE SPECTRA AND TIME WAVEFORMS TAKEN AT MOTOR INBOARD BEARING HOUSING UNIT OPERATING AT 2910 RPM

Enclosure 6

from top to bottom:

- Motor inboard bearing housing, vertical direction (MIV)
- Motor inboard bearing housing, horizontal direction (MIH):
- Motor inboard bearing housing, vertical direction (MIV)
- Motor inboard bearing housing, horizontal direction (MIH)

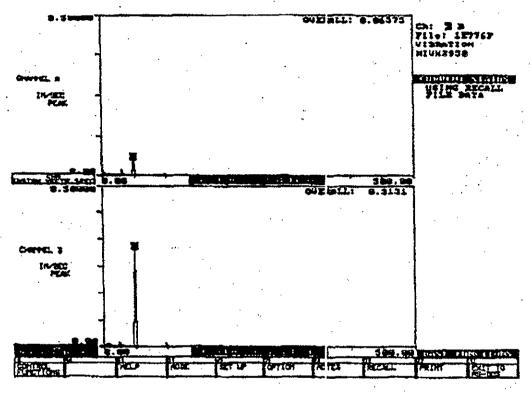

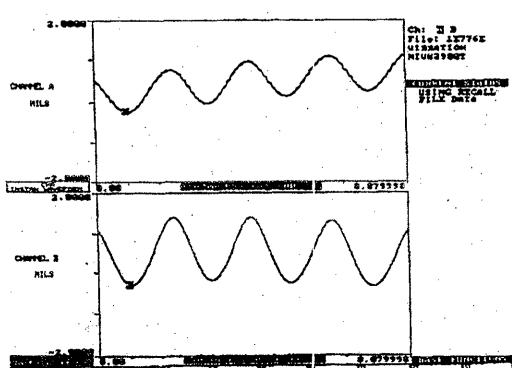

HNF-2504, REV. 0


ATTACHMENT | PAGE 270


T-002 P.12/13 F-647

### Enclosure 7

## A-PUMP (1E776): MODAL TESTING OF PUMP INBOARD BEARING HOUSING

- top: Pump inboard bearing housing, horizontal direction
   bottom: Pump inboard bearing housing, vertical direction

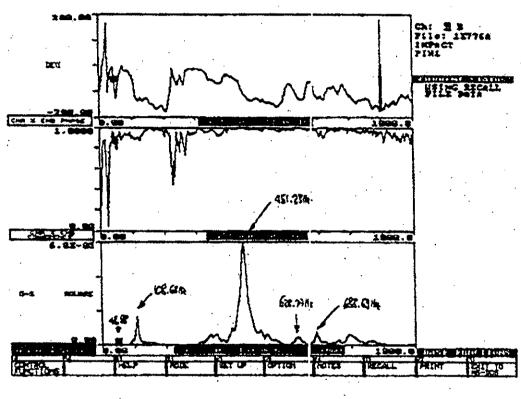

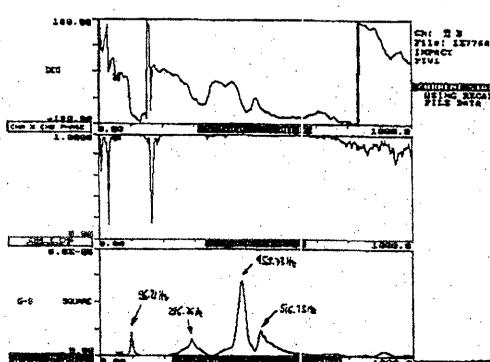

HNF-2504, REV. 0


ATTACHMENT | PAGE 271

T-002 P.13/19 F-647

## A-PUMP (1E776): MODAL TESTING OF PUMP OUTBOARD BEARING HOUSING

- top: Pump outboard bearing housing, horizontal direction
- bottom: Pump outboard bearing housing, vertical direction

Enclosure 8

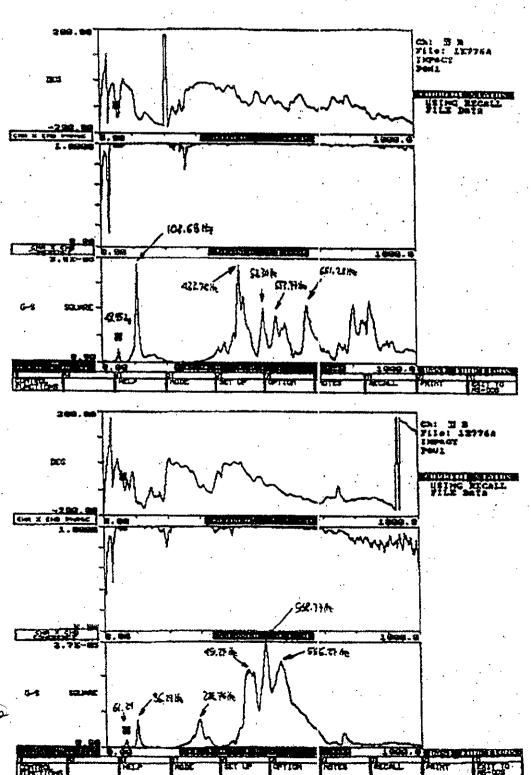

HNF-2504, REV. 0


ATTACHMENT I PAGE 272

T-002 P.14/19 F-647

B-PUMP (1E776): MODAL TESTING OF PUMP INBOARD BEARING HOUSING

- top: Pump inheard bearing housing, horizontal direction
- bottom: Pump inboard bearing housing, vertical direction

Enclosure 9

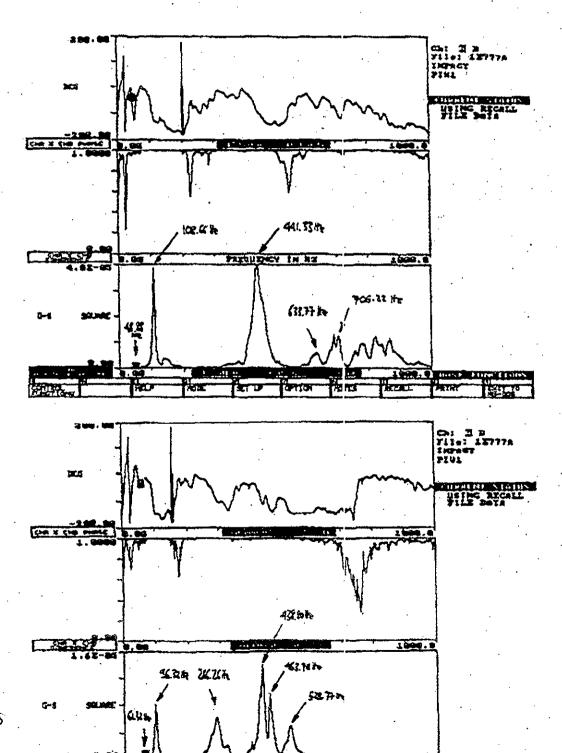


HNF-2504, REV. 0

ATTACHMENT | PAGE 213


T-002 P.15/19 F-647

B-PUMP (1E776): MODAL TESTING OF PUMP OUTBOARD BEARING HOUSING top: Pump outboard bearing housing, borizontal direction

Enclosure 10

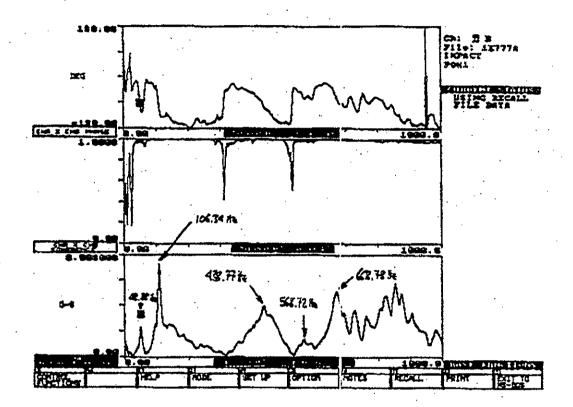


T-002 P.16/19 F-647

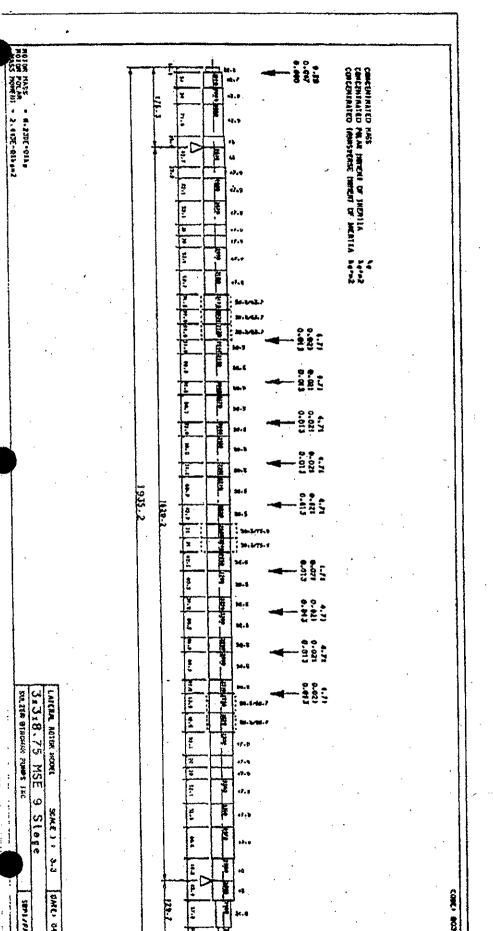

Enclosure 11


HNF-2504, REV. 0 ATTACHMENT | PAGE 22

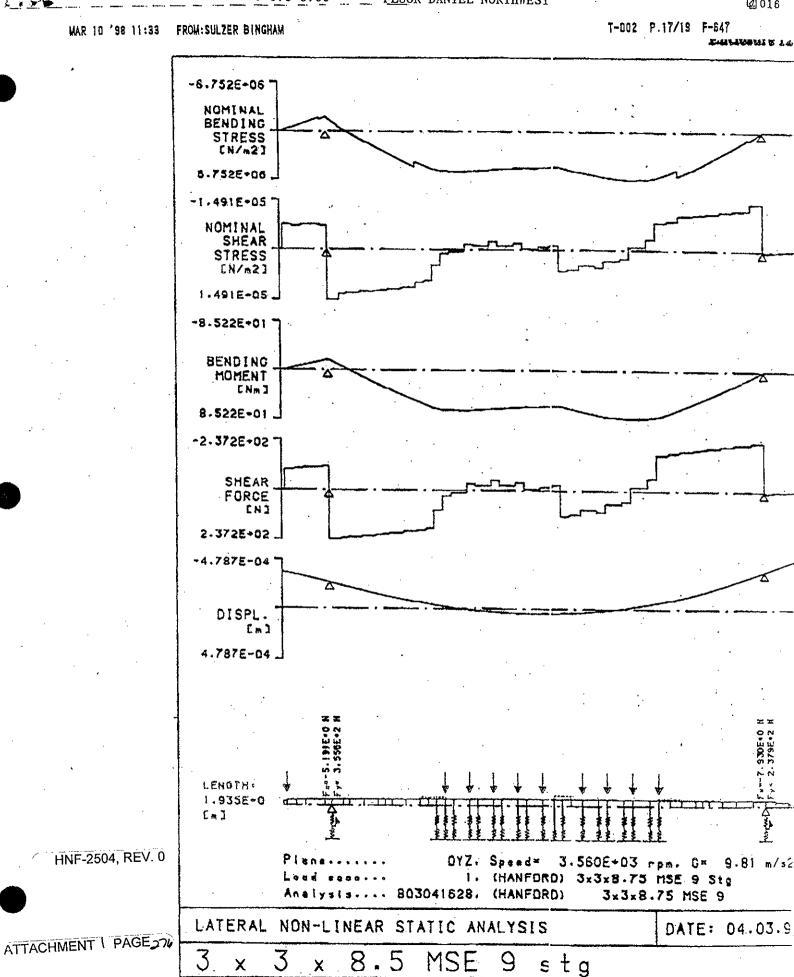

T-002 P.18/19 F-647

Enclosure 13

LIST	OF FREC	UENCIES	AND DA	MPING		
MODE NO.	SYMBOL	FREC CHrJ	UENCY [rem]	DAMPING EXI	ROTOR SPEED	PRECESSION FACTOR
. 1	១១០១១	37-67 58-24 79-66 101-89 123-54	2260 3495 4779 6113 7412	31.1 32.5 32.8 32.6 32.1	1560 2560 3560 4560, 5560	0.97 0.98 1.00 1.00
2000	66669	78.06 88.50 102.38 120.95 143.25	4684 5310 8143 7257 9595	14.4 19.6 22.0 22.1 26.5	1560 2560 3560 4560 5560	0.99 1.00 1.00 0.99
33333	Δ Δ Δ Δ	133.81 136.13 137.98 136.97 133.47	8028 8168 8279 8218 8008	2.5 4.1 5.1 8.9 6.3	1560 2560 3560 4560 5560	0.92 0.97 1.00 1.00 1.00

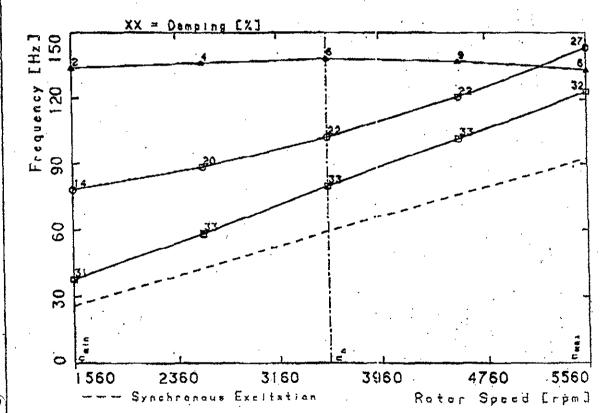

HNF-2504, REV. 0

ATTACHMENT | PAGE277


Pump State: New Analysis ... 803041633, (HANFORD) 3x3x8.75 MSE 99tg


EIGVC: FREQUENCY LIST AND CAMPBELL DIAGRAM DATE: 04:03.9


x 8.5 MSE stg


T-002 P.19/19 F-647


encontains 14

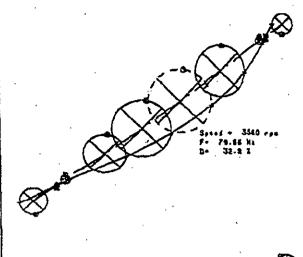









HNF-2504, REV. 0

ATTACHMENT | PAGE

Mode Shape No.

Pump State: New Analysis.... 803041633, (HANFORD) 3x3x8.75 MSE 95tg

LATERAL DAMPED NATURAL FREQUENCIES ANALYSIS

MSE 9 8.5 stg DATE: 04.03.

# PREOPERATIONAL TESTING POTP-007, CROSS SITE TRANSFER SYSTEM INTEGRATED TEST HNF-1857 PAGE 1 OF 1

REVISION NO. <u>0</u>

ATTACHMENT D

TEST EXCEPTION REPORT						
TEST PROCEDURE NO. & SECTION:	TEST-NAME:		T.E. NUMBER:			
HNF-1857	POTP-007 INT	EGRATED TEST	TE-006			
DESCRIPTION OF PROBLEM: Both A and B pumps restart automatically after a VSD fault because the start signal from PCU-2 is latched in and a VSD fault does not unlatch the start signal. Also the start/stop inputs to the VSD's are reversed.						
ORIGINATOR:		IMPACT ON TESTING:   HOL	D FOR RESOLUTION X CONTINUE			
M. D. Gerken 02/19/98		M. D. Gerken	02/19/98			
ORG: DATE:		TEST ENGINEER	DATE			
ORG: DATE: TEST ENGINEER DATE  DISPOSITION:  Write ECN to correct logic (unlatch start signal ECN 393) and wiring (start/stop inputs reversed ECN-391) at PCU-2 and retest that pump does not restart automatically after a local stop.  Retest:  1. Start pump P-3125A /P-3125B verify start energized and pump status "ON" are green on pump graphic screen and pump is running locally.  2. After 6 seconds verify start energized and pump status "ON" go off on pump graphic screen and pump continues to run locally.  3. Initiate a pump stop from the VSD and verify pump stops locally and does not automatically restart.  NOTE: Operations needs to reconfigure RSVIEW so that the start energized and pump status "ON" remain enabled. This requires the VSD run signals for both pumps to be connected to a spare input at PCU-2 and assigning this input to operate the RSVIEW tags for pump status.						
DISPOSITION AND RETEST REQUIREMENTS BY:  M. D. Gerken  DATE  DATE  DATE  DISPOSITION ACTIONS COMPLETE:  Verified  Verified  N. D. Gerken  DATE  RETEST COMPLETE:  M. D. Gerken  03/27/98						
DATE DATE	21/10	TEST ENGINEER	DATE			

## **ENGINEERING CHANGE NOTICE**

Page 1 of 4

1. ECN 647594-

	<u> </u>					
2. ECN Category (mark one)	<ol> <li>Originator's Name and Telephone No.</li> </ol>	e, Organization, MSIN,	4. USO Required?		5. Date	
Supplemental [X]	MA FRIEDRICH,T		[] Yes [	No	4-1-98	
Direct Revision []	7407					
Change ECN [] Temporary []	6. Project Title/No.		7. Bldg./Sys	s./Fac. No.	8. Approval Designator	
Standby [] Supersedure []		F CROSS-SITE XFER	241	-SY	<b>SQ/SC1</b>	
Cancel/Void []	9. Document Numbers	V058, C12300	10. Related	ECN No(s).	11. Related PO No.	
<u>.</u> :	(includes sheet r	no. and rev.)		•		
12a. Modification Work	HINT - 18:	57 REV 0-A	Complete		NA red to Original Condi-	
	No.		compress	tion (Temp.	or Standby ECN only)	
[] Yes (fill out Blk. 12b)	NA .	NA' .	•	NA	•	
[X] No (NA Blks. 12b,		Design Authority/Cog.	. Engineer	Design A	uthority/Cog. Engineer	
12c, 12d)		Signature & Da	rte	s	ignature & Date	
13a. Description of Change		13b. Design Baseline	Document?	] Yes [년	No   SC-3	
HNF-1857, REV 0-A:		•			•	
a) REVISE PAGE	13, AS SHOWN ON	PAGE 3 OF THIS EC	CN.		•	
b) REVISE PAGE	14, AS SHOWN ON	I PAGE 4 OF THIS EC	N.		•	
				٠		
		,				
<u> </u>		·			,	
	:					
14a. Justification (mark o	one)			· · · · · · · · · · · · · · · · · · ·		
Criteria Change []	Design Improvement	[] Environmental	[]	Facili	ty Deactivation []	
As-Found[]	Facilitate Const	[] Const. Error/C	Omission [X	] Design	Error/Omission []	
14b. Justification Details		דוור רו טון סאדר דטי	בטאורב וואס	DEEM DE	הבכוארה דויר	
THE DECADE BOX HAS INTERLOK (I-15) HAS	AS BEEN UNITITED. S REEN REVISED	THE FLOW RATE TOL				
ASPECTS OF THE DES		,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	.07 7 201			
		•	•			
15. Distribution (include				-	RELEASE STAMP	
FDNW DISTRIBUTION		RIBUTION LMUC S	20.00			
CONST DOC CONTROL			50-09 R1-56	DATE:	B SORPH STATE OF THE STATE OF T	
			3-47		KARFORD ( 10:	
				STA: Z	T RELEASE 2.	
				Lanno		
· ·				APR 0	1 1220	

	<u></u>			1. ECN (use no. from pg. 1)
ĖN	IGINEERING CHAN	GE NOTICE	Page 2 of	W-058-395
- 16. Design Verification Required	17. Cost Impact ENGINEERING	i con	ISTRUCTION MAN	18. Schedule Impact (days)  NOTE
[] Yes	Additional 🔀	\$ 150 Additional	[]_\$	Improvement []
TV NO	Savings	_\$ Savings —	[] \$	Delay []
19. Change Impact is that will be as SDD/DD Functional Design Criterion Operating Specification Criticality Specification Conceptual Design Reportangue Equipment Spec. Const. Spec. Procurement Spec. Vendor Information OM Manual FSAR/SAR Safety Equipment List Radiation Work Permit Environmental Impact St Environmental Report Environmental Permit	Review: Indicate the refected by the change depends on the change		an the engineering doer the affected document [] [] [] [] [] [] [] [] [] [] [] [] [] [	ocuments identified on Side 1)
indicate that	Documents: (NOTE: Do the signing organization mber/Revision	ocuments listed below will on has been notified of oth Document Number/Re	er affected document:	is ECN.) Signatures below s listed below. Document Number Revision
21. Approvals  Design Authority  Prof. Eng.  28g. Mgr.  QA L.R.HALL CFT  Safety M. C.  Environ. NA  Other MJ Sut	on Jalan . O	Date 4/1/98 1-4-98 4-1-98 4-1-98 4/1/98 NA 4-1-98 NA	Sign Design Agent MOLPE HALLIST OA Safety NA Design MOLF FLE Environ. Other  DEPARTMENT OF ENERGY Signature or a contracks the Approva	A NA NA Trol Number that
			ADDITIONAL	

	•	3	UNL . 1021
ISION NO. O-A		•	

		·	
		4.13.6	Multi-meter 0-600V.
			Manufacturer: Model No
			Serial No. Calibration Date D.G.
	,	• •	Calaboataon Oug Hato
			3/30/98
	. •	4.13.7	Process Instrument Calibrator, with 4-20 mA signal
			capability and simulating a 100 ohm (type 385) RTD. D. J. 14/17/97
			Manufacturer: Beta Model No. 110
			Serial No. 1776 Calibration Date 7/9/97
			Calibration Due Date 7/9/98 Cal. Social No. 817-23-01-002
i		4.13.8	Pucket with volumetric markings on side to collect oil
] [	٠.	4.10.0	Bucket, with volumetric markings on side, to collect oil drained from booster pump bearing housings
	-	מינו וו	
		4.13.9 ded 12/17/97	Decade Box Manufacturer: General Resistance Inc. Model No. DA-74-3X
Į	5.0	PROCEDURE	Serial No.: 723 Calibration Date: 5/97
Ì		·	Calibration Due Date: 5/98
		5.1 Preopera	tional testing shall be performed using Attachment A of this
•.		procedur	e
			ECN Na W -058-395 Page 3/4
•			Ref. Dwg Sh Rev
(	5.0	ACCEPTANCE CR	Prep. By M. FRIEDRICH Ckd. By
			<del></del>
			headers 3150 and 3160 from the Diversion Box to the Vent
	•		were filled with water; water was circulated through them by
		the boos	ter pumps; and the headers were vented and drained.  Test Engineer: Form House
			Test Eligities. Tours Jacks
			Quality Control
	/	$\sim$	
	ζ,	·	
			pumps $P$ -3125A and P-3125B operated at the design flowrates $\setminus$
1	(		pm $\pm$ (5)gpm and 140 gpm $\pm$ 7 gpm. and at a high flow condition
- (		nu of 160 g	pm $\pm 8$ gpm, under control of system flow feedback. (Sections
	7	9.0 and	10.0).
(			Tost Engineer of
			Test Engineer Docy John
		<u>}</u>	Ouality Control

HNF-2504, REV. 0 ATTACHMENT 2 PAGE 30

UNE 10E7

CHMASE

י חב זבה

ARKITHIS IS EXPLIMANTON FOR CHANGE

PREOPERATIONAL	TEST POTP-007,	CROSS	SITE	TRANSFER	SYSTEM	THILLIO
•		HNF	1857			

PAGE 14 OF 14

ISION NO. O-A

- 6.3 The following interlocks operate properly:
  - I-2: On high pressure shutdown operating booster pump, P-3125A or P-3125B.
  - I-6: The operating booster pump, P-3125A or P-3125B will shutdown:
    - A) On high pump bearing temperature
    - B) On high motor winding temperature
    - C) On high vibration
    - D) On pump seal failure
    - E) On low oil level
  - I-7: The pump will not be permitted to operate if the inlet pressure is lower than 10 psig
  - I-9: Transfer pump P-102-SY-02A will not be permitted to operate if operating booster pump is shutdown
  - I-10: Upstream transfer pump P-102-SY-02A will be shutdown if inlet pressure reaches 70 psig
  - I-14: On high discharge pressure, shutdown appropriate operating pump
  - I-15: The booster pump will not be permitted to operate if the associated vent and drain valves are not closed.
  - I-20 (with respect to supernate line vent only); On high pressure, shutdown transfer pump P-102-SY-02A.

Test Engineer Doug St. B. Quality Control

ECN No. W-058-395 Page 4/4

Ref. Dwg. Sh. Fale ORICH Ckd. Ed. Mar. Page 4/4

Prop. Sy M. FRIEDRICH

HNF-2504, REV. 0 ATTACHMENT 2 PAGE 283

INTERLOCK LOGIC (H-2-822400, Sh 1, Rev 5)

- If a leak is detected shutdown operating Booster Pump, P-3125A or P-3125B, 1. Transfer Pump P-102-SY-02A, and input signal to 200 West Master Pump Circuit. (Software)
- On high pressure shutdown operating Booster Pump, P-3125A or P-3125B. 2. (Software)
- On low level, shutdown Transfer Pump, P-102-SY-02A. (Software) 3.
- Sump pump will not be permitted to operate if associated outlet valve is not open. (Software)
- On positive pressure (gage), in transfer line, vent valves will not be permitted to 5. open. (Software)
- The operating Booster Pump, P-3125A or P-3125B, will shutdown: 6.
  - A) On high pump bearing temperature. (Software)
  - B) On high motor winding temperature. (Software)
  - C) On high vibration. (Software)
  - D) On pump sear failure. (Software)
  - E) On low oil level. (Software)
  - X) On local control. (Software)
- The Booster Pump will not be permitted to operate if the inlet pressure is lower 7. than 10psig. (Software)
- Shutdown operating Booster Pump when rupture disk PSE 841 or PSE 842 fails. 8. (Software)
- Transfer Pump P-102-SY-SY-02A, will not be permitted to operate if operating Booster Pump is shutdown. (Software)

- Upstream transfer pump P-102-SY-02A, will be shutdown if inlet pressure 10. reaches 70psig. (Software)
- On leak detection, shutdown Booster Pump P-3125A and P-3125B. (Hardwired) 11.
- On leak detection, shutdown Transfer Pump P-102-SY-02A. (Hardwired) 12.
- 13. On leak detection, input signal to 200East and 200West Master Shutdown Circuits. See Drawings H-2-822440 sh1 and 442 sh 1. (Hardwired)
- 14. On high discharge pressure shutdown appropriate operating pump. (Software)
- The Booster Pump will not be permitted to operate is the associated vent and 15. drain valves are not closed. (Software)
- 16. On high pressure, input signal to 200West Master Shutdown circuits. (Hardwired)
- If valve is open, input signal to 200West Master Shutdown circuits. (Hardwired) 17.
- 18. On low level, shutdown flush pump P-3100A. (Software)
- 19. On high process temperature, high heater sheath temperature, or low flow heater is shutdown. (Hardwired)
- 20. On high pressure, shutdown transfer pump P-102-SY-02A. (Software)
- 21. On positive pressure (gage), in transfer line, sump pump valves will not be permitted to open. (Software)

IL	SYS	DEVICE	P&ID	ALARM	IL ACTION/(HW or SW)	FUNCTION	LOCATION	TESTED	COMMENTS
01	SNL/SLL	LDE3150	403	LEAK	STOP P3125A/B & 2W MPS/S	SUMP LD	DB PUMP RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3150	403	LEAK	STOP P3125A/B & 2W MPS/\$	SUMP LD	DB PUMP RM	POTP-008	2.18 (Note 5)
01	SNL/SLL	LDE3150A	403	LEAK	STOP P3125A/B & 2W MPS/S	SUMP LD	DB PUMP RM	POTP-008	2.31 (Note 5)
01	SNL/SLL	LDE3151	404	LEAK	STOP P3125A/B & 2W MPS/S	SUMP LD	VS VAULT	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3151	404	LEAK	STOP P3125A/B & 2W MPS/S	SUMP LD	VS VAULT	POTP-008	2.44 (Note 5)
01	SNL/SLL	LDE3151A	404	LEAK	STOP P3125A/B & 2W MPS/S	SUMP LD	VS VAULT	POTP-008	2.58 (Note 5)
01	SNL/SLL	LDE3160A	403	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	DB SWGR RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3160B	403	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	DB SWGR RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3160C	403	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	DB SWGR RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3160D	403	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	DB SWGR RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3161A	404	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	VS SWGR RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3161B	404	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	VS SWGR RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3161C	404	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	VS SWGR RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3161D	404	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	VS SWGR RM	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3162A	405	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	CAB6241	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDE3162B	405	LEAK	STOP P3125A/B & 2W MPS/S	ENCASEMENT LD	CAB6241	ATP004//POTP005	9.10(A)/10.10(B)//12(MPS)
01	SNL/SLL	LDEPP	405	LEAK	STOP P3125A/B & 2W MPS/S	LIFT STATION LD	244A LIFT STA	POTP-004	9.34(A)(MPS)/10.34(B)(MPS)
02	SLL	PT3168	404	P>10PSIG	SHUT DOWN P3125A OR B/S	PROTECT VS HEPA	VS VAULT	ATP-004//POTP007	9.10/10.10//2.37/3.37
02	SLL	PT842	405	P>200PSIG	SHUT DOWN P3125A OR B/S	PROTECT EXST TF	244A LIFT STA	POTP-004	9.49(A)/10.49(B) (Note 1)
03	SNL	LSL3102	401	LEVEL LO	P102SYO2A PERMSVE/S	XFER PUMP LEVEL	SY102	ATP-003	9.1 (Note 2)
04	SNL	SOV3167A	404	≠OPEN	INHIBIT SUMP PUMP/S	SUMP DISCHARGE	VS VAULT	POTP-005	11.12-11.24
04	SNL	SOV3167B	404	≠OPEN	INHIBIT SUMP PUMP/S	SUMP DISCHARGE	VS VAULT	POTP-005	11.12-11.24
04	SNL	SOV3173A	403	≠OPEN	INHIBIT SUMP PP/S	SUMP DISCHARGE	DB PUMP RM	POTP-005	9.12-9.24
04	SNL	SOV3173B	403	≠OPEN	INHIBIT SUMP PP/S	SUMP DISCHARGE	DB PUMP RM	POTP-005	9.12-9.24
05	SNL	PT3126A	404	p>0PSIG	INHIB VENT VALVE OPEN/S	SUPER PRESSURE	VS VAULT	POTP-005	4.0
05	SLL	PT3126B	404	P>0PSIG	INHIB VENT VALVE OPEN/S	SLURRY PRESS	VS VAULT	POTP-004	5.0

HNF-2504, REV O ATT 3 PG 285

IL	SYS	DEVICE	P&ID	ALARM	IL ACTION/(HW or SW)	FUNCTION	LOCATION	TESTED	COMMENTS
06A	SLL	TE3125A1	400/2	T>200°F	SHUTDOWN P3125A/S	BP BRG TEMP	DB PUMP RM	POTP-007	2.26
06A	SLL	TE3125A2	400/2	T>200°F	SHUTDOWN P3125A/S	BP BRG TEMP	DB PUMP RM	POTP-007	2.27
06A	SLL	TE3125B1	400/2	T>200°F	SHUTDOWN P-3125B/S	BP BRG TEMP	DB PUMP RM	POTP-007	3.26
06A	SLL	TE3125B2	400/2	T>200°F	SHUTDOWN P-3125B/S	BP BRG TEMP	DB PUMP RM	POTP-007	3.27
06B	SLL ·	TSH3125A	400/2	T>175°F	SHUTDOWN P3125A/S	BP MOTOR TEMP	DB PUMP RM	POTP-007	2.28
06B	SLL	TSH3125B	400/2	T>175°F	SHUTDOWN P-3125B/S	BP MOTOR TEMP	DB PUMP RM	POTP-007	3.28
06C	SLL	VT3125A1	400/1	V>.6IN/S	SHUTDOWN P3125A/S	BP VIBRATION	DB PUMP RM	POTP-007	2.29
06C	SLL .	VT3125A2	400/2	V>.6IN/S	SHUTDOWN P3125A/S	BP VIBRATION	DB PUMP RM	POTP-007	2.30
06C	SLL	VT3125B1	400/1	V>.6IN/S	SHUTDOWN P-3125B/S	BP VIBRATION	DB PUMP RM	POTP-007	3.29
06C	SLL	VT3125B2	400/2	V>.6IN/S	SHUTDOWN P-3125B/S	BP VIBRATION	DB PUMP RM	POTP-007	3.30
06D	SLL	F\$H3125A1	400/2	F>11SCFH	SHUTDOWN P3125A/S	BP SEAL AIR	DB COMP RM	POTP-007	2.33
06D	SLL	FSH3125A2	400/2	F>11SCFH	SHUTDOWN P3125A/S	BP SEAL AIR	DB COMP RM	POTP-007	2.34
06D	SLL	FSH3125B1	400/3	F>11SCFH	SHUTDOWN P-3125B/S	BP SEAL AIR	DB COMP RM	POTP-007	3.33
06D	SLL	FSH3125B2	400/3	F>11SCFH	SHUTDOWN P-3125B/S	BP SEAL AIR	DB COMP RM	POTP-007	3.34
06D	SLL	PSL3125A1	400/2	P<110PSIG	SHUTDOWN P3125A/S	BP SEAL AIR	DB COMP RM	POTP-007	2.35
06D	SLL	PSL3125A2	400/2	P<110PSIG	SHUTDOWN P3125A/S	BP SEAL AIR	DB COMP RM	POTP-007	2.36
06D	SLL	PSL3125B1	400/3	P<110PSIG	SHUTDOWN P-3125B/S	BP SEAL AIR	DB COMP RM	POTP-007	3.35
06D	SLL	PSL3125B2	400/3	P<110PSIG	SHUTDOWN P-3125B/S	BP SEAL AIR	DB COMP RM	POTP-007	3.36
06E	SLL	LSL3125A1	400/2	LEVEL LO	SHUTDOWN P3125A/S	BP OIL LEVEL	DB PUMP RM	POTP-007	2.31
06E	SLL	LSL3125A2	400/2	LEVEL LO	SHUTDOWN P3125A/S	BP OIL LEVEL	DB PUMP RM	POTP-007	2.32
06E	SLL	LSL3125B1	400/2	LEVEL LO	SHUTDOWN P-3125B/S	BP OIL LEVEL	DB PUMP RM	POTP-007	3.31
06E	SLL	LSL3125B2	400/2	LEVEL LO	SHUTDOWN P-3125B/S	BP OIL LEVEL	DB PUMP RM	POTP-007	3.32
06X	SLL	HS3125A	400/2	OFF	SHUTDOWN P3125A/S	HAND-OFF-AUTO	DB SWGR RM	POTP-007	7.2.1
06X	SLL	HS3125B	400/2	OFF	SHUTDOWN P-3125B/S	HAND-OFF -AUTO	DB SWGR RM	POTP-007	8.4.1
07	SLL	PT3125A	403	P<10PSIG	INHIBIT P3125A/S	BP-A INLET P	DB PUMP RM	POTP-007	2.38
07	SLL	PT3125B	403	P<10PSIG	INHIBIT P-3125B/S	BP-B INLET P	DB PUMP RM	POTP-007	3.38

IL	SYS	DEVICE	P&ID	ALARM	IL ACTION/(HW or SW)	FUNCTION	LOCATION	TESTED	COMMENTS
08	SLL	YAS841	405	RD FAIL	STOP P3125A/B/S	RUPT DISK MON	244A	POTP-004	9.70(A)/10.70(B) (Note 1)
08	SLL	YAS842	405	RD FAIL	STOP P 3125A/B/S	RUPT DISK MON	244A .	POTP-004	9.79(A)/10.79(B) (Note 1)
09	SNL/SLL	P3125A or B	403	RUN	P102SY02A PERMSVE/S	XFER PUMP	DB PUMP RM	POTP-007	2.25/3.25
10	SNL/SLL	PT3125A	403	P > 70PSIG	STOP TRANSFER PUMP/S	BP-A INLET P	DB PUMP RM	POTP-007	2.38
10	SNL/SLL	PT3125B	403	P>70PSIG	STOP TRANSFER PUMP/S	BP-B INLET P	DB PUMP RM	POTP-007	3.38
11	SLL	LDE3151	404	LEAK	STOP P 3125A&B/H	SUMP LD	VS VAULT	POTP-005	10.23/10.24
11	SLL	LDE3151	404	LEAK	STOP P 3125A&B/H	SUMP LD	VS VAULT	POTP-008	2.48/2.49 (Note 5)
11	SLL	LDE3151A	404	LEAK	STOP P 3125A&B/H	SUMP LD	VS VAULT	POTP-008	2.62/2.63(Note 5)
11	SLL	LDK3150	403	LEAK	STOP P 3125A&B/H	SUMP LD	DB PUMP RM	POTP-005	8.23/8.24
11	SLL	LDK3150	403	LEAK	STOP P 3125A&B/H	SUMP LD	DB PUMP RM	POTP-008	2.22/2.23(Note 5)
11	SLL	LDK3150A	403	LEAK	STOP P 3125A&B/H	SUMP LD	DB PUMP RM	POTP-008	2.34/2.35(Note 5)
12	SNL/SLL	LDE3151	404	LEAK	STOP XFER PMP SY-02A/H	SUMP LD	VS VAULT	POTP-005	10.19-10.22
12	SNL/SLL	LDE3151	404	LEAK	STOP XFER PMP SY-02A/H	SUMP LD	VS VAULT	POTP-008	2.46(Note 5)
12	SNL/SLL	LDE3151A	404	LEAK	STOP XFER PMP SY-02A/H	SUMP LD	VS VAULT	POTP-008	2.60 (Note 5)
12	SNL/SLL	LDK3150	403	LEAK	STOP P102SY02A/H	SUMP LD	DB PUMP RM	POTP-005	8.19-8.22
12	SNL/SLL	LDK3150	403	LEAK	STOP P102SY02A/H	SUMP LD	DB PUMP RM	POTP-008	2.20(Note 5)
12	SNL/SLL	LDK3150A	403	LEAK	STOP P102SY02A/H	SUMP LD	DB PUMP RM	POTP-008	2.32.1(Note 5)
13	SNL/SLL	LDE3151	404	LEAK	INPUT TO 2E & 2W MPS/H	SUMP LD	VS VAULT	POTP-005	10.25 (Note 3)
13	SNL/SLL	LDE3151	404	LEAK	INPUT TO 2E & 2W MPS/H	SUMP LD	VS VAULT	POTP-008	2.47 (Note 5)
13	SNL/SLL	LDE3151A	404	LEAK	INPUT TO 2E & 2W MPS/H	SUMP LD	VS VAULT	POTP-008	2.61 (Note 5)
13	SNL/SLL	LDK3150	403	LEAK	INPUT TO 2E & 2W MPS/H	SUMP LD	DB PUMP RM	POTP-005	8.25 (Note 3)
13	SNL/SLL	LDK3150	403	LEAK	INPUT TO 2E & 2W MPS/H	SUMP LD	DB PUMP RM	POTP-008	2.21(Note 5)
13	SNL/SLL	LDK3150A	403	LEAK	INPUT TO 2E & 2W MPS/H	SUMP LD	DB PUMP RM	POTP-008	2.33(Note 5)
14	SLL	PT3125C	403	P>1250PSIG	STOP P3125A/S	BP-A OUTLET P	DB PUMP RM	ATP-004//POTP007	9.10//2.39
14	SLL	PT3125D	403	P>1250SPIG	STOP P-3125B/S	BP-B OUTLET P	DB PUMP RM	ATP-004//POTP007	10.10//3.39
· 15	SLL	MOV3125AA	400/2	≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40

HNF-2504, REV O

ATT D

PG 487

IL	sys	DEVICE	P&ID	ALARM	IL ACTION/(HW or SW)	FUNCTION	LOCATION	TESTED	COMMENTS
15	SLL	MOV3125AB	400/2	≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40
15	SLL	MOV3125AC	400/2	≠CLOSED ≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40
15	SLL	MOV3125AD	400/2	≠CLOSED ≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40
					· · · · · · · · · · · · · · · · · · ·				
15	SLL	MOV3125AE	400/2	≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40
15	SLL	MOV3125AF	400/2	≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40
15	SLL	MOV3125AG	400/2	≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40
15	SLL	MOV3125AH	400/2	≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40
15	SLL	MOV3125AJ	400/2	≠CLOSED	INHIBIT P3125A/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	2.40
15	\$LL	MOV3125AK	400/2	≠CLOSED	INHIBIT P3125A/S	BP VENT VALVE	DB PUMP RM	POTP-007	2.40
15	SLL	MOV3125BA	400/2	≠CLOSED	INHIBIT P-3125B/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	. 3.40
15	SLL	MOV3125BB	400/2	≠CLOSED	INHIBIT P-3125B/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	MOV3125BC	400/2	≠CLOSED	INHIBIT P-3125B/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	MOV3125BD	400/2	<b>≠CLOSED</b>	INHIBIT P-3125B/\$	BP DRAIN VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	MOV3125BE	400/2	≠CLOSED	INHIBIT P-3125B/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	MOV3125BF	400/2	≠CLOSED	INHIBIT P-3125B/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	MOV3125BG	400/2	≠CLOSED	INHIBIT P-3125B/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	MOV3125BH	400/2	≠CLOSED	INHIBIT P-3125B/S	BP DRAIN VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	MOV3125BJ	400/2	≠CLOSED	INHIBIT P-3125B/\$	BP DRAIN VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	MOV3125BK	400/2	≠CLOSED	INHIBIT P-3125B/S	BP VENT VALVE	DB PUMP RM	POTP-007	3.40
15	SLL	SOV3163	403	≠CLOSED	INHIBIT P3125A/B/S	PROCESS VV	DB PUMP RM	POTP-007	2.40, 3.40
16	SNL	PSH3113	402	P>10PSIG	2W MPS SHUTDOWN/H	SYS. PRESS	241SYA VP	POTP-005	12.34-12.37 (Note 1)
16	SNL	PSH3113	402	P>10PSIG	2W MPS SHUTDOWN/H	SYS. PRESS	241SYA VP	POTP-008	2.66, 2.68(Note 5)
16	SNL	PSH3113A	402	P>10PSIG	2W MPS SHUTDOWN/H	SYS. PRESS	241SYA VP	NEW	NEW (Note 4)
16	SNL	PSH3113A	402	P>10PSIG	2W MPS SHUTDOWN/H	SYS. PRESS	241SYA VP	POTP-008	2.71, 2.73(Note 5)
17	SNL	ZSH3113	402	≠CLOSED	2W MPS SHUTDOWN/H	VALVE POSITION	241SYA VP	POTP-005	12.39-12.43 (Note 1)
18	SNL/SLL	LIT302C-1	409	LEVEL<5'	STOP P3100A	FLUSH TK LEVEL	FLUSH TK	POTP-001	4.37-4.39

IL	SYS	DEVICE	P&ID	ALARM	IL ACTION/(HW or SW)	FUNCTION	LOCATION	TESTED	COMMENTS
19	SNL/SLL	FSL302C-4A	400/1	NO FLOW	SHUTDOWN HTR 2/H	FLUSH FLOW	FLUSH SKID	POTP-001	5.4-5.7
19	SNL/SLL	FSL302C-4B	400/1	NO FLOW	SHUTDOWN HTR 1/H	FLUSH FLOW	FLUSH SKID	POTP-001	5.4-5.7
19	SNL/SLL	TIC302C-4C	400/1	T>180°F	SHUTDOWN HTR 2/H	PROCESS TEMP HI	FLUSH SKID	POTP-001	5.72-5.80
19	SNL/SLL	TIC302C-4D	400/1	T>180°F	SHUTDOWN HTR 1/H	PROCESS TEMP HI	FLUSH SKID	POTP-001	5.26-5.34
19	SNL/SLL	TIC302C-4E	400/1	T>375°F	SHUTDOWN HTR 2/H	SHEATH TEMP HI	FLUSH SKID	POTP-001	5.87-5.94
19	SNL/SLL	TIC302C-4F	400/1	T>375°F	SHUTDOWN HTR 1/H	SHEATH TEMP HI	FLUSH SKID	POTP-001	5.41-5.48
20	SNL	PT3167	404	P>10PSIG	SHUT DOWN XFER PUMP/S	SUPER PRESS	VS PUMP RM	POTP-005	7.0-7.12
20	SNL	PT3173	403	P> 10PSIG	STOP P102SY02A/S	SUMP TO SUPER	DB PUMP RM	POTP-005	6.0-6.12
20	SNL	PT3185	404	P>10PSIG	SHUT DOWN XFER PUMP/S	SUPER PRESS	VS PUMP RM	POTP-007	2.44-2.56
21	SNL	PT3125E	403	P>0PSIG	INHIBIT SUMP VALVES	SUMP DISCHARGE	DB PUMP RM	POTP-005	5.8-5.14
21	SNL	PT3126E	404	P>0PSIG	INHIBIT SUMP VALVES	SUMP DISCHARGE	VS PUMP RM	POTP-005	4.9-4.14

(2/12/98)

7

#### Notes:

- Jumpers not installed at the time of the test. Testing was performed, using appropriate signals, from the connection point at the pit interface.
- LSL3102 (Level in Tank SY-102) does not show in the current design as a control element. (Wiring was removed per project ECN W-058-339, pages 4 and 9.) However, the functional control of this device was tested as part of ATP-003, section 9.1 in the event that it is reinstated..
- In accordance with design requirements, W-058 leak detection is not connected to the 200E Tank Farm Master Pump Shutdown (MPS) scheme. Interposing relays are provided at the 244A lift station for future connection, if desired. These relays were tested for proper action. The project is connected to the 200W MPS and this connection was also tested.
- Device PT3113A is redundant to PT3113. This device was not installed prior to the completion of testing for POTP-005.
- Redundant devices PT3113A, LDE3150A, and LDE3151A were installed subsequent to the normal testing. POTP-008 was put in place to perform the testing of these devices and to retest the original instruments.

Scc. Gerlen Dunks

SULZER PUMPS

Between Bearings Business Unit Kevin M. Harold Product Group Manager 2800 N.W. Front Avenue Portland, OR 97210-1502 U.S.A. Tel. (503) 226-5354

Tel. (503) 226-5354 Fax (503) 226-5242

Your reference:

Our reference: 1E776/777

Date: January 20, 1998

Fluor Daniel Northwest Inc. 2355 Stevens Drive Richland, Washington 99352-1100

Attn: Mr. Tony Gasperino

Subject: Oil Float Detectors - Revised

Dear Mr. Gasperino:

After further review, our engineering group has revised the oil level values as follows:

- Normal Oil level in bearing housing is 2.625 inches below shaft centerline
- Minimum Oil level in bearing housing (switch activation level) remains at 3.06 inches below shaft centerline

We apologize for the confusion. If you have any questions, please contact our office.

Best regards,

Kein W. Harold

<sup>^</sup>Kevin M. Harold

c:\windows\temp\1e776v.doc, 20.01.98, 14:17

age I/I

LINE ACOL O D. A-

\_\_\_\_

. .

## CORRESPONDENCE DISTRIBUTION COVERSHEET

Author

Addressee

Correspondence No.

G. R. Porter 372-2648

R. J. Brown, LMHC

NHC-9852239 March 11, 1998

subject: PROJECT W-058, "REPLACEMENT CROSS-SITE TRANSFER SYSTEM", BOOSTER PUMP STORAGE RECOMMENDATION

DISTRIBUTION						
Approval	Date	'Name	Location	w/att		
		Correspondence Contro	1 A3-01	Х		
		Fluor Daniel Northwes	t, Inc.			
,		K. J. Dempsey	G3-12	Х		
		J. L. Henderson	G3-14	χ.		
	, <i>'</i>	Lockheed Martin Hanfo	ord Corporation			
		M. G. Al-Wazani	T4-07	Χ		
		C. B. Bryan	T4-07	X		
		C. R. Reichmuth	T4-07	Χ		
		M. J. Sutey	T4-08	X		
	,	Lockheed Martin Servi	ices,_Inc.			
		Project Files	R1-29	· X		
•		Numatec Hanford Corpo	oration	•		
	E. Pacquel	P. A. Haine.	R3-47	X		
		G. L. Parsons	R3-47	χ		
		G. R. Porter	R3-47	. Х		
		GLP File/LB	R3-47	χ		

RECEIVED

MAR 1 1 1998

P.A. HAINE

A-6001-538 (11/97) WEF008



March 11, 1998

NHC-9852239

Mr. R. J. Brown, Manager Technical Operations and Projects T4-08 Lockheed Martin Hanford Corporation Post Office Box 1500 Richland, Washington 99352-1505

Dear Mr. Brown:

PROJECT W-058, "REPLACEMENT CROSS-SITE TRANSFER SYSTEM", BOOSTER PUMP STORAGE RECOMMENDATION

Supplemental recommendations for long term maintenance of the Cross-Site Transfer System booster pumps has been received from Sulzer Pumps. A copy of these recommendations is attached for your information.

The Project recommends that Option 3 be implemented by Operations for the long term maintenance/storage of the subject pumps. This option entails some pump disassembly, but provides the greatest long term protection of the pump with the least maintenance monitoring activities. This option is also consistent with current TWRS planning that reflects no slurry transfers within the next several years.

Very truly yours,

Md Parsona

G. L. Parsons, Project Manager Replacement Cross-Site Transfer System Tank Farm Upgrade Projects

map

Attachment



## 1E776/1E777 INSTRUCTION MANUAL SUPPLEMENT

## RECOMMENDED PROCEDURE FOR 1E776/1E777 HANFORD TRANSFER HORIZONTAL MSE PUMPS

## LONG TERM MAINTENANCE FOR INSTALLED PUMPS

## WARNING: Seals must have gas purge maintained at all times when pump is flooded.

This procedure outlines three (3) methods that can be used for pumps which may have long terms of inactivity between in operation:

OPTION 1 FULL OPERATION - (Frequency: 15-30 minute runs every month)

The purpose of this monthly run is to circulate the oil around the bearing housing to prevent corrosion of metal parts:

- 1) PARTIALLY CLOSE DISCHARGE VALVE
- 2) START NITROGEN PURGE TO SEAL
- 3) OPEN PUMP SUCTION VALVE
- 4) OPEN VENT VALVES, ENSURE PUMP IS COMPLETELY PRIMED
- 5) CLOSE VENT VALVES
- 6) START PUMP, BRING UP TO 2500 RPM (WITHIN 5 SECONDS)
- 7) FULLY OPEN DISCHARGE VALVE AND ENSURE PUMP REACHES BEST EFFICIENCY FLOW AND DESIGN PRESSURE
- 8) OPERATE PUMP FOR 15-30 MINUTES

## OPTION 2 'BUMP' OPERATION - (Frequency: Once every three (3) months or less)

Due to discharge system pipe work not being available/operational, an alternative is to 'bump' start pump (i.e. pump operates for approximately 15 seconds against fully closed discharge valve):

- 1) -FULLY CLOSE DISCHARGE VALVE
- 2) START NITROGEN PURGE TO SEAL
- 3) OPEN PUMP SUCTION VALVE
- 4) OPEN VENT VALVES, ENSURE PUMP IS COMPLETELY PRIMED
- 5) CLOSE VENT VALVES
- 6) START PUMP, BRING UP TO 2500 RPM WITHIN 5 SECONDS
- 7) OPERATION AT 2500 RPM IS NOT TO EXCEED 10 SECONDS, (DUE TO TEMPERATURE INCREASE IN PUMPAGE) THEN STOP PUMP (COAST DOWN TIME IS ACCEPTABLE AND DESIRABLE)

TECHNICAL NOTE: The main concerns with infrequent operation is moisture in the bearing housing, which could cause corrosion. For this reason, SBPI selected a synthetic oil due to:



## 1E776/1E777 INSTRUCTION MANUAL SUPPLEMENT

## RECOMMENDED PROCEDURE FOR 1E776/1E777 HANFORD TRANSFER HORIZONTAL MSE PUMPS

## LONG TERM MAINTENANCE FOR INSTALLED PUMPS

- Does not emulsify with water
- Synthetic corrosion inhibitors ironically bond to metal surfaces displacing water and other contamination's

Synthetic oil reduces operation time to every three (3) months, although every month would be even more desirable. Bump starting for 15 seconds (plus coast down time) will allow the oil rings to disperse synthetic oil throughout the bearing housing internals.

## OPTION 3 REMOVE BEARINGS AND SEALS -

If the time between installation and pumping contaminants is long (>1 year) and pump is dry, bearing and seal removal from shaft should be considered:

Advantages:

- No maintenance (i.e., pump operation/turning not required)
- No risk of corrosion in bearing housing

### The procedure is:

- 1) REMOVE COUPLING, BEARING HOUSINGS, COMPONENTS AND SEALS
- 2) COAT BEARING AND HOUSING SURFACES WITH RUST PREVENTATIVE (SHELL ENSIS FLUID NO. 210 OR EQUAL). ENCLOSE DESICCANT (BAGGED, NON-HALOGENATED, NON-DELIQUESCENT, CHEMICALLY INSERT SILICA GEL TO COMPLY WITH MIL-D-3464-D, TYPE 11). SEAL OFF WITH PROTECTIVE TARPAULIN
- 3) REMOVE SEALS. STORE SEALS IN ACCORDANCE WITH SEAL MANUFACTURERS INSTRUCTIONS.
- 4) PUMP ROTATING ELEMENT RESTS ON STATIONARY WEAR RINGS (NOTE DO NOT TURN "SHAFT!)
- 5) BLANK OFF STUFFING BOX WITH WOODEN COVER AND WRAP WITH TARPAULIN TO PREVENT ENTRY OF FOREIGN MATERIAL
- 6) SEAL OFF EXPOSED SHAFTS WITH TARPAULIN

TECHNICAL NOTE: During rebuild/start-up a SBPI Field Services representative is recommended. It is also recommended, that if the storage period is excessive (>1 year), all elastomers (in seals) and bearings should be replaced prior to 'contaminated' start up.

DISTRIBUTION SHEET					
То	From	Page 1 of 1			
Distribution	E.A. Pacquet - W-058 Testing	Date 03/31/98			
Project Title/Work Order		EDT No. 623670			
Replacement Cross-Site	Tranfer System	ECN No. N/A			

Name	MSIN	Text With All Attach.	Text Only	Attach./ Appendix Only	EDT/ECN Only
R.J. Brown, LMHC	T4-08	Х			
W.G. Brown, LMHC	T4-07	χ			
J.R. Collins, FDNW	G3-14	Χ			
J.E. Dunks, FDNW	R3-47	Х			
J.M. Dormant, NHC	R3-47	χ			
L.R. Hall, FDNW	R3-47	Х			
B.J. Harp, DOE-RL	S7-54	Х			
D.A. Greenaway, LMHC	T4-09	Х			
J.L. Henderson, FDNW	G3-14	X		·	
O.M. Jaka, LMHC	S5-12	X			
R.L. Legg, LMHC	R2-50	Х			
G.A Leshikar, Cogema Engineering	S0-08	Х			
D.R. Nunamaker, LMHC	T4-07	X			
E.A. Pacquet, NHC	R3-47*	X			
G.L. Parsons, NHC	R3-47*	X			
C.R. Reichmuth, LMHC	T4-07*	X			
M.J. Sutey, LMHC	T4-08	X			
C. van Katwijk, NHC	R3-47	X			
M.D. Gerken, NHC	R3-47*	X			
D.O. Dobson, LMHC	R2-50	X			
M.J. Bailey, LMHC	T4-07	X			
Project Files	R1-29	. Х		<del> </del>	

<sup>\*</sup> Advance Copy
