

Plutonium Finishing Plant Update

For the Week Ending January 27, 2019

Summary:

Completed mentoring for 31 new D&D workers at the PFP mock-up areas. Continued housekeeping and sizing of lower-risk debris and load out in preparation for lower-risk demolition to begin within the next month.

Accomplishments: (Week of Jan. 20)

- Continued mentoring sessions for new D&D work crews at mock-up areas
- Performed additional housekeeping around main processing facility
- Shipped 30 containers to the Environmental Restoration Disposal Facility (ERDF)

Safety Issues or Concerns:

- None

Radiological Issues or Concerns:

- None

Contamination Discovered Outside the Radiological Buffer Area (RBA):

- None

Bioassays Requested:

- None

Upcoming Work:

- Continue lower-risk demolition debris sizing and load out on the north side of 234-5Z
- Continue preparations to resume lower-risk demolition of 234-5Z
- Completed mentoring of 31 new PFP workers and prepared for deployment to field crews

Employee Interface:

Summary:


- PFP management continues holding regular (bi-weekly) roundtables with employees.




Under the tutelage of experienced mentors, new PFP employees practice wrapping, covering and securing mock waste in large containers in an area designed to simulate work at the facility. This week, the new hires will be assigned to field work crews based on their skills and abilities.

PFH HAZARD REDUCTION PROGRESS

MAR and Waste Reduction During Demo

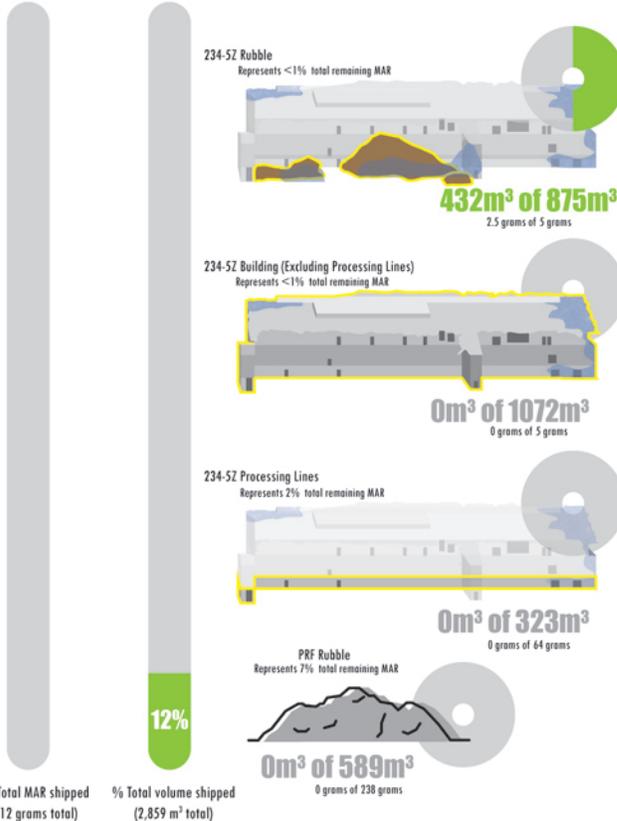

Loaded Low Level Waste

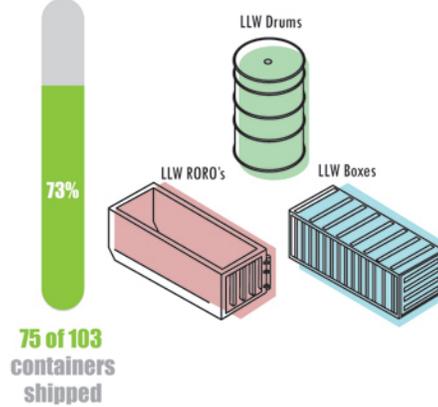

Loaded Universal/Hazardous Waste



TRU Waste Dispositioning During Stabilization



MAR=Material at Risk (Plutonium)

234-SZ=Main Processing Facility

PRF=Plutonium Reclamation Facility

LLW RORO's=Low-Level Waste Roll-On Roll-Off Containers

TRU=Transuranic (Waste)

SLB2=Standard Large Box 2

SWB=Standard Waste Box
