

Plutonium Finishing Plant Update

For the Week Ending February 10, 2019

Summary:

Snow and sustained below-freezing temperatures slowed work last week on debris resizing and load out. Lower-risk demolition is still on track to begin later this month. Began preparations for the independent management assessment required prior to restart of higher-risk work.

Accomplishments: (Week of Feb. 4)

- Performed additional housekeeping around main processing facility
- Loaded 8 containers for shipping to the Environmental Restoration Disposal Facility (ERDF)
- Began preparations for independent management assessment set to begin March 25

Safety Issues or Concerns:

- None

Radiological Issues or Concerns:

- None

Contamination Discovered Outside the Radiological Buffer Area (RBA):

- None

Bioassays Requested:

- None

Upcoming Work:

- Continue lower-risk demolition debris sizing and load out on the north side of 234-5Z
- Continue preparations to resume lower-risk demolition of 234-5Z later this month
- Continue preparations for independent management assessment required prior to restart of higher-risk work


Employee Interface:

Summary:


- PFP management continues holding regular (bi-weekly) roundtables with employees.
- PFP project is holding briefings for neighboring projects and teams on plans to resume lower-risk demolition activities.

PFM HAZARD REDUCTION PROGRESS


MAR and Waste Reduction During Demo

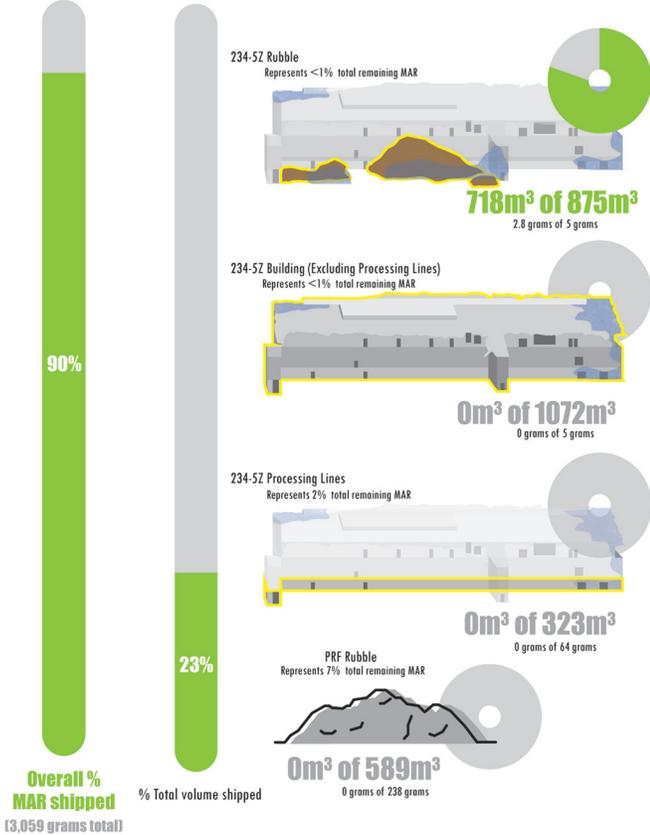


Loaded Low Level Waste

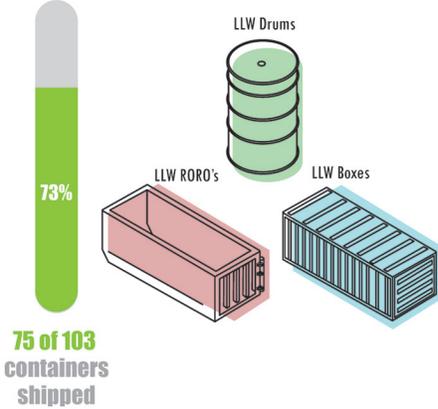

Loaded Universal/Hazardous Waste

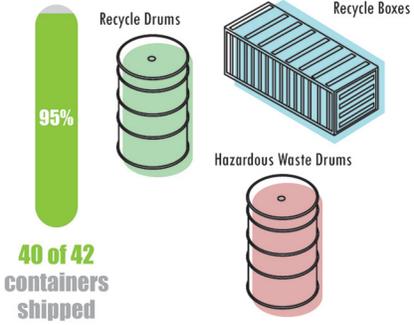

TRU Waste Dispositioning During Stabilization

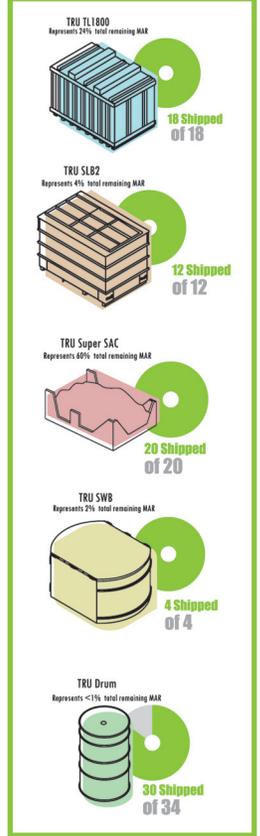

MAR=Material at Risk (Plutonium) PRF=Plutonium Reclamation Facility TRU=Transuranic (Waste) SWB=Standard Waste Box
234-5Z=Main Processing Facility LLW RORO's=Low-Level Waste Roll-On Roll-Off Containers SLB2=Standard Large Box 2
