

Plutonium Finishing Plant Update

For the Week Ending July 14, 2019

Summary:

Continued demolition and debris load out on remaining lower-risk portion of the PFP Main Processing Facility.

Key Accomplishments: (Week of July 7)

- Continued lower-risk demolition at east end of the PFP Main Processing Facility; prepared to begin demo on west end of the facility. (See graphic on page 2)
- Continued work to expand ERDF container loading area
- Shipped 12 containers to ERDF

Safety Issues or Concerns:

- None

Radiological Issues or Concerns:

- None

Contamination Discovered Outside the Radiological Buffer Area (RBA):

- None

Bioassays Requested:

- None

Upcoming Work:

- Continue demolition on remaining lower-risk portion of the Main Processing Facility
- Continue shipments of debris to ERDF
- Continue preparations for the start of higher-risk demolition activities

Employee Interface:

- PFP management continues holding regular roundtables with employees.




Early June 2019



July 11, 2019

Lower-risk demolition continues to make good progress on the Main Processing Facility.

PFP Main Processing Facility Lower-Risk Demolition: 25% Complete

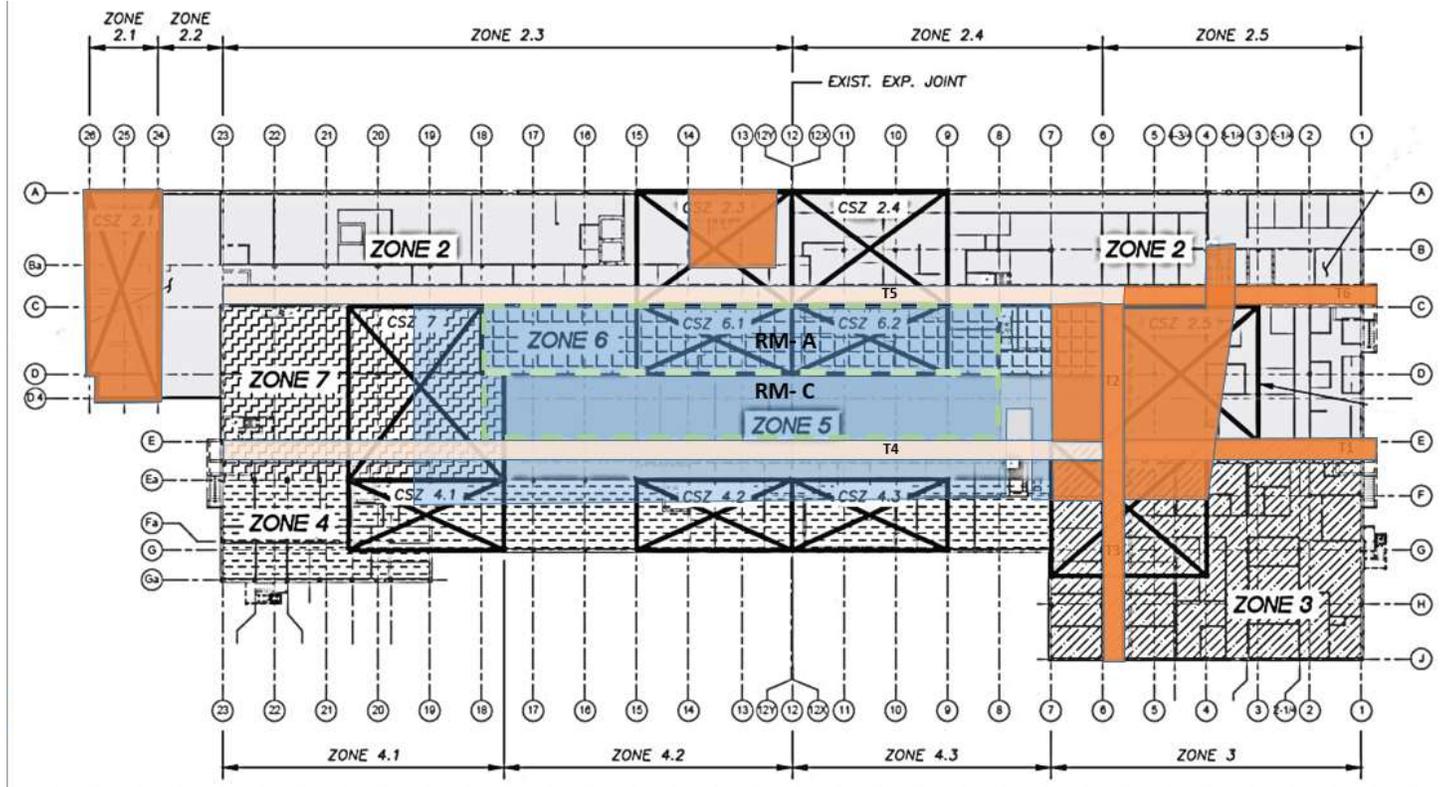

- Remaining building for demo
- Tunnel to be demolished
- Completed Lower Risk Demo
- RM-A and RM-C area
