

Plutonium Finishing Plant Update

For the Week Ending Nov. 3, 2019

Summary:

Completed demolition of lower-risk portion of the PFP Main Processing Facility. Prepared to begin final phase of demolition on remaining structure.

Key Accomplishments: (Week of Oct. 27)

- Completed lower-risk demolition of the PFP Main Processing Facility. (See graphic below)
- Shipped 10 containers to ERDF

Safety Issues or Concerns:

- None

Radiological Issues or Concerns:

- None

Contamination Discovered Outside the Radiological Buffer Area (RBA):

- None

Bioassays Requested:

- None



Upcoming Work:

- Begin demolition of remaining portion of the Main Processing Facility
- Continue shipments of debris to ERDF

Employee Interface:

- PFP management continues holding regular roundtables with employees.
- PFP management is offering briefings for neighboring projects on demolition progress and path forward.

PFP Main Processing Facility Lower-Risk Demolition: ~93% Complete

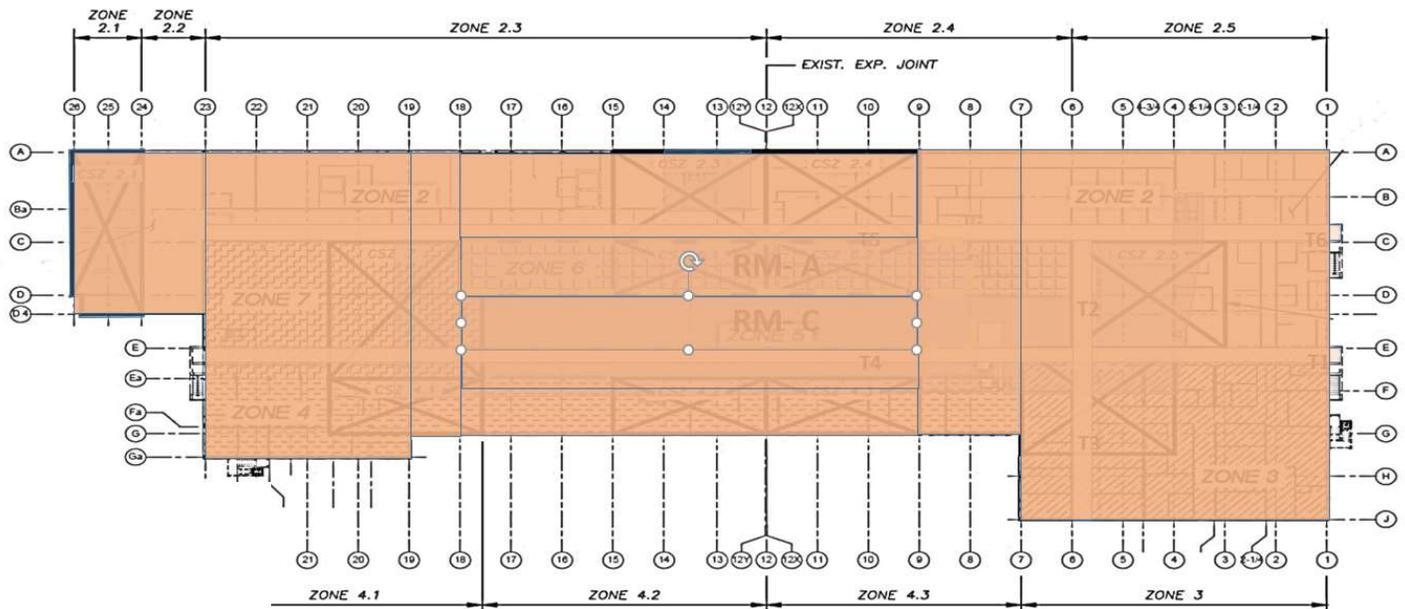



PFP south side on Oct. 25, 2019



PFP south side on Oct. 31, 2019
