

Plutonium Finishing Plant Update

For the Week Ending Jan. 19, 2019

Summary:

Continued safe progress on the final phase of demolition activities at PFP this month amid weeks of windy, freezing and snowy conditions. The forecast looks to be improving this week.

Key Accomplishments: (Week of Jan. 13)

- Shipped 16 containers to ERDF

Safety Issues or Concerns:

- None

Radiological Issues or Concerns:

- None

Contamination Discovered Outside the Radiological Buffer Area (RBA):

- None

Bioassays Requested:

- None


Upcoming Work:

- Complete sizing and load out of Remote Mechanical A (RMA) line debris
- Continue preparations for removal and disposal of rubble from Plutonium Reclamation Facility

Employee Interface:

- PFP management continues holding regular roundtables with employees.
- PFP management is offering briefings for neighboring projects on demolition progress and path forward.

PFP Main Processing Facility Final Phase Demolition: 75% Complete

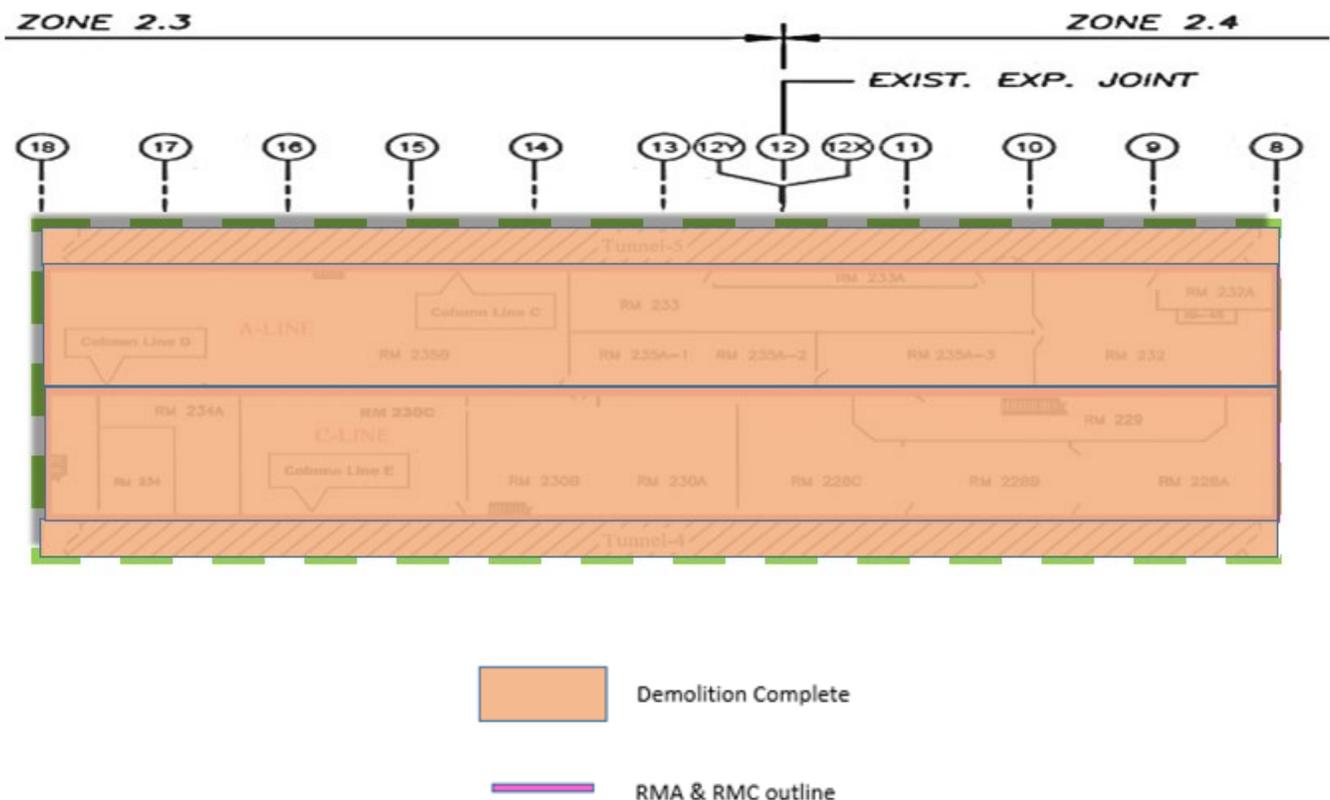



*Crews are nearing completion of sizing and load out of remaining debris from the main processing facility.
Photo from Jan. 20, 2020*
