
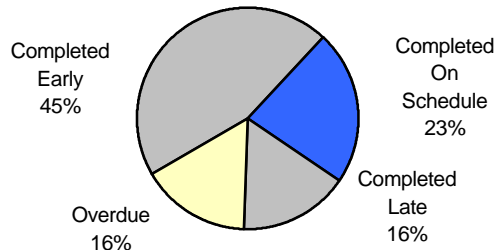
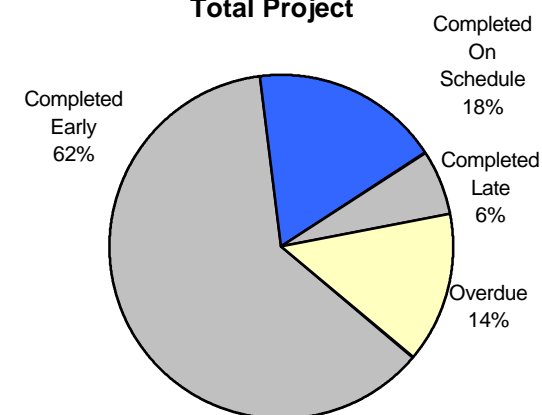
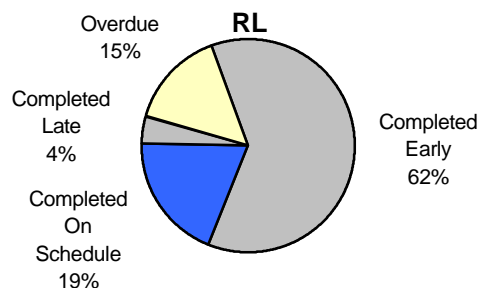


<b>HANFORD SITE PERFORMANCE REPORT</b>	<b>TOTAL ALL HANFORD PROJECTS</b>	<b>FEBRUARY 1998</b>
--	-----------------------------------	----------------------

**MILESTONE ACHIEVEMENT**

MILESTONE TYPE	FISCAL YEAR-TO-DATE				REMAINING SCHEDULED			TOTAL FY 1998
	Completed Early	Completed On Schedule	Completed Late	Overdue	Forecast Early	Forecast On Schedule	Forecast Late	
Enforceable Agreement	25	3	0	2	0	49	7	86
DOE-HQ	2	1	0	2	0	25	2	32
FO	14	7	5	5	2	88	4	125
RL	29	9	2	7	0	154	11	212
<b>Total Project</b>	<b>70</b>	<b>20</b>	<b>7</b>	<b>16</b>	<b>2</b>	<b>316</b>	<b>24</b>	<b>455</b>

**Enforceable Agreement****FO****Total Project****RL****DOE-HQ**
