
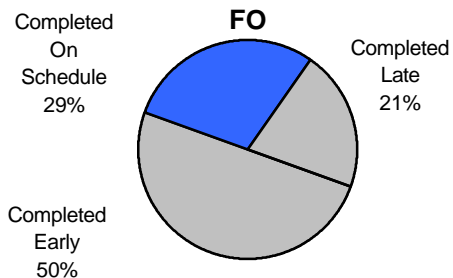
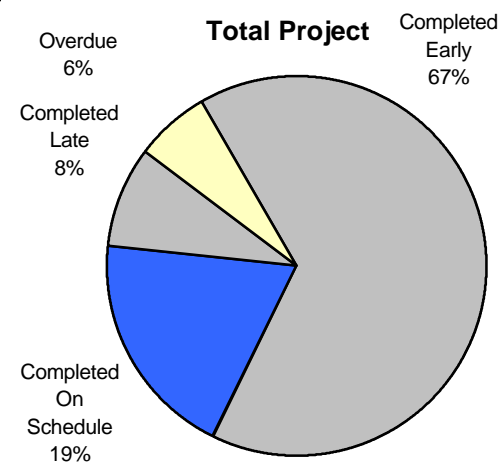
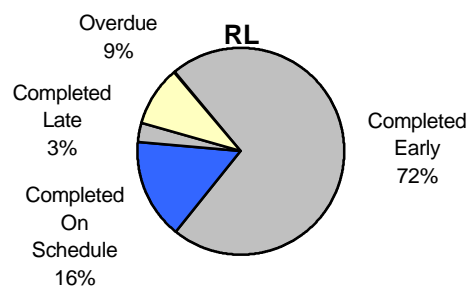


<b>HANFORD SITE PERFORMANCE REPORT</b>	<b>TOTAL ALL HANFORD PROJECTS</b>	<b>MARCH 1998</b>
--	-----------------------------------	-------------------

**MILESTONE ACHIEVEMENT**

MILESTONE TYPE	FISCAL YEAR-TO-DATE				REMAINING SCHEDULED			TOTAL FY 1998
	Completed Early	Completed On Schedule	Completed Late	Overdue	Forecast Early	Forecast On Schedule	Forecast Late	
Enforceable Agreement	29	5	1	3	0	43	3	84
DOE-HQ	2	1	0	1	0	20	4	28
FO	24	14	10	0	0	84	3	135
RL	46	10	2	6	0	130	6	200
<b>Total Project</b>	<b>101</b>	<b>30</b>	<b>13</b>	<b>10</b>	<b>0</b>	<b>277</b>	<b>16</b>	<b>447</b>

**Enforceable Agreement****FO****Total Project****RL****DOE-HQ**
