
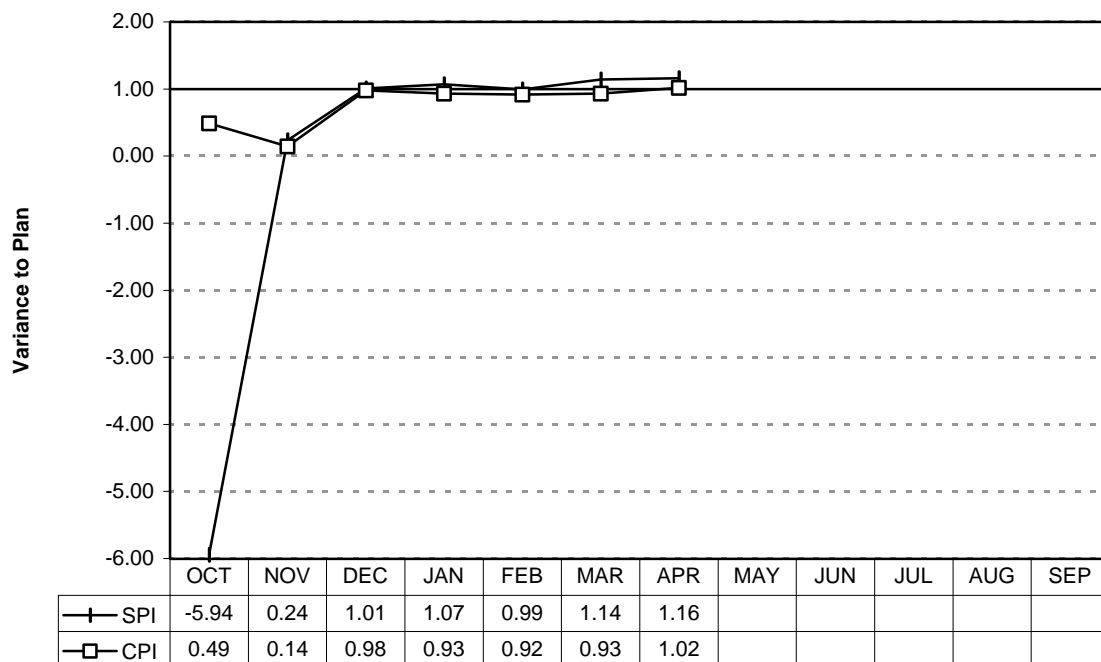


Source: PTS

<b>HANFORD SITE PERFORMANCE REPORT</b>	<b>HAMMER WBS: 1.9</b>	<b>APRIL 1998</b>
--	----------------------------	-------------------

**FY 1998 COST/SCHEDULE PERFORMANCE - ALL FUND TYPES**

Cumulative to Date Status

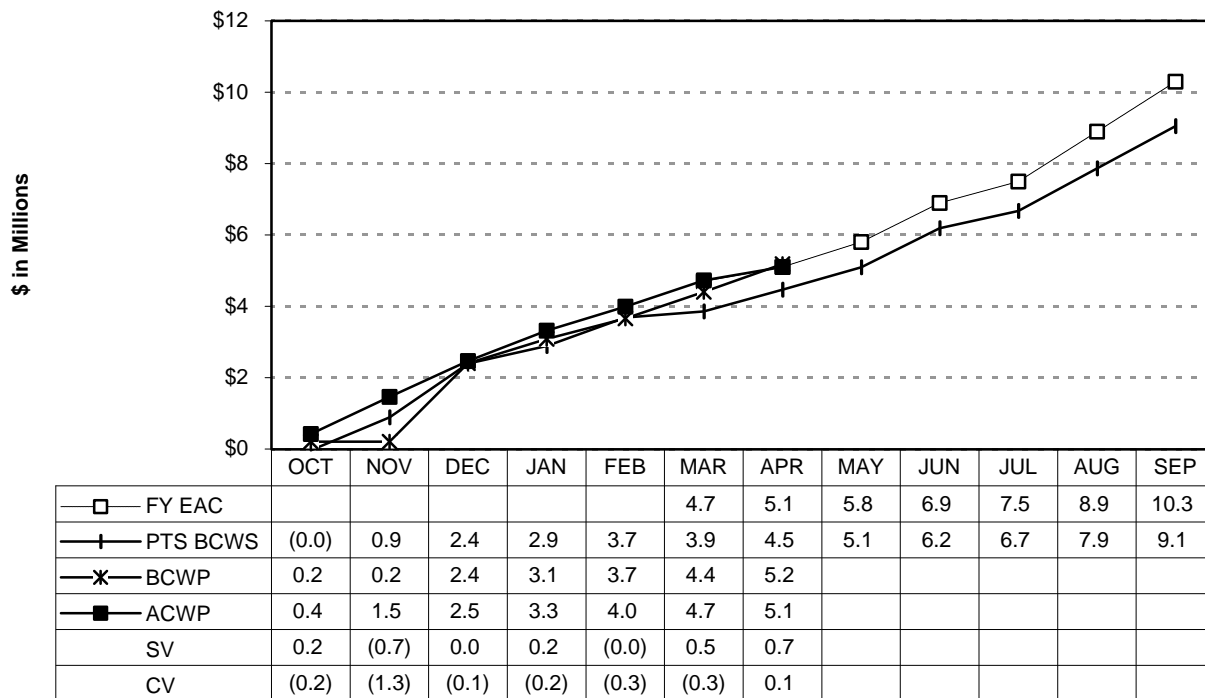

Source: PTS

Section N

<b>HANFORD SITE PERFORMANCE REPORT</b>	<b>HAMMER WBS: 1.9</b>	<b>APRIL 1998</b>
--	----------------------------	-------------------

			<u>BCWS</u>	<u>BCWP</u>	<u>FYTD ACWP</u>	<u>SV</u>	<u>CV</u>	<u>CUR BSLN</u>	<u>PTS BCWS</u>	<u>FY EAC</u>
PBS										
HM01	HAMMER	Expense	3.6	3.7	3.3	0.1	0.3	5.1	7.2	7.8
		CENRTC	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
		GPP/LI	<u>0.9</u>	<u>1.5</u>	<u>1.8</u>	<u>0.7</u>	<u>(0.2)</u>	<u>0.0</u>	<u>1.9</u>	<u>2.5</u>
		Total HAMMER*	4.5	5.2	5.1	0.7	0.1	5.1	9.1	10.3

\$ in Millions

\* The difference between the current baseline and PTS BCWS column is that the FY 1998 MYWP does not include prior year funding of \$2,388K for the Tulane/Xavier Grant for FY 1998 work. Additionally, the FY 1998 MYWP does not include prior year funding of \$1,875K for Line Item work to be completed this fiscal year. The difference between the PTS BCWS and FY EAC columns is that the Line Item FY EAC includes \$1,062K of cost for prior year BCWS.
