
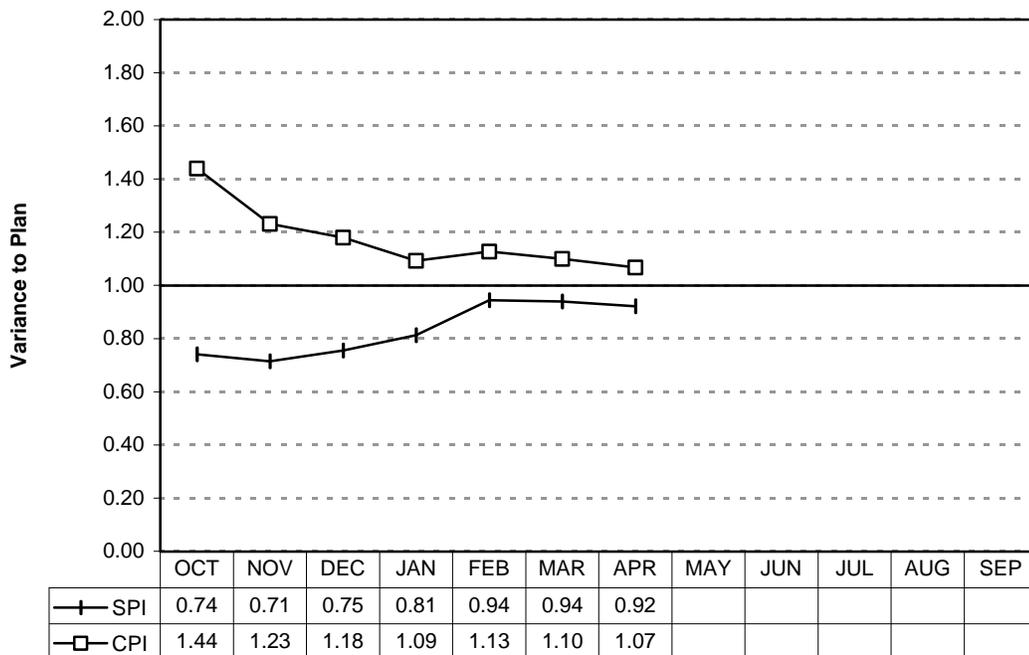


HANFORD SITE	SCIENCE & TECHNOLOGY	APRIL 1998
PERFORMANCE REPORT	WBS: 1.7	

FY 1998 COST/SCHEDULE PERFORMANCE - ALL FUND TYPES

Cumulative to Date Status

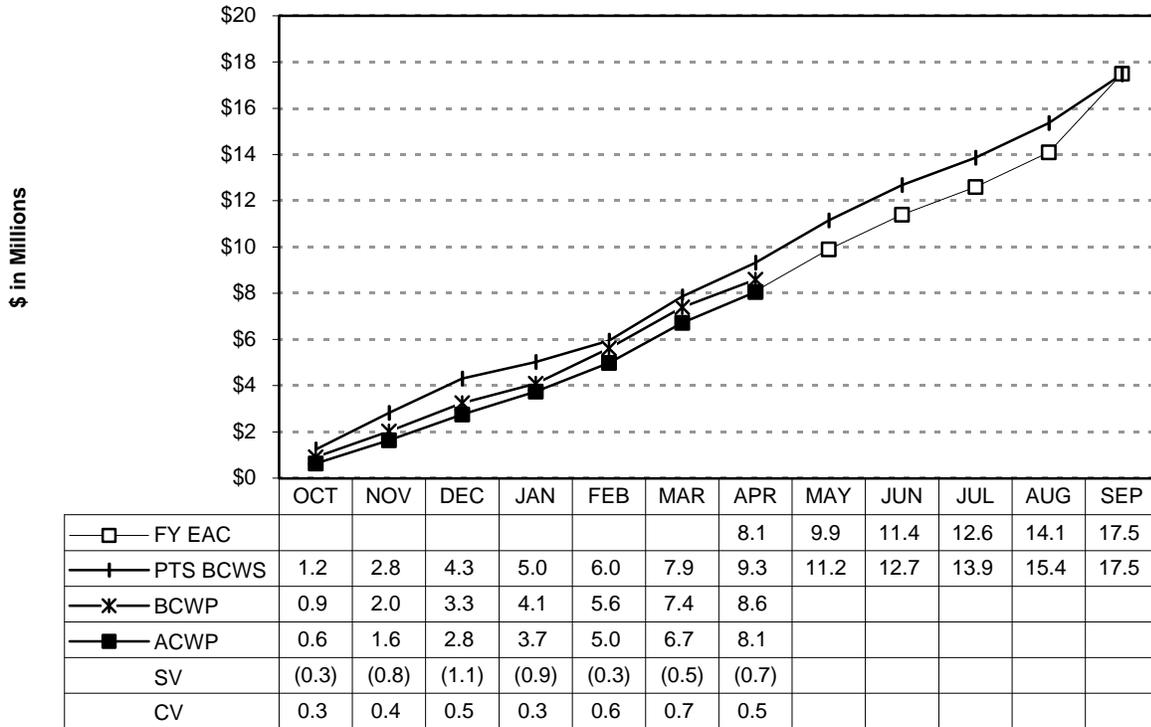

Source: PTS

Section L

HANFORD SITE PERFORMANCE REPORT	SCIENCE & TECHNOLOGY WBS: 1.7	APRIL 1998
------------------------------------	--	------------

			BCWS	BCWP	FYTD ACWP	SV	CV	CUR BSLN	PTS BCWS	FY EAC
1.3										
PBS										
ST01	PNNL Waste Management	Expense	8.2	7.6	7.0	(0.6)	0.6	15.9	15.9	15.8
		CENRTC	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
		GPP/LI	<u>1.1</u>	<u>1.0</u>	<u>1.1</u>	<u>(0.1)</u>	<u>(0.1)</u>	<u>1.6</u>	<u>1.6</u>	<u>1.7</u>
	Sub-Total ST01		9.3	8.6	8.1	(0.7)	0.5	17.5	17.5	17.5
ST02	Science & Technologies	Expense	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
		CENRTC	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
		GPP/LI	<u>0.0</u>	<u>0.0</u>	<u>0.0</u>	<u>0.0</u>	<u>0.0</u>	<u>0.0</u>	<u>0.0</u>	<u>0.0</u>
	Sub-Total ST02		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
	Total Science & Technology	Expense	8.2	7.6	7.0	(0.6)	0.6	15.9	15.9	15.8
		CENRTC	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
		GPP/LI	<u>1.1</u>	<u>1.0</u>	<u>1.1</u>	<u>(0.1)</u>	<u>(0.1)</u>	<u>1.6</u>	<u>1.6</u>	<u>1.7</u>
	Total		9.3	8.6	8.1	(0.7)	0.5	17.5	17.5	17.5

\$ in Millions

* The difference between the current baseline column on this page and the current baseline column on A: VI-1, "FY 1998 Project Baselines," is that BCR PWM98-018, which adds \$723K was approved on 4/27/98, after the close of the fiscal month. The current FY 1998 baseline, as of April 30, is \$17,471K.
