



Section F

EM-50

Science & Technology Activities

MILESTONE ACHIEVEMENT

M I L E S T O N E T Y P E	FISCAL YEAR-TO-DATE				REMAINING SCHEDULED			T O T A L F Y 2 0 0 1
	Completed Early	Completed On Schedule	Completed Late	Overdue	Forecast Early	Forecast On Schedule	Forecast Late	
Enforceable Agreement	0	0	0	0	0	0	0	0
DOE-HQ	0	0	0	0	0	1	0	1
RL	0	0	1	0	0	0	0	1
Total Project	0	0	1	0	0	1	0	2

MILESTONE EXCEPTION REPORT

<u>Number/WBS</u>	<u>Level</u>	<u>Milestone Title</u>	<u>Baseline Date</u>	<u>Forecast Date</u>
-------------------	--------------	------------------------	----------------------	----------------------

Overdue – 0

Forecast Late – 0

FY 2001 SCHEDULE / COST PERFORMANCE – ALL FUND TYPES CUMULATIVE TO DATE STATUS – (\$000)

Green


	FYTD									
	BCWS	BCWP	ACWP	SV	SV%	CV	CV%	PEM	EAC	
Technology Development (EM-50)	\$ 13,736	\$ 12,491	\$ 13,797	\$ (1,246)	-9%	\$(1,307)	-10%	\$ 23,339	\$ 21,539	
Total	\$ 13,736	\$ 12,491	\$ 13,797	\$ (1,246)	-9%	\$(1,307)	-10%	\$ 23,339	\$ 21,539	

FY TO DATE SCHEDULE / COST PERFORMANCE

The schedule and cost variances are within established thresholds.

SCHEDULE / COST PERFORMANCE (MONTHLY AND FYTD)

Fiscal Year to Date Performance Indices

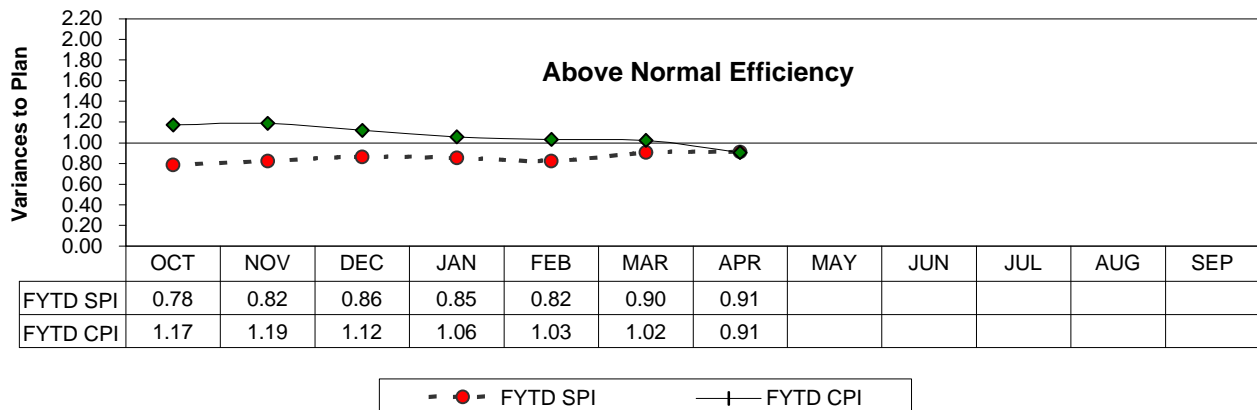

Monthly Performance Analysis

