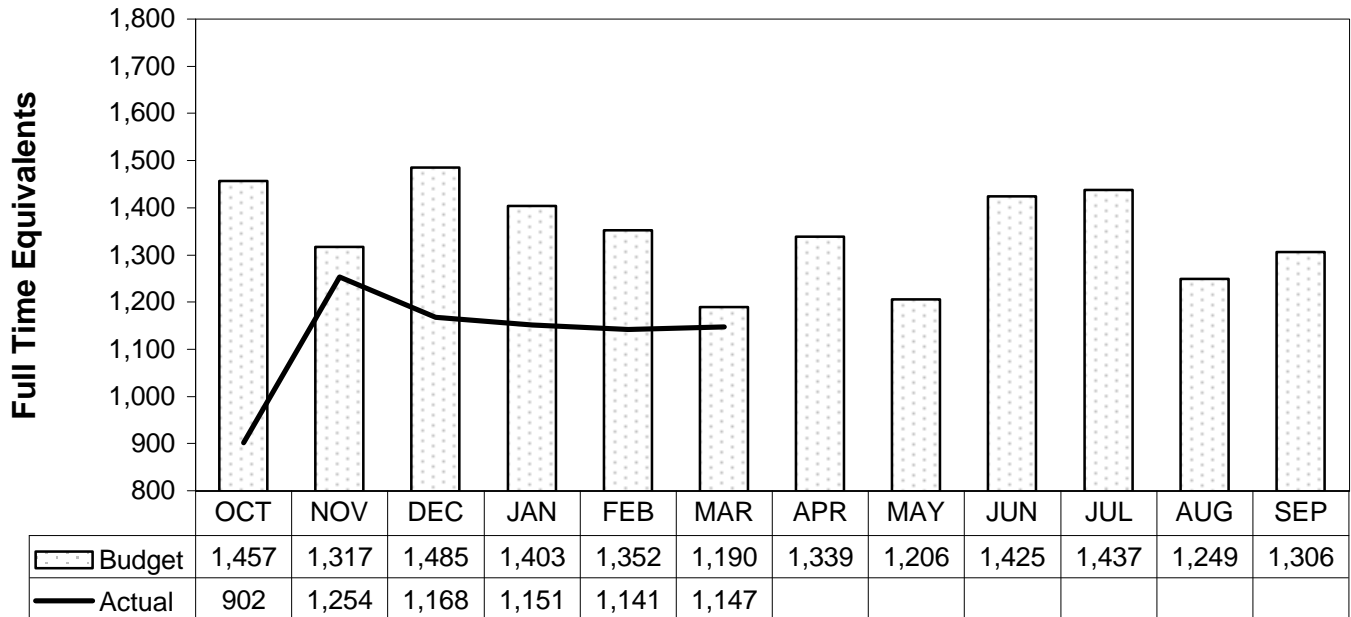


Hanford Site
Performance Report**HANFORD SITE STAFFING**
PHMC Tank Waste Remediation System**MARCH 1998**

The current month 43 FTE underrun was the net result of several factors. The two primary underruns were 1) Characterization Laboratory Analysis being planned as FTEs but costed as an assessment and 2) the utilization of contract personnel to supplement permanent staff. These underruns were offset by additional resources required to support Tank Farm Operations; additional Operating Engineers were hired to support this project, and the reduction in force at the Plutonium Finishing Plant resulted in additional operators being assigned to TWRS.
